



REQUEST FOR PROPOSALS

Integrated Project Delivery utilizing
Construction Manager/General Contracting
Services
State of Colorado
Colorado Mesa University

Notice Number: CMU 2868
Project Number: 8010-26-1
Project Title: Centennial Village South
Estimated Project Cost: \$33,607,452

Table of Contents

I. NOTICES.....	1
II. PROJECT OVERVIEW	2
Scope of Services	5
III. MINIMUM REQUIREMENTS	5
IV. NON MANDATORY PRE-SUBMISSION CONFERENCE AND SITE TOUR.....	6
V. SCHEDULE.....	6
VI. QUESTIONS, CLARIFICATIONS AND ADDENDA.....	7
VII. POINT OF CONTACT/CLARIFICATION	7
VIII. SUBMITTALS OF QUALIFICATIONS	7
IX. METHOD OF SELECTION AND AWARD	8
A. Short List	8
B. Oral Interview	8
X. EVALUATION OF QUALIFICATIONS	10
A. PREQUALIFICATION SUBMITTAL CRITERIA.....	10
1. QUALIFICATIONS OF THE FIRM(s)	10
2. QUALIFICATIONS OF THE MANAGEMENT TEAM MEMBERS.....	10
3. PROJECT MANAGEMENT APPROACH	10
4. PRIOR PROJECT EXPERIENCE/SUCCESS	11
5. EQUITY DIVERSITY AND INCLUSION.....	12
6. MISCELLANEOUS CONSIDERATIONS	12
XI. ORAL INTERVIEWS EVALUATION CRITERIA	13
1. QUALIFICATIONS OF THE FIRM.....	13

2. QUALIFICATIONS OF THE MANAGEMENT TEAM MEMBERS.....	13
3. PROJECT MANAGEMENT APPROACH.....	13
4. PRIOR PROJECT EXPERIENCE/SUCCESS	14
5. MISCELLANEOUS CONSIDERATIONS	14
XII. FEE PROPOSALS.....	14
XIII. ACKNOWLEDGEMENT AND ATTESTATION FORM	18
Appendix A: Evaluation Forms	23
Appendix B: Construction Manager/General Contractor (CM/GC) Agreement with General Conditions of the Construction Manager/General Contractor Agreement	24
Appendix C: Direct Labor Burden Calculation	25
Appendix D: Applicable Prevailing Wage Rates & Apprenticeship Contribution Rates	26
Appendix E: Apprenticeship Utilization Certifications	27
Appendix F: Program Plan, etc.	28

I. NOTICES

1. For all projects with a total dollar value above \$150,000 Notice of Final Settlement is required by C.R.S. §38-26-107(1). Final Settlement, if required, will be advertised in the same location as the original solicitation.
2. For State Public Works C.R.S. §8-17-101 - Colorado labor shall be employed to perform at least 80% of the work. Colorado labor means any person who is a resident of the state of Colorado at the time of the Public Works project.
3. All respondents accept the conditions of this RFP, including but not limited to, the following:
 - a. All submittals shall become the property of the State of Colorado and will not be returned.
 - b. Late submittals shall not be evaluated.
 - c. The State reserves the right to reject any or all proposals on the basis of being unresponsive to this RFP or for failure to disclose requested information.
 - d. The State shall not be liable for any costs incurred by respondents in the preparation of submittals and proposals nor in costs related to any element of the selection and contract negotiation process.
 - e. Any restriction as to the use of submitted materials must be clearly indicated as proprietary. The requested limitation or prohibition of use or release shall be identified in writing on a cover sheet. Blanket claims of proprietary submittals will not be honored. Fee proposals will be considered proprietary.
 - f. The respondent has reviewed Appendix B and by responding has agreed that the terms and conditions of the sample Construction Management/General Contracting Agreement are expressly workable without reservation.
4. The respondent has reviewed Appendix B and by responding has agreed that the terms and conditions of the sample Construction Manager/General Contractor (CM/GC) Agreement (SC-6.5) and General Conditions of the Construction Manager/General Contractor Agreement (SC- 6.51) are expressly workable without reservation. Any exceptions to the contract must be communicated formally in writing before the bid closes.
5. Per C.R.S. §24-92-115 unless prohibited by applicable federal law, contract for any public project in the amount of one million dollars or more, that does not receive federal money, in the amount of one million dollars or more shall require the general contractor to which the contract is awarded to submit, at the time the mechanical, electrical, or plumbing subcontractor is put under contract, documentation that identifies the contractors or subcontractors that

will be used for all mechanical, sheet metal, fire suppression, sprinkler fitting, electrical, and plumbing work required on the project and certifies that all firms identified participate in apprenticeship programs registered with the United States department of labor's employment and training administration or state apprenticeship councils recognized by the United States department of labor and have a proven record of graduating a minimum of 15% of its apprentices for at least three of the past five years.

6. Per C.R.S. §24-92-117, a public construction project in the amount of five hundred thousand dollars or more shall be subject to the Buy Clean Colorado (BCCO) Act program requirements. The BCCO Act requires the Office of the State Architect to establish a maximum acceptable global warming potential (GWP) limit for each category of eligible materials, which include asphalt and asphalt mixtures, cement and concrete mixtures, glass, post-tension steel, reinforcing steel, structural steel, and wood structural elements. For any solicitation for a contract for the design of an eligible project, a State Agency or institution shall require the designer who is awarded the contract to include in project specifications when final construction documents are released, a current Environmental Product Declaration (EPD) that meets the maximum acceptable GWP limits for each eligible material specified for the project. A contractor that is awarded a contract for an eligible project shall not install any eligible materials on the project until the contractor submits an EPD for each eligible material procured for the project.
7. Per C.R.S. §24-92-Part 2, a public construction project in the amount of five hundred thousand dollars or more shall be subject to the State prevailing wage rate, of the regular, holiday, and overtime wages paid and the general prevailing payments on behalf of employees to lawful welfare, pension, vacation, apprentice training, and educational funds in the State, for each employee needed to execute the contract. Payments to the funds must constitute an ordinary business expense deduction for federal income tax purposes by contractors and subcontractors. Contractors are required to pay their employees at weekly intervals and shall comply with the enforcement provisions of C.R.S. §24-92-209. Contractors awarded a project of this size will be required to utilize the LCPTracker cloud-based labor compliance and certified payroll application.
8. Preference shall be given to Colorado resident bidders and for Colorado labor, as provided by law.

II. PROJECT OVERVIEW

Introduction

CMU seeks to add additional capacity to its residential on-campus offerings and endeavors to have these additional beds delivered for the fall semester of 2027 to accommodate year over year student enrollment growth. CMU is considering two sites on campus for this development (see descriptions and graphics below). CMU must consider immediate repercussions of each site to determine what is in the best interest of the university to develop for this next phase of housing.

Enrollment growth for first-time, first-year students has shown steady increases over the past decade, in line with the 1% annual growth projection described in the 2023 update to CMU's Campus Master plan. However, growth for first-time, first-year students increased to 28% in fall 2024, up from 1,830 students in 2023 to 2,348 students in 2024. Said increase in enrollment has required construction of an additional 310 bed residence hall scheduled to be open for students in fall 2026. Bringing an additional 310 beds on-line which will fill the need for the influx of new students in 2026 and will allow CMU to terminate existing leases for off campus housing but doesn't provide a buffer for increased demand for student housing moving forward.

The Fixed Limit of Construction costs for this project has been set at \$26,847,927.

Design is projected to begin in May 2026, with the potential for an early release bid package to include site utilities and earthwork as early as September 7, 2026. Final project completion is anticipated prior to the start of the spring semester which begins the second week of January, 2028

Background

CMU is considering two locations for the next phase of student housing, Centennial Village South, located immediately west of the north wing of Lucero Hall, north of North Ave., west of Cannell Ave. right-of-way, and wrapping around a potential parking structure located in the center of campus at parking lot CP-9.

Considerations for the building design if the Centennial Village South Location is chosen should include:

- a. the context and materiality precedent of the new Centennial Village Apartments
- b. the nature of its proximity to a planned new major campus entrance, and thus be planned to showcase a welcoming presence for students and the public alike
- c. should consider a maximum five-story structure to match the elevation of Centennial Village to the north and to maximize the number of beds possible on this site.
- d. All commercial buildings on the property on North Avenue have been purchased by the University and are slated for demolition should this site be selected for the next phase of housing.
- e. Careful coordination for this site should be had with the University and current tenants in the commercial buildings on the site on North Avenue. Sensitivity to displacement of these tenants should be considered and coordinated with CMU to minimize hardship on North Avenue business tenants, particularly those who intend to occupy newly developed retail/commercial space in the new building.
- f. A retail/commercial component like the east-west wing of Lucero Hall is desired and should balance with the housing needs of the university. Coordination with the university balancing the two is encouraged.
- g. Consideration should be given to match floor levels and elevations of the new Centennial Village Apartments with one exception, that being the main floor to level 2 floor-to-floor height. Whereas that floor-to-floor height in Centennial

Village is 12'-0", a minimum of 14'-0" floor to floor height is desired for lower-level retail spaces. This precedent exists currently in the retail/commercial space in the east/west wing of Lucero Hall to the east.

- h. The schematic graphic below shows the building setback from North Avenue, however, if parking is offered close by the designer and planner should consider if the housing on this site should push the to the property line on North Avenue to maximize the number of beds that can be planned with development of Site 1.
- i. A 5-story facility should be planned. Consideration should be given for the construction type of the facility which will either be all Type 3B (All Wood Construction with Exterior Fire Walls), or Type 1A / Type 5A (Four Combustible Floors over a Main Floor Non-combustible Podium). Both Construction types require the building to be fire sprinklered.

Considerations for the building design if the CP-9 parking lot location is chosen Centennial Village South Location is chosen should include: a master-planned property divided into two phases of housing: a north-to-south wing in Phase 1, and an east-to-west wing in Phase 2 (refer to program plan in the appendix for more detailed analysis). Additional considerations for the building design should include:

- a. The building should be offset from the planned parking garage structure by a minimum of 30'. This will serve for both fire separation and a relief that is sufficient for the tenants whose view will be the parking structure. This separation distance will also provide enough separation for landscaping and pedestrian circulation paths.
- b. Because the master plan for this housing is an L-shape, consideration should be given to provide a pedestrian breezeway path through the corner of the building to the west with a connection to the **Formation Food Hall** immediately to the west.
- c. A 5-story facility should be planned. Consideration should be given for the construction type of the facility which will either be all Type 3B (All Wood Construction with Exterior Fire Walls), or Type 1A / Type 5B (Four Combustible Floors over a Main Floor Non-combustible Podium). Both Construction types require the building to be fire sprinklered.
- d. The building should be planned in coordination with the traffic circulation (ingress/egress) of vehicular traffic wrought by the planned parking structure. The graphic below anticipates a one-way ingress off of the Asteria Way/Bunting Ave roundabout on the southwest and a one-way exit east of the east-west wing which is the second phase of the L-shaped building.
- e. The new resident facilities should be a minimum of a 12' floor to floor height 1st to 2nd floor, then 10' floor to floor height thereafter.
- f. Consider the materials from the surrounding buildings, namely Dominguez Hall, The Art Building, Bunting Hall, Centennial Village Apartments, Asteria Theater, and the new Formation Food Hall.
- g. It is NOT anticipated that Site II will have a commercial/retail component as would Site I.

The State of Colorado, (CMU) is soliciting proposals from qualified CMGC contractors for the Student Parking Garage project.

CMU anticipates using a Construction Manager/General Contractor (CM/GC) approach to project delivery. A Guaranteed Maximum Price (GMP) and an updated project duration schedule will be established by the Architect/Engineer and the Construction Manager/General Contractor in conjunction with Colorado Mesa University. The CM/GC will evaluate, among other things, availability of materials and labor, project schedule, project costs as they relate to the established budget, constructability, and will work closely with the Architect/Engineer and CMU throughout the planning, design and construction phases of the project. Construction is estimated to commence June 1, 2026.

The process to be used in the selection of the CM/GC is comprised of two steps. STEP I is the Submittal of Prequalification as described in Section X. STEP II is the Oral Interview/Fee Proposal as described in detail in Section XI. A Jury Panel of individuals who will be involved in the project and/or understand the required services associated with Construction Management/General Contracting will evaluate responses to this RFP for both STEPS. Upon completion of the evaluation of the Submittals of Prequalification, a limited number of firms will be invited to the oral interviews. Sealed fee proposals will be required only from those firms who are interviewed and are to be submitted as indicated in this RFP. Both qualifications and cost will be considered in the final ranking of firms with qualifications given 70% of the value of the weighted criteria and fees for the Fee Proposal given 30%.

Selection and award of this project will be based on a combination of qualifications and costs that represent the best overall value to the State.

Scope of Services

The scope of services assistance to the State during the process of assessment, design, construction, and warranty period. Specific tasks to be performed by the Construction Manager/General Contractor (CM/GC) include those generally performed by the CM/GC construction community where the Construction Manager is also the Contractor. A sample copy of the State's CM/GC contract is contained within the RFP. A Guaranteed Maximum Price (GMP) will be required at the completion of Design Development phase.

Per C.R.S. §38-26-106, if a contract amounts to \$150,000 or more, the awarded contractor shall provide payment and performance bonds not less than 50% of the value of the contract. The costs associated with this bond are to be included in the contractor's proposal.

III. MINIMUM REQUIREMENTS

Notice is hereby given to all interested parties that all firms will be required to meet all minimum requirements to be considered for this project. Interested parties should be prepared to show evidence of the following to be considered as qualified, as a minimum:

1. Not previously terminated by the State for non-performance on a State Buildings contract or procurement.

2. The contractor must have been in the same business under the same name for the last two (2) years.
3. Demonstrated specific contracting experience in projects of similar scope and complexity for at least two (2) projects each in excess of \$24,000,000 (hard costs), utilizing the expertise present in their Colorado Office; and
4. Demonstrated bonding capability up to \$24,000,000 for an individual project coincidentally with current and anticipated workloads; provide letter from surety that affirms this capacity.
5. Respondents must acknowledge all issued addenda in their submittal and proposal.
6. For a respondent to be considered responsive to this RFP, the submittal must be posted on Bidnet/Rocky Mountain E-Purchasing System (RMEPS) website, <https://www.rockymountainbidsystem.com>.

Firms meeting the minimum requirements may obtain additional proposal documents on the website accompanying this advertisement.

All forms related to this RFP will be posted on Bidnet/Rocky Mountain E-Purchasing System (RMEPS).

Questions and requests for clarification regarding this project shall be submitted only via Bidnet/Rocky Mountain E-Purchasing System (RMEPS) before the deadline listed in the above Schedule.

Communication regarding the project during the procurement, outside of this submission process or scheduled procurement milestones is not permitted.

IV. NON MANDATORY PRE-SUBMISSION CONFERENCE AND SITE TOUR

To ensure sufficient information is available to firms preparing submittals, a non-mandatory pre-submittal conference has been scheduled. The intent of this conference is to tour the site and to have CMU staff available to discuss the project. Firms preparing submittals are encouraged to attend and sign-in.

A non-mandatory Pre-Submission Meeting will be held at:

Building Address:	<u>University Center (1455 N. 12th Street, 81501)</u>
Room:	<u>University Center, room 221</u>
Date/Time	<u>March 24, 2:00pm MDT</u>

V. SCHEDULE

The following is a tentative schedule of events for the Proposal Submittal process and an outline of the schedule for the balance of the project. All dates are subject to change and changes in the schedule will be issued via addendum.

Request for Proposal Issued	<u>March 13, 2026</u>
Pre-Submittal Conference and Tour	<u>March 24, 2026 at 2pm</u>
Request for Clarifications Due	<u>March 26, 2026</u>
Final Addendum Issued (anticipated)	<u>March 27, 2026</u>
Submittals Due (Prequalification: Step I)	<u>April 2, 2026 at 2pm</u>

Interview Short List Announced	<u>April 3, 2026</u>
Sealed Proposal Due	<u>April 17, 2026</u>
Oral Interviews	<u>April 17, 2026</u>
Selection Announced	<u>April 20, 2026</u>
Negotiation of Contract	<u>April 24, 2026</u>
Anticipated Design Start	<u>April 29, 2026</u>
Anticipated CM/GC Start	<u>May 1, 2026</u>
Anticipated Construction Start/Finish	<u>Sept. 7, 26/Nov. 30, 27 (450 days)</u>

The above schedule is tentative. Responding firms shall be notified of revisions in a timely manner by postings on the Rocky Mountain E-Purchasing System (RMEPS) website, <https://www.rockymountainbidsystem.com>. Respondents may elect to verify times and dates by email, but no earlier than 36 hours before the scheduled date and time.

VI. QUESTIONS, CLARIFICATIONS AND ADDENDA

Owner initiated changes to this RFQ will be issued under numerically sequenced addenda on Bidnet/Rocky Mountain E-Purchasing System (RMEPS), <https://www.rockymountainbidsystem.com>.

Questions and requests for clarification regarding this project shall be submitted before the deadline listed in the above schedule on Bidnet/Rocky Mountain E-Purchasing System (RMEPS), <https://www.rockymountainbidsystem.com>..

Communication regarding the project during the procurement, outside of this submission process or scheduled procurement milestones is not permitted.

VII. POINT OF CONTACT/CLARIFICATION

Name:	<u>Breanne Meier, Director of Campus Procurement</u>
Agency:	<u>Colorado Mesa University</u>
Email Address:	<u>bmeier@coloradomesa.edu</u>
Phone:	<u>970-248-1417</u>

VIII. SUBMITTALS OF QUALIFICATIONS

1. This RFP document, it's appendices, and any written addenda issued prior to the closing of the solicitation, and written clarifications shall serve as the only basis for the proposal.
2. All submittals must comply with the following items, a through h. The State retains the right to waive any minor irregularity, or requirement should it be judged to be in the best interest of the State.
 - a. Qualifications shall be formatted and tabbed in the exact form and numeric sequence of the Evaluation Form (1 through 6) in Appendix A. A two-sided single-page cover letter addressed to the (Breanne Meier, Director of Campus Procurement outlining the firm(s) qualifications is required at the front of the submittal.

- b. Not counting the cover letter and required Acknowledgement and Attestation form, the entire submittal is to be no more than 30 doubled sided 8 ½' x 11" sized pages in portrait format, at least 12 font. No physical submittals.
- c. Qualifications shall be evaluated in accordance with criteria as indicated in PREQUALIFICATION SUBMITTAL CRITERIA and ranked on the corresponding Evaluation Form in Appendix A.
- d. Response to all items shall be complete.
- e. All references shall be current and relevant.
- f. Complete and execute the appropriate Acknowledgment and Attestation Form as provided in Section VI and submit at the back of the Prequalification Submittal.
- g. An electronic copy of the qualification package, submitted via Bidnet/Rocky Mountain E-Purchasing System (RMEPS), <https://www.rockymountainbidsystem.com> is due April 2, 2026 and shall be received no later than 2:00 PM (MDT).
- h. Late submittals or any other submittals not posted to Bidnet/Rocky Mountain E-Purchasing System will be rejected without consideration. The State of Colorado assumes no responsibility for costs related to the preparation of submittals.

IX. METHOD OF SELECTION AND AWARD

A. Short List

- 1. From the submittals received, a short list of qualified respondents shall be identified using the scoring indicated on the enclosed Evaluation Form, Appendix A.
- 2. Firms failing to meet the minimum required qualifications will not receive further consideration.

B. Oral Interview

- 1. Mandatory oral interviews shall be conducted for the short-listed firm(s) only. Interview times and location will be arranged by the Colorado Mesa University and all short-listed firms will be notified in advance. At the option of the State, a visit to the short-listed firm(s) managing home office and/or representative field office may be required.

C. Fee Proposals

- 1. Only those firms shortlisted for interview are required to submit their sealed proposals. (Only one copy is required on the scheduled submission date.) Fee Proposals will remain sealed until after the qualitative scoring and will then be opened. The Fee Proposal will then be considered (equivalent to 30 percent of the weighted

criteria) in conjunction with the qualitative score from the response and interview (equivalent to 70 percent of the weighted criteria).

2. Fee Proposals shall be submitted on the form provided in Section XII, without modification. A Fee Proposal shall be accompanied with sufficient detail to clearly identify the fee for service and include a detailed schedule of estimated (not-to-exceed) reimbursable and non-reimbursable costs. The percentage of the cost of work is not acceptable value. The Fee Proposal should be prepared independently in accordance with the following:
 - a. Fees are outlined in Exhibit A of the Sample Agreement attached to this solicitation as Appendix B.
 - b. Any specific services requested in the RFP and its appendices that are not included should be clearly identified. Exclusion of any required service may result in the proposal being found non-responsive.
 - c. Provide a CM/GC staff schedule with staff by name, position and man-hours (assume 8-hour days) per month estimated on the project.
 - d. Provide a detailed estimate of reimbursable costs including breakdown of direct salaries and payroll fringes (DPE) for on-site CM/GC personnel associated with the services. Not-to-exceed reimbursable expenses shall be provided at direct cost.
 - e. Provide a detailed estimate of non-reimbursable expenses (included in fee).
 - f. The State reserves the right to reject any Fee Proposal not prepared in the above manner. Proposals that exceed the available funds may be rejected outright but the State reserves the right to negotiate a reasonable fee for service within the available funds. The CM/GC contract will be a bonded lump sum contract including not-to-exceed reimbursables with a Guaranteed Maximum Price to encompass all construction work; some not-to-exceed allowances may be included as directed by the State.
3. This Fee Proposal is a binding offer to perform the services associated with the Scope of Services described in this RFP and the Designated Services and Method of Payment Matrix in Appendix B. The State reserves the right to negotiate a cost adjustment based on scope clarification after selection and prior to contract execution.

D. Method of Selection and Award

1. The Jury Panel shall complete a combined evaluation of qualifications and fee in accordance with the criteria as indicated in Section X, EVALUATION OF QUALIFICATIONS and Section XI ORAL INTERVIEWS EVALUATION CRITERIA. Numerical ranking and selection of the most qualified firm (including fee) will then occur on the corresponding evaluation forms in Appendix A.
 2. The final fee amount and scope of services may be negotiated at the State's discretion. The award and contract will be contingent on the availability of key proposed Project Management Team staff.
- E. After selection and award all proposals, qualifications and ranking documents will be made available to the public on the agency or institutions solicitation platform.

X. EVALUATION OF QUALIFICATIONS

A. PREQUALIFICATION SUBMITTAL CRITERIA

1. QUALIFICATIONS OF THE FIRM(s)

- Provide a description of the composition and management structure of your firm. Identify the firm's roles and responsibilities and relevant experience with projects of similar scope and complexity and similar fast track project delivery methods. Describe how the firm's experience will relate to the success of this project.
- Provide a description and separate graphic organizational chart complete with working titles identifying the lines of authority, responsibility and coordination.
- Provide a detailed description of the process of how your firm selects qualified sub-contractors and manages them effectively on complex multi-phased projects. How does your organization attempt to utilize disadvantaged and small businesses
- Provide a detailed description of how your firm will maximize the Colorado construction workforce on this project.
- Provide your firm's safety record over the last ten years and describe your firm's efforts to retain and support employees.

2. QUALIFICATIONS OF THE MANAGEMENT TEAM MEMBERS

- Describe the qualifications and relevant experience of the superintendent including demonstrated experience working on projects of similar scope and complexity and time commitment for this project.
- Describe the qualifications and relevant experience of other key in-house staff and time commitments for this project.
- Identify all current office locations of the assigned staff and any other resident expertise intended to be provided under this RFP.

3. PROJECT MANAGEMENT APPROACH

- Provide a strategic project approach summary: Include discussion of your firm's approach in providing successful Construction Management/General Contracting services based on prior experience in

cost, schedule and quality effectiveness. Include specific examples (1-2-page excerpts) of actual products (estimates, progress reports, schedules, constructability reviews, value engineering studies, forms, general conditions budgets, organizational structures, etc.).

- Providing a description of construction work Project Management Team has capability to competitively bid and self-perform, including qualifications to do such. It is the perception of Colorado Mesa University subcontracting CM/GC construction work is in the State's best interest in terms of price competition. CMU may, at its discretion, limit the types and amount of work Project Management Team bids and self-perform.

4. PRIOR PROJECT EXPERIENCE/SUCCESS

a. Select your three (3) most relevant projects and provide, at a minimum, the following:

- The project/contract name
- Description of services provided
- Overall construction cost of project, as applicable, including initial contract value and change orders including reasons for change orders
- Organizational structure of service delivery under the contract (include the owner's organization as it interfaced with the respondent's contract)
- Key assigned in-house staff (name and title)
- Subcontracts (service) used in the performance of the contract
- Schedule history
- Reference(s) for Owner and Architect as described in Section VIII, SUBMITTALS OF QUALIFICATIONS
- Continuing services, if any

b. Timeliness

In general, Construction Management/General Contracting work is seen as successful if it is on time, on budget, and of high quality of workmanship. Timeliness is generally based on completion by the originally scheduled date and is indicated by a Certificate of Occupancy. Please demonstrate for each of the above projects how timely delivery occurred.

c. Budget Considerations

Similar to timeliness, being on budget historically means the work was completed within the originally identified available budget. Demonstrate for the above projects examples of how you accomplished the following cost control services. For the purposes of this RFP, the State is interested not only in being within budget but also in the respondents' ability to address these issues:

- Conceptual estimating
- Value analysis

- Alternate solutions
- Scope reduction that maintains project function
- Cost/benefit analysis

Demonstrate for the above projects examples of how you accomplished the above cost control services.

d. Quality

Construction quality has the obvious traditional connotations (workmanlike, in compliance with the specifications, normal standard of care, etc.). Demonstrate for the above project examples how a high quality of workmanship was achieved.

e. Services Disruption

Demonstrate how your services on the above project examples dealt with issues of disruption at existing facilities, etc. if applicable.

f. Project Acceptability

Please discuss how your Construction Management/General Contracting services helped achieve owner satisfaction regarding project quality and acceptability with your project examples.

g. Compliance

Provide information on how compliance with industry standards of care, building codes, etc. was achieved.

5. EQUITY DIVERSITY AND INCLUSION

- Describe how your team is incentivized to hire and promote diverse individuals
- Describe how your team attempts to contract with Service-Disabled Veteran Owned Small Businesses or historically disadvantaged businesses

6. MISCELLANEOUS CONSIDERATIONS

a. Claims/Litigation History of Firm

Provide information on any past, current or anticipated claims (i.e., knowledge of pending claims) on respondent contracts; explain the litigation, the issue, and its outcome or anticipated outcome.

b. Apprenticeship Training Program (Optional for Step I)

Where an Apprentice Training Program certified by the Office of Apprenticeship located in the Employment and Training Administration in the United States Department of Labor exists in the State, or a comparable program for the training of apprentices is available in the State:

1. Each submitter shall demonstrate access to the certified program or a comparable alternative (Note that it is the responsibility of the submitter to demonstrate the comparability of a non-certified program) and,
 - c. Each submitter's subcontractor at any tier with a contract value of two hundred fifty thousand dollars or more shall demonstrate access to the certified program or a comparable alternative.
 - d. Apprenticeship Training Program (Optional for Step I)
 - e. Other

This category is included in other items provided by the submitter. Inclusions may include standard firm promotional literature, testimonials, awards, corporate memberships in professional organizations or sponsorships, additional project/contract histories, etc., intended to demonstrate why your firm is uniquely qualified for this project.

XI. ORAL INTERVIEWS EVALUATION CRITERIA

(Note that the primary focus of the Oral Interview evaluation in addition to the Fee Proposal will be the proposed project management team members' capabilities).

1. QUALIFICATIONS OF THE FIRM

- Explain the composition and structure of your project management team and how the firm will support their efforts in the field throughout this project.
- Are the lines of authority, responsibility and coordination clearly identified?

2. QUALIFICATIONS OF THE MANAGEMENT TEAM MEMBERS

- Explain the prior experience with projects of similar scope and complexity and similar fast track project delivery methods of the superintendent and all other project management team members. Explain their roles and responsibilities and authority and why they are the right team members for this project.
- Explain anticipated project management team staff current and projected workload.
- Identify all current office locations and the resident expertise intended to be provided under this RFP. Identify the location of the staff for the performance of this contract, their expertise, and generic equipment that will be located in Colorado and act in support of the anticipated contract.

3. PROJECT MANAGEMENT APPROACH

- Explain the strategic project approach for this project in summary: Include discussion of your team's approach in providing successful CM/GC services based on the needs of this specific project utilizing the

team's prior past experience including cost, schedule, and quality control.

- Explain the construction work, the project management team has the capability to competitively bid and self-perform including qualifications to do such work.
- Provide a detailed description of how your project management team will select qualified sub-contractors and manage them effectively on this project.

4. PRIOR PROJECT EXPERIENCE/SUCCESS

- Explain the most relevant projects the superintendent and the team members have completed together and/or separately and what their role was. Colorado Mesa University at its discretion contact references and/or conduct independent performance analysis on projects on which the team member has worked).
- Provide descriptions of other related experiences of superintendent and other project management team members.

5. MISCELLANEOUS CONSIDERATIONS

- Craft Labor Capabilities: Describe the availability of resources that will be utilized to successfully complete the project.
- Apprenticeship Training Program (Mandatory for Step II): Describe access to federal or state-approved apprenticeship programs, as available.
- Other: This category is included for other items provided by the presenter. Inclusions may include testimonials, awards, corporate memberships in professional organizations or sponsorships, additional project/contract histories, etc., intended to demonstrate why this management team is uniquely qualified for this project.

XII. FEE PROPOSALS

1. Only those teams short listed for interview are required to submit their sealed proposals. Shortlisted teams will receive correspondence noting their scheduled time for their interview as well as where to send their Fee Proposal. Fee Proposals are due on the scheduled submission date prior to the start of oral interviews. Only one sealed copy is required. Fee Proposals will remain sealed until after the qualitative scoring and will then be opened. The fee amount will then be considered (30 percent) in conjunction with the qualitative score from the response and interview (70 percent).
2. Carefully review the CM/GC Contract sample (Appendix B) before initiating your response submittal. Any exceptions to the contract must be communicated formally in accordance with Section VI. QUESTION, CLARIFICATIONS AND ADDENDA.
3. Appendix D and E of this RFP includes mandatory State apprenticeship and prevailing wage requirements based on the construction value of the project.

4. The State reserves the right to make non-material changes to the appended model agreement, including additions and /or modifications that may be necessary to more completely describe the services defined or implied herein.
5. Any approved reimbursable expenses made under the terms of the final agreement shall be a direct pass-on cost with no adjustment to the fee described therein.
6. Any and all products, systems, methods, and procedures developed, as a result of this agreement shall remain the exclusive property of the State.
7. Immediately following the Acknowledgement and Attestation Form is a Fee Proposal Form to be utilized to summarize the fee proposal for the services. Only those firms short-listed will be required to submit fee proposals as directed by CMU.
8. This RFP document, it's appendices, and any written addenda issued prior to the submitting proposals, and written clarifications prior to the interview shall serve as the only basis for proposals.
9. The respondent, by submitting this proposal, does hereby accept that minor changes by the State to the exhibited contract and its exhibits, which do not adversely affect the respondent, shall not be cause for withdrawal or modification of the amounts submitted herein. Exceptions to the RFP documents and/or modification of the proposal may render the proposal non-responsive.
10. Upon due consideration and review of this document along with its appendices, written addenda, and written clarifications prior to the interview, the respondent does hereby submit the following proposal for Construction Management/General Contracting fees, consistent with the schedules provided in the Scope of Services. Respondents are hereby advised that it is the State's desire to accelerate design and construction schedules where reasonably possible, without adverse cost impact.
11. Respondent should complete the Fee Proposal Form by filling in all blanks on the form that follows.
12. Respondents should include a separate detailed not-to-exceed reimbursable estimate.

XII. FEE PROPOSAL FORM
CONSTRUCTION MANAGER/GENERAL CONTRACTING (CM/GC) SERVICES

Project Number: CMU2868

Project Title: Centennial Village South

Date: _____

- | | | |
|-----------------|---|----------|
| 1. | CM/GC Preconstruction Fee | \$ _____ |
| 2. | CM/GC Construction Fee | \$ _____ |
| 3. | General Conditions On-Site CM/GC Staff | \$ _____ |
| 4. | Other Reimbursable General Conditions (NTE) | \$ _____ |
| Total CM/GC Fee | | \$ _____ |

Fees are to be calculated per Exhibit A (SC-6.5), CM/GC Designated Services and Method of Payment.

Please provide a detailed breakdown to adequately describe the CM/GC staff provided, term of their services, and associated anticipated reimbursable costs so as to demonstrate as complete an understanding as possible of the services provided.

Reimbursable general condition expenses are generally confined to the on-site CM/GC construction phase staff reimbursed at direct personnel expense, plus those on-site materials, equipment and facilities to support the work of the CM/GC staff and construction subcontractors.

Acknowledge receipt of Addendum Nos. _____

Anticipates Services outside the United States or Colorado^{1*} ☐ Yes ☐ No

If the respondent anticipates services under the contract or any subcontracts will be performed outside the United States or Colorado, the respondent shall provide in a written statement which must include, but need not be limited to the type of services that will be performed at a location outside the United States or Colorado and the reason why it is necessary or advantageous to go outside the United States or Colorado to perform such services. (Does not apply to any project that receives federal moneys)

Will comply with 80% Colorado Labor ☐ Yes ☐ No

For State Public Works Project per C.R.S 8-17-10, Colorado labor shall be employed to perform at least 80% of the work. "Colorado Labor" means any person who is a resident of the state of Colorado at the time of the Public Works project. Respondents indicating that their proposal will not comply with the 80% Colorado Labor requirement are required to submit written justification along with the proposal submission. A governmental body that

¹ Does not apply to projects for Institutions of Higher Education that have opted out of the State Procurement Code.

allows a waiver shall post notice and justification for the waiver on its web site. (Does not apply to any project that receives federal moneys)

Design/Build entity is a Service-Disabled Veteran Owned Small Business²* ☐ Yes ☐ No

A Service-Disabled Veteran Owned Small Business (SDVOSB) per C.R.S. 24-103-905, means a business that is incorporated or organized in Colorado or maintains a place of business or has an office in Colorado and is officially registered and verified by the Center for Veteran Enterprise within the U.S. Department of Veteran Affairs. Attach proof of certification along with the proposal submission.

Applicant or Corporate Officer Signature

Title

² Does not apply to projects for Institutions of Higher Education that have opted out of the State Procurement Code.

XIII. ACKNOWLEDGEMENT AND ATTESTATION FORM

1. Several versions of the Acknowledgment and Attestation Form follow this section. Proper completion of the appropriate form is a mandatory requirement for a respondent to be considered responsive to this RFP Prequalification Submittal.
2. Qualifications made by a respondent in executing this form may render a submittal non-responsive as determined by the State.

**XIII. ACKNOWLEDGEMENT AND ATTESTATION FORM
(Partnership Format)**

Date: _____

Page 1 of 1

By responding to this RFP, the respondent(s) certify that he/she has reviewed the Construction Management/General Contracting sample contract, and its exhibits contained herein, and is familiar with their terms and conditions and finds them expressly workable without change or modification.

We certify and declare that the foregoing is true and correct.

Subscribed on _____ at _____
Date City

_____, State of _____
County State

1) _____
Partner Signature³

Typed Name: _____

2) _____
Partner Signature

Typed Name: _____

Notary: _____ Date _____

Commission Expires: _____

Offeror Acknowledges Receipt of Addendum No. _____, _____, _____, _____ (Addenda MUST be acknowledged)

³ Add additional signatures if there are more than two partners.

XIII. ACKNOWLEDGEMENT AND ATTESTATION FORM (Joint Venture Format)

Date: _____

Page 1 of 1

By responding to this RFP, the respondent(s) certify that he/she has reviewed the Construction Manager/General Contractor sample contract, and its exhibits contained herein, and is familiar with their terms and conditions and finds them expressly workable without change or modification.

We certify and declare that the foregoing is true and correct.

Subscribed on _____ at _____,
Date City
_____, State of _____.
County State

1) _____
Venture Partner

_____ Binding Signature _____ Date

_____ Type of Business

Typed Name: _____
Title: _____

Witness

Date

Typed Name: _____

2) _____
Venture Partner

_____ Binding Signature _____ Date

Type of Business

Typed Name: _____
Title: _____

Witness _____ Date _____

Typed Name: _____

Offeror Acknowledges Receipt of Addendum No. _____, _____, _____, _____ (Addenda MUST be acknowledged)

Note:

1. Add additional venture partners as necessary.
2. Witnesses of venture partners shall be corporate secretary for corporations, partners for partnerships, and notaries for sole proprietorships.
3. Attach venture agreement
4. Type of business shall identify the venture partner as a corporation, venture, partnership, sole proprietorship, or other legal entity.

XIII. ACKNOWLEDGEMENT AND ATTESTATION FORM (Corporate Format)

Date: _____

Page 1 of 1

By responding to this RFP, the respondent(s) certify that he/she has reviewed the Construction Management/General Contracting sample contract, and its exhibits contained herein, and is familiar with their terms and conditions and finds them expressly workable without change or modification.

We certify and declare that the foregoing is true and correct.

Subscribed on _____ at _____,
Date City

_____, State of _____
County _____ State _____

Corporate Officer Signature

Date _____

Secretary _____

Date _____

Note: Use full corporate name and attach corporate seal here.

Offeror Acknowledges Receipt of Addendum No. _____, _____, _____, _____ (Addenda MUST be acknowledged)

(SEAL)

XIII. ACKNOWLEDGEMENT AND ATTESTATION FORM (Sole Proprietorship Format)

Date: _____

Page 1 of 1

By responding to this RFP, the respondent(s) certify that he/she has reviewed the Construction Management/General Contracting sample contract, and its exhibits contained herein, and is familiar with their terms and conditions and finds them expressly workable without change or modification.

We certify and declare that the foregoing is true and correct.

Subscribed on _____ at _____,
Date City

_____, State of _____.

County _____ State _____

Respondent _____ Date _____

Typed Name: _____

Notary: _____ Date _____

Commission Expires: _____

Offeror Acknowledges Receipt of Addendum No. _____, _____, _____, _____ (Addenda MUST be acknowledged)

Appendix A: Evaluation Forms

Appendix A1: Prequalification Submittal/Evaluation Form

Appendix A2: Oral Interview /Evaluation Form

Appendix A3: Submittal and Interview Ranking Matrix

**Appendix B: Construction Manager/General Contractor (CM/GC) Agreement with
General Conditions of the Construction Manager/General Contractor Agreement
(Forms SC- 6.5 and SC-6.51) (Sample)**

Appendix C: Direct Labor Burden Calculation

(SBP-6.18)

Appendix D: Applicable Prevailing Wage Rates & Apprenticeship Contribution Rates

Appendix E: Apprenticeship Utilization Certifications

(SBP-6.17)

Appendix F: Program Plan, etc.

(Optional)



APPENDIX A: EVALUATION OF QUALIFICATIONS FORM: INTEGRATED PROJECT DELIVERY

Name of Firm: _____
Name of Project: CMU 2868 Centennial Village South CMGC
Evaluator No: _____
Date: _____

RFP REFERENCE MINIMUM REQUIREMENTS Y ____ N ____
ACKNOWLEDGEMENT AND ATTESTATION INCLUDED: Y ____ N ____

If the minimum requirements have not been met, specify the reason(s):

INSTRUCTIONS:

- Weights are to be assigned prior to evaluation and are to be consistent on all evaluation forms.
- Use only whole numbers.
- Rating: 0 = not provided, 1 = Unacceptable, 2 = Poor, 3 = Fair, 4 = Good, 5 = Excellent
- Total score includes the sum total of all criteria.
- A passing score (as a percentage of the total points available) is to be established by the state prior to evaluation.

1. <u>QUALIFICATIONS OF THE FIRM(S)</u>		Weight	X	Rating	=	Score
☐ Overall qualifications		5	x		=	
☐ Organizational structure/lines of authority		5	X		=	
☐ Subcontractor selection and management		5	X			
☐ Colorado workforce		5	X			
☐ Safety/employee support		5	X			
2. <u>QUALIFICATIONS OF MANAGEMENT TEAM MEMBERS</u>		Weight	X	Rating	=	Score
☐ Qualifications and relevant experience of superintendent		10	X		=	
☐ Qualifications and relevant experience of in-house staff		8	X			
☐ Location/Access		7				
3. <u>PROJECT MANAGEMENT APPROACH</u>		Weight	X	Rating	=	Score
☐ Approach to successful CM/GC Services		6	X		=	
Cost Effectiveness		7	X			
Schedule effectiveness						

Quality effectiveness	<u>6</u>	X	<u> </u>	<u> </u>
□ Competitively Bid/Self Performed Work	<u>6</u>		<u> </u>	<u> </u>
4. <u>PRIOR PROJECT EXPERIENCE/SUCCESS</u>	Weight	X	Rating	= Score
□ Project #1	<u>5</u>	X	<u> </u>	= <u> </u>
Timeliness				
Disruption				
Budget Considerations				
Quality				
Acceptability/Punchlist				
Compliance				
□ Project #2	<u>5</u>	X	<u> </u>	= <u> </u>
Timeliness				
Disruption				
Budget Considerations				
Quality				
Acceptability/Punchlist				
Compliance				
□ Project #3	<u>5</u>	X	<u> </u>	= <u> </u>
Timeliness				
Disruption				
Budget Considerations				
Quality				
Acceptability/Punchlist				
Compliance				
5. <u>EQUITY, DIVERSITY AND INCLUSION</u>	Weight	X	Rating	= Score
□ Hiring and Promotion Practices	<u>3</u>	X	<u> </u>	= <u> </u>
□ Subcontracting Practices	<u>2</u>	X	<u> </u>	= <u> </u>
6. <u>MISCELLANEOUS</u>	Weight	X	Rating	= Score
□ Claims/litigation history	<u>2</u>	X	<u> </u>	= <u> </u>
□ Apprenticeship Training Program	<u>2</u>	X	<u> </u>	= <u> </u>
□ Other	<u>1</u>	X	<u> </u>	= <u> </u>

Total Score:



APPENDIX A1: EVALUATION OF QUALIFICATIONS FORM: INTEGRATED PROJECT DELIVERY

Name of Firm: _____
Name of Project: CMU 2868 Centennial Village South CMGC
Evaluator No: _____
Date: _____

INSTRUCTIONS:

1. Weights are to be assigned prior to evaluation and are to be consistent on all evaluation forms.
2. Use only whole numbers.
3. Rating: 0 = not provided, 1 = Unacceptable, 2 = Poor, 3 = Fair, 4 = Good, 5 = Excellent
4. Total score includes the sum total of all criteria.
5. A passing score (as a percentage of the total points available) is to be established by the state prior to evaluation.

1. <u>QUALIFICATIONS OF THE FIRM(S)</u>	Weight	Rating	Score
	<u>25</u>	x _____	= _____
2. <u>QUALIFICATIONS OF MANAGEMENT TEAM MEMBERS</u>	<u>25</u>	X _____	= _____
3. <u>PROJECT MANAGEMENT APPROACH</u>	<u>25</u>	X _____	= _____
4. <u>PRIOR PROJECT EXPERIENCE/SUCCESS</u>	<u>15</u>	X _____	= _____
5. <u>MISCELLANEOUS CONSIDERATIONS</u>	<u>10</u>	X _____	= _____

Total Score: _____



APPENDIX A2: QUALIFICATIONS AND PROPOSAL RANKING MATRIX: INTEGRATED PROJECT DELIVERY

INSTRUCTIONS/EXAMPLE:

1. QUALIFICATIONS Example uses the 60% / Fee 40% split. [Optional is to use a \(30% / Fee 70% split\)](#)
2. Insert total score from each evaluator's SUBMITTAL review.
3. Add all evaluators' total scores and divide by the number of evaluators to determine the average score for each firm's qualifications.
4. The maximum score for qualifications on the evaluation form is equivalent to 40 points and is equivalent to the maximum points available for qualifications. Therefore, each firm's score is determined as a percentage of the maximum points available. To score each average qualification score, use the example formula.
5. Assume the highest score is 600.

SCORING OF QUALIFICATIONS

$$\text{FIRM B: } \frac{600}{600} \times 40 \text{ points} = 40 \text{ points}$$

$$\text{FIRM C: } \frac{500}{600} \times 40 \text{ points} = 33.33 \text{ points}$$

$$\text{FIRM A: } \frac{400}{600} \times 40 \text{ points} = 26.66 \text{ points}$$

6. Determine score for each firm's sealed proposal with the lowest fee being equivalent to a maximum score of 60 points. To score each proposal, use the example formula.
7. Assume the lowest Proposal was \$100,000.

SCORING OF PROPOSALS

$$\text{FIRM A: } \frac{\$100,000}{\$100,000} \times 60 \text{ points} = 60 \text{ points}$$

$$\text{FIRM B: } \frac{\$100,000}{\$125,000} \times 60 \text{ points} = 48 \text{ points}$$

$$\text{FIRM C: } \frac{\$100,000}{\$150,000} \times 60 \text{ points} = 39.99 \text{ points}$$

8. Add the average qualification score to the Proposal score to determine cumulative qualifications and fee score.
9. Numerically rank all firms with the highest scoring firm being the most qualified and advantageous to the state.

***CMU has chosen to use 70 (quals) / 30(fee) optional split**

FIRM	QUALIFICATIONS						AVE. QUALS	QUALS SCORE	PROPOSAL SCORE	QUALS & PROPOSAL SCORE	R A N K
	EVAL #1	EVAL #2	EVAL #3	EVAL #4	EVAL #5	EVAL #6					

STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM

CONSTRUCTION MANAGER / GENERAL CONTRACTOR (CM/GC) AGREEMENT

(STATE FORM SC-6.5)

State Agency

Colorado Mesa University

Department I.D.

Insert Department identification

Contract I.D. Number

Insert CMS number or other contract number

Project Number

8010-26-1

Project Name

CMU 2868 Centennial Village South

Contractor Name

Insert Contractor's full Legal Name including "Inc.", "LLC" etc.

Principal Representatives

For the State:

Name

Department Name

Address Line 1

Address Line 2

City, State ZIP

Email

For Contractor:

Name

Company Name

Address Line 1

Address Line 2

City, State ZIP

Email

ATTACHMENT 1: The General Conditions of the Contractor's Design/Bid/Build (D/B/B) Agreement (SC-6.23)

**STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM**

**CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT
(STATE FORM SC-6.5)**

TABLE OF CONTENTS Page
Table of Contents for the entire Agreement is located in THE GENERAL CONDITIONS OF THE
CONSTRUCTION MANAGER.GENERAL CONTRACTOR (CMGC) AGREEMENT (SC-6.51)

SIGNATURE PAGE	Error! Bookmark not defined.
RECITALS:	2
1 ARTICLE 1 PERFORMANCE OF THE WORK.....	3
1.1 THE WORK	3
1.2 CONTRACT DOCUMENTS.....	5
2 ARTICLE 2 EXHIBITS TO THE AGREEMENT	5
2.1 EXHIBITS	5
3 ARTICLE 3 CONSTRUCTION MANAGER’S SERVICES.....	6
3.1 AVAILABLE FUNDS	7
3.2 BUDGETING AND FIXED LIMIT OF CONSTRUCTION COST	7
3.3 CONSULTATION AND VALUE ENGINEERING	7
3.4 CONSTRUCTION COSTS	8
3.5 OTHER PRECONSTRUCTION SERVICES	11
3.6 CONTROL OF THE WORK	14
3.7 SCHEDULE AND COORDINATION	16
3.8 AMENDMENTS AND CHANGE ORDERS	17
3.9 PRINCIPAL REPRESENTATIVE CONSULTANTS.....	17
3.10 START UP	17
4 ARTICLE 4 TIME OF COMMENCEMENT AND COMPLETION	18
4.1 COMMENCEMENT.....	18
4.2 COMPLETION.....	18
5 ARTICLE 5 COMPENSATION	18
5.1 CONSTRUCTION MANAGER’S FEE	18
5.2 ADJUSTMENTS IN FEE.....	20
5.3 PAYMENT OF FEE.....	21
5.4 GUARANTEED MAXIMUM PRICE.....	21

5.5	CONTRACT SUM	23
6	ARTICLE 6 CONDITION PRECEDENT	24
6.1	FUTURE APPROPRIATIONS	24
6.2	OBLIGATIONS	24
7	ARTICLE 7 OPTIONAL PROVISIONS AND ELECTIONS	24
7.1	MODIFICATION OF ARTICLE 2. EXECUTION, CORRELATION, INTENT OF DOCUMENTS, COMMUNICATION AND COOPERATION	24
7.3	MODIFICATION 1 OF ARTICLE 27. LABOR AND WAGES	24
7.4	MODIFICATION 2 OF ARTICLE 27. LABOR AND WAGES	25
7.5	MODIFICATION OF ARTICLE 39. NON-BINDING DISPUTE RESOLUTION – FACILITATED NEGOTIATIONS.....	25
7.6	MODIFICATION OF ARTICLE 45. GUARANTEE INSPECTIONS AFTER COMPLETION.....	25
7.7	MODIFICATION OF ARTICLE 46. TIME OF COMPLETION AND LIQUIDATED DAMAGES. 25	
8	ARTICLE 8 NOTICE IDENTIFICATION	26
	EXHIBIT A DESIGNATED SERVICES AND METHOD OF PAYMENT	A
	EXHIBIT B CONSTRUCTION MANAGER’S CERTIFICATION	B
	EXHIBIT C REQUEST FOR PROPOSAL	C
	EXHIBIT D CONSTRUCTION MANAGER’S FEE PROPOSAL	D
	EXHIBIT E SALES AND USE TAX FORM	E
	EXHIBIT K BUILDING CODE COMPLIANCE POLICY	A
	SUPPLEMENTARY GENERAL CONDITIONS: FEDERAL PROVISIONS	K

SIGNATURE PAGE

THE PARTIES HERETO HAVE EXECUTED THIS AGREEMENT

Each person signing this Agreement represents and warrants that the signer is duly authorized to execute this Agreement and to bind the Party authorizing such signature.

In accordance with §24-30-202, C.R.S., this Contract is not valid until signed by the State Controller (or an authorized delegate) or the Colorado Mesa University per the Fiscal Rules of the individual Institution of Higher Education

Project Number/Name: 8010-26-1/ CMU 2868 Centennial Village South

Contract ID No.: Insert CMS Number & Encumbrance Number

CONTRACTOR

INSERT: Legal Name of Contractor

STATE OF COLORADO

Jared S. Polis, Governor

INSERT: Name of Agency or IHE

INSERT: Name & Title of Head of Agency or
IHE

By: Name & Title of Person Signing for Contractor

Date: _____

By: Name & Title of Person Signing for Agency or
IHE

Date: _____

OFFICE OF THE STATE ARCHITECT

State Buildings Program

LEGAL REVIEW

Philip J. Weiser, Attorney General

By: Name & Title of Person Signing for State
Buildings

Date: _____

By: Assistant Attorney General

Date: _____

STATE CONTROLLER

Robert Jaros, CPA, MBA, JD

By: Name of Agency or IHE Delegate
Effective Date: _____

STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM

CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT
(STATE FORM SC-6.5)

Department ID: Insert Dept. Code Contract ID #: Insert Contract ID Project #: 8010-26-1

PARTIES. THIS AGREEMENT is entered into by and between the STATE OF COLORADO, acting by and through the Colorado Mesa University hereinafter referred to as the State or Principal Representative, and Insert Contractor's full Legal Name including "Inc.", "LLC" etc. having its offices at Street address, City, State and Zip Code hereinafter referred to as the Construction Manager or the contractor.

EFFECTIVE DATE AND NOTICE OF NONLIABILITY. This Agreement shall not be effective or enforceable until it is approved and signed by the State Controller or its designee (hereinafter called the "Effective Date"), but shall be effective and enforceable thereafter in accordance with its provisions. The State shall not be liable to pay or reimburse Construction Manager for any performance hereunder or be bound by any provision hereof prior to the Effective Date.

RECITALS:

WHEREAS, the Principal Representative intends to engage the services of the Construction Manager to construct the following: Insert Project Name as provided by the State Controller's Office hereinafter called the Project; and

WHEREAS, authority exists in the Law and Funds have been budgeted, appropriated, and otherwise made available, and a sufficient unencumbered balance thereof remains available for payment in In Fund Number Insert Fund Number Here, Account Number Insert Account Number here; and

WHEREAS, the State of Colorado has appropriated and the Principal Representative has been authorized to expend the total sum of Insert dollar value written in words Dollars (\$____) for this Project including all professional services, construction management/general contractor services, construction/improvements, Project contingencies, reimbursables, furnishings, movable equipment, and miscellaneous expenses; and

~~**WHEREAS,** funds are available for only a portion of the services defined herein, as more fully described in Article 6 Condition Precedent hereof; and~~

WHEREAS, the Principal Representative has established the **Fixed Limit of Construction Cost** in the amount Insert dollar value written in words Dollars (\$____); and

WHEREAS, the Construction Manager shall establish a **Guaranteed Maximum Price (GMP)** that is within the Fixed Limit of Construction Cost as established by the Principal Representative at the completion of the Design Development Phase; and

WHEREAS, in accordance with Article 5 Compensation the Construction Manager's total fee and The General Conditions of the Construction Manager/General Contractor Agreement ("General Conditions") for the Project is Insert dollar value written in words Dollars (\$____); and

WHEREAS, the Architect/Engineer for the Project is Insert legal name of Design Firm; and

WHEREAS, the Construction Manager acknowledges the statutory authority and responsibility of the Principal Representative within the State of Colorado; and

WHEREAS, the Construction Manager was selected after a determination that its proposal was the most advantageous to the Principal Representative pursuant to a request for proposal issued and awarded on ____; and

WHEREAS, the Construction Manager and the Principal Representative have finalized the terms of this Agreement pursuant to the Colorado Procurement Code or the applicable procurement code for institutions of higher education.

WITNESSETH, that the Principal Representative and the Construction Manager agree as follows:

1 ARTICLE 1 PERFORMANCE OF THE WORK

1.1 THE WORK

1.1.1 The Construction Manager will construct the Project within the Fixed Limit of Construction Cost specified, and the Construction Manager will furnish all the services, labor and materials to perform all the Work, including design, for the complete and prompt execution of the Project in accordance with the Contract Documents as identified in Section 1.2.

1.1.2 In the performance of the Work under this Agreement, the Construction Manager acknowledges that time is critical for Project delivery and that portions of the Work could have their design completed as separate Bid Packages and under construction before other portions of the Work are fully designed. It is further recognized that this accelerated approach to construction utilizing the services of an Architect/Engineer and Construction Manager is defined as "Fast Track Construction" and requires maximum cooperation between all parties. It is also recognized that the services to be rendered by the Construction Manager and the inter-relationships and coordinative aspects thereof are in the developmental state and not fully defined. The Construction Manager has reviewed the Architect/Engineer's Agreement and accepts the terms thereof as expressing a workable concept. In furtherance thereof, in the event there appears to be a duplication, overlap or conflict of the responsibilities of or duties between the Architect/Engineer and Construction Manager or an absence of designation, the question shall be submitted to the Principal Representative for determination. The Construction Manager shall abide by the decision of the Principal Representative provided it does not

require the performance of work beyond what was reasonably contemplated and is accepted by the Construction Manager as its responsibility. If the Construction Manager claims any increase in the Work arises by virtue of such a decision, it shall give its Notice of Claim as provided in Article 35.

- 1.1.3 The Construction Manager acknowledges that the Principal Representative shall provide Insert number of packages () Bid Packages to accomplish the Work. In the event the Construction Manager for any reason within the Construction Manager's control, requests more than Insert number of packages () Bid Packages to be furnished by the Principal Representative, the Principal Representative shall make arrangement with the Architect/Engineer for the additional Bid Packages desired and shall directly compensate the Architect/Engineer for all fees and cost associated therewith. The Construction Manager shall reimburse the Principal Representative for all of the Architect/Engineer's fees and costs associated therewith.
- 1.1.4 The Construction Manager agrees to use best efforts, to cooperate fully with the Principal Representative in the construction aspects of the Work, and to keep within the Principal Representative's monetary, schedule and quality limitations, as stipulated within this Agreement.
- 1.1.5 The organization of the Specifications into division, section, and article, and the arrangement of Drawings shall not control the Construction Manager in dividing the Work among any level of Subcontractors or in establishing the extent of the Work to be performed by any trade.
- 1.1.6 The Construction Manager understands the relationship of trust and confidence established between it and the Principal Representative and accepts those responsibilities as described in this Agreement. The Construction Manager covenants with the Principal Representative to furnish its best skill and judgment and to cooperate with the Architect/Engineer in furthering the interests of the Principal Representative. The Construction Manager agrees to furnish efficient business administration and superintendence and to use its best efforts to complete the Work in an expeditious and economical manner consistent with the interests of the Principal Representative.
- 1.1.7 The Construction Manager, the Principal Representative, and the Architect/Engineer, called the "Construction Team", shall work during design through to construction completion. The Construction Manager shall provide leadership to the Construction Team on all matters relating to construction.
- 1.1.8 The Architect/Engineer is a representative of the Principal Representative as provided in the Contract Documents and its Agreement is with the Principal Representative. In case of termination of employment or death of the Architect/Engineer, the Principal Representative shall appoint a capable and reputable Architect/Engineer against whom the Construction Manager makes no reasonable objection, whose status under the Agreement shall be the same as that of the former Architect/Engineer.
- 1.1.9 The Architect/Engineer shall not be responsible for or have control or charge of construction means, methods, techniques, sequences or procedures, or for safety precautions and programs in connection with the Work and except for the Architect/Engineer's specifically enumerated Contract Administration duties such as observation of the Work, shall not be responsible for the Construction Manager's failure

to carry out the Work in accordance with the Contract Documents. The Architect/Engineer shall not be responsible for or have control or charge over the acts or omissions of the Subcontractors of any tier or any of their agents or employees, or any other persons performing any of the Work.

1.1.10 The Contract Documents shall not be deemed to create any contractual relationship between the Architect/Engineer and the Construction Manager or any separate contractors, Subcontractors of any tier or suppliers on the Project; nor shall anything contained in the Contract Documents be deemed to give any third party any claim or right of action against the Principal Representative, the Architect/Engineer or Construction Manager which does not otherwise exist without regard to the Contract Documents.

1.1.11 The initial Work of the Construction Manager shall consist of its services in connection with the Preconstruction Phase. The Preconstruction Phase of the Work shall be parallel and coincidental with the Schematic Design, Design Development, and Construction Document Phases as defined in the Architect's Engineer's CMGC Agreement. As the Bid Packages are prepared and prices are established for the work to be performed within each respective Bid Package, the parties contemplate that the work to be performed by the Construction Manager shall be adjusted by Amendment or Change Order to this Agreement to place the work contained within the various Bid Packages within the work to be performed by the Construction Manager with corresponding adjustments made to the Contract Sum, Guaranteed Maximum Price and Contract Time.

1.2 CONTRACT DOCUMENTS

1.2.1 The Contract Documents are described in Article 1.1 of the General Conditions of the Construction Manager/General Contractor Agreement (SC-6.51) and are essential parts of this Agreement and are fully incorporated herein.

1.2.2 Capitalized terms used herein and not defined shall have the meanings ascribed to them in The General Conditions of the Construction Manager/General Contractor (CMGC) Agreement (SC-6.51)

1.2.2

2 ARTICLE 2 EXHIBITS TO THE AGREEMENT

2.1 EXHIBITS

The following Exhibits are, or will be, attached to this Agreement and are or shall become when approved and accepted, part of the Contract Documents.

1. Exhibit A, Construction Manager's Designated Services and Method of Payment;
2. Exhibit B, Construction Manager Certification;
3. Exhibit C, Request for proposal (minus blank template forms) dated ;
4. Exhibit D1, Construction Manager's Fee Proposal dated ;
5. Exhibit D2, Construction Manager's Certificates of Insurance;
6. Exhibit D3, Construction Manager's Direct Labor Burden Calculation;
7. Exhibit E, State Sales and Use Tax Forms;

Amendment Exhibits based on Schematic Design Documents

8. Exhibit F, List of Pre-Qualified Subcontractors (Add by Amendment when approved by the Principal Representative and prior to bidding);

9. Exhibit G, Schematic Design Estimate Summary and Updated Summaries (Add by Amendment when approved by the Principal Representative);

Amendment (incorporating GMP) Exhibits based on Design Development Documents

10. Exhibit H.1, GMP Documents, Drawings and Specifications including Addenda and Modifications (When approved by the Principal Representative);
11. Exhibit H.2, Schedule of Anticipated Bid Package Descriptions and Issuance Dates (as applicable);
12. Exhibit H.3, Schedule of Values (prepared at the time of the GMP Amendment);
13. Exhibit H.4, Allowance Schedule (prepared at the time of the GMP Amendment);
14. Exhibit H.5, Detailed Critical Path Method Construction Schedule (Prepared at the time of the GMP Amendment);

Subsequent Amendments (incorporating Bid Packages) Exhibits

- a) Exhibit I.1, Drawings, Specifications and Addenda (When approved by the Principal Representative);
- b) Exhibit I.2, Schedule of Values (Consistent with GMP Schedule of Values);
- c) Exhibit I.3, Labor Overhead (SBP-6.18) for each Subcontractor to be applied to all change orders and Amendments);
- d) Exhibit I.4, Allowance Schedule (consistent with GMP Allowance Schedule);
- e) Exhibit I.5, Performance Bond (Form SC-6.22);
- f) Exhibit I.6, Labor and Material Payment Bond (Form SC-6.221);
- g) Exhibit I.7, Insurance Certificates;
- h) Exhibit I.8, Detailed Critical Path Method Construction Schedules (when approved by the Principal Representative);
- i) Exhibit I.9, Applicable Prevailing Wage Determinations (If applicable)
- j) Exhibit I.10, Apprenticeship Utilization Certifications (SBP-2.1) (If applicable)

Miscellaneous Exhibits

- k) Exhibit J, Notice to Proceed to Commence Construction Phase (Form SC-7.26) (when issued);
- l) Exhibit K, Building Code Compliance Policy: Coordination of Approved Building Codes, Plan Reviews, and Building Inspections.
- m) Supplementary General Conditions: Federal Provisions (if applicable);
- n) SLFRF Federal Funds: Contractor Terms and Conditions - Certification (if applicable); and
- o) SLFRF Federal Funds: Contractor Terms and Conditions (if applicable).

3 ARTICLE 3 CONSTRUCTION MANAGER'S SERVICES

The Construction Manager shall perform the following services under this Agreement in each of the phases described below:

PRECONSTRUCTION SERVICES

SC-5.3

Rev. 07/2025

3.1 AVAILABLE FUNDS

- 3.1.1 The Construction Manager acknowledges that the Principal Representative is limited in the sum available to design and construct the Project. Should funding of a lesser amount be made available for the Project, it is the obligation of the Principal Representative to revise the Project scope consistent with the ultimate appropriation.

3.2 BUDGETING AND FIXED LIMIT OF CONSTRUCTION COST

- 3.2.1 The Construction Manager shall assist the Architect/Engineer in evaluating the Principal Representative's preliminary budget. Based on consultation with the Architect/Engineer and the Construction Manager, the Principal Representative shall furnish a Project Budget ("Project Budget" to the Construction Manager which shall set forth the dollar amount available for the total construction cost of the Project and include contingencies for bidding and construction.

- a) The Fixed Limit of Construction Cost has been established by the Principal Representative, converting the applicable portion of the Project Budget into the Fixed Limit of Construction Cost, as set forth in the Recitals above.
- b) The Fixed Limit of Construction Cost may be revised only by approved Amendments or Change Orders issued after execution of the Contract Documents.

3.3 CONSULTATION AND VALUE ENGINEERING

- 3.3.1 The Construction Manager shall provide consultation throughout the Preconstruction and Construction phases including but not limited to the furnishing of Value Engineering Services to identify cost effective changes in the State's specifications that will result in reducing the Contract price without impairing essential functions or characteristics. The objective of Value Engineering is to achieve optimum value for each construction dollar spent and keep the time of completion and cost of the Work within the time and fiscal constraints set forth throughout the Contract Documents. In cooperation with the Principal Representative, the Construction Manager shall:

- a) Formulate and evaluate alternative designs, systems, materials, etc.;
- b) Provide cost estimates of the alternatives to be evaluated. Cost estimates shall include industry standard operating and maintenance costs when appropriate to evaluate life-cycle costs of the alternatives. Cost estimates shall take into consideration all cost impacts related to alternatives including but not limited to construction costs. The Construction Manager shall, at a minimum, review the cost estimate at the completion of the Schematic Design, and Design Development Phases and include an analysis and commentary as to any discrepancies observed in the report referenced in paragraph 3.3.1.d below;
- c) Evaluate the alternatives on the basis of costs, time schedules, availability of labor and materials, construction feasibility, etc.;
- d) With the assistance of the Architect/Engineer prepare written reports at the end of the Schematic Design and Design Development Phases summarizing the Value Engineering activities accomplished and any recommendations developed within each phase;
- e) If estimates of construction and/or bids received for the Work contained in any Bid Package cause the anticipated cost of the Work to exceed the then current Estimate

of Construction Cost, the Fixed Limit of Construction Cost, the Guaranteed Maximum Price or Schedule of Values, the Construction Manager shall, at no additional cost to the Principal Representative unless caused by an increase in the Construction Manager's Work requested by the Principal Representative, provide additional Value Engineering services in conjunction with any and all appropriate items in the Estimate of Construction, the Fixed Limit of Construction Cost, the Guaranteed Maximum Price, and/or the Schedule of Values for the Work; and

- f) Lead a formal Value Engineering workshop as requested by the Principal Representative, at the end of the Schematic Design, Design Development and Construction Documents Phases review and estimating tasks, bringing multidiscipline cost/construction experts to evaluate alternative designs, systems and materials.

3.3.2 The Principal Representative shall participate in the formulation and evaluation of alternatives in the Value Engineering activity, and shall approve Value Engineering alternatives accepted in each design phase.

3.4 CONSTRUCTION COSTS

3.4.1 It is the desire of the Principal Representative to incorporate as many alternate bid items into the Project as reasonable, in order to maximize the scope for the Fixed Limit of Construction Cost. All parties recognize that the availability of costs to perform the Work depend, in part, upon favorable market conditions. With thorough and careful planning, cost estimating and cooperation, funds may become available for the alternates through the procurement process at less than the Construction Manager's estimated cost therefore. Together with savings through the unexpended portion of the bidding contingency, the Principal Representative may authorize alternates and/or additional scope, all within the Fixed Limit of Construction Cost.

3.4.2 To accomplish the inclusion of alternates and/or increases, the Project contingency shall be as follows and included in the GMP:

- a) The bidding contingency for all Bid Packages together with the construction of the Work shall be equal to at least two point five percent (2.5%) of the total Guaranteed Maximum Price, all within the Fixed Limit of Construction Cost.

The bidding contingency shall be allocated between the presently Insert number of packages (____) Bid Packages, equally proportionate to the value associated with each Bid Package. The Construction Manager shall notify, in writing, the Principal Representative of the allocation of the bidding contingency for each Bid Package.

- b) The construction contingency for the Work shall be equal to at least three percent (3%) of the total Guaranteed Maximum Price, all within the Fixed Limit of Construction Cost.

3.4.3 At the conclusion and award of the Bid Packages, all differences between the Construction Manager's estimated cost of the Work contained within the Bid Packages, exclusive of contingency, versus the actual cost thereof as determined by bidding and award (buyouts) of subcontracts shall be promptly calculated and totaled. If the total of all of the buyouts exceed the Construction Manager estimated cost therefore, the bidding contingency identified in paragraph 3.4.2.a shall be applied by the Construction Manager, after prior written notice to the Principal Representative, to cover any overrun per Bid Package.

3.4.4 After all of the Bid Packages have been bought out, and subcontracts and purchase agreements have been executed, any and all savings achieved through the buyouts of the Bid Packages together with all unexpended sums remaining in the bidding contingencies shall forthwith accrue to the Principal Representative to be applied by the Principal Representative, in its sole and absolute discretion, to include desired alternates into the Work or to otherwise increase the Scope of Work to be performed by the Construction Manager, and/or to reduce the Guaranteed Maximum Price.

3.4.5 The construction contingency shall only be used to cover costs for labor, materials, equipment and similar costs for items or Work to be furnished during the Construction Phase of the Project. It is not the intent of this Agreement to use the construction contingency for costs incurred during the Preconstruction phase or bidding phase or for costs to correct any errors, omissions, mistakes or rejected Work caused by Subcontractors. The construction contingency may be used to cover the Construction Manager's costs (i) arising from estimating cost overruns in the costs of **Exhibit H.4** Allowance Schedule; (ii) unexpected additional trade coordination costs incurred for Work directly performed by the Construction Manager that could not have been reasonably contemplated; (iii) items required and reasonably inferable from the Contract Documents, or items included within the Contract Documents but missed within the Subcontractor buy-out which the Construction Manager can show were not specifically called out within the estimate or bid documents of the Construction Manager or any Subcontractor ; (iv) losses or damages to property related to the Work not covered by insurance provided by the Construction Manager and including any insurance deductible(s); (v) arising from expediting or acceleration of the Project schedule where such cost is not a basis for an increase in the GMP under Article 7.6 of the Agreement;; (vi) Bid Package buyout overrun costs for additional Bid Packages that were not part of anticipated Construction Phases defined in 1.1.3, but only if bidding procedures contemplated hereunder were followed and the bidding contingency has been exhausted; or (vii) other costs incurred not reasonably expected that are approved by the Principal Representative in the Principal Representative's sole discretion, so long as those costs are not recovered under any insurance policy provided pursuant to this Agreement and so long as the total costs under this Agreement do not exceed the Guaranteed Maximum Price. No expenditure from the construction contingency for any matters or Work activities shall be made without the prior written approval of the Principal Representative, which approval, with the exception of item (vii) above, shall not be unreasonably withheld. Expenditures from the construction contingency shall be made only by Change Order.

The Construction contingency shall include all costs associated with a stated scope including, if applicable, direct work, insurance, bonds, fees, and General Conditions (if appropriate).

3.4.6 When preparing any estimates of construction and in development of the Schedule of Values, such documents shall include, without duplication:

- a) All labor, materials, equipment, tools, construction equipment and machinery, water, heat, utilities, transportation, and other facilities and services necessary for the proper execution and completion of the Work, whether temporary or permanent, and whether or not incorporated or to be incorporated in the Work;

- b) Any allowance designated by the Principal Representative;
 - c) Any Principal Representative furnished equipment which has been designed, specified, selected or specifically provided for by the Architect/Engineer;
 - d) The Construction Manager's fee and the cost of work provided by the Construction Manager;
 - e) All bonds, insurance premiums and applicable taxes;
 - f) Contingencies for bidding, price escalation, and construction;
 - g) Plumbing and electrical building permits from appropriate entities and any other building permits as directed by the Principal Representative; and
 - h) Administrative expenses directly related to the Work. (Refer to Section 12.2, Schedules of the General Conditions (SC-6.51))
- 3.4.7 Estimates of Construction Cost shall not include the compensation of the Architect/Engineer and, the Architect/Engineer mechanical, electrical, plumbing, structural, civil, and any other consultants and subconsultants required in the Request For Proposal or any other sums due the Architect/Engineer and its consultants, and shall not include the costs of land, right of way, financing or other costs, which are the responsibility of the Principal Representative.
- 3.4.8 The Construction Manager, in preparing its estimates of construction cost and providing the Guaranteed Maximum Price, shall consult with the Architect/Engineer to determine what materials, equipment, component systems and types of construction are to be included in the Contract Documents, to make reasonable adjustments in the scope of the Work, and to include in the Contract Documents alternate items, as approved by the Principal Representative in writing, for bid so as to permit the adjustment of the estimate of construction cost.
- 3.4.9 The Construction Manager shall prepare an estimate of construction as soon as major Project requirements have been identified and update it periodically. For the Schematic Design Phases, the Construction Manager shall prepare a quantity take-off cost estimate based on building systems, assemblies, components, etc., and update periodically. During the Design Development Phase, the Construction Manager shall prepare a final cost estimate in preparation for a Guaranteed Maximum Price and update periodically. All estimates of construction shall include separate defined allowances for bidding and Construction price escalation. During the Construction Documents Phase, the Construction Manager shall continually monitor the cost estimates and develop a cost estimate to help assure that the cost of the Work remains within the applicable portion of the Project Budget, Fixed Limit of Construction Cost and Guaranteed Maximum Price.
- 3.4.10 Estimates shall be prepared and shall be based on quantitative takeoffs whenever possible and shall be supported in sufficient depth and organization to be used in preparing budgets based on Construction Specifications Institute (CSI) Division, funding sources, sub-trades, combinations of sub-trades, building systems, Bid Packages or combinations thereof. The specific cost coding structure, estimating guidelines, assumptions, and contents of the cost estimates shall be mutually resolved between the Construction Manager and the Architect/Engineer prior to development of the first cost estimate to assure that estimates developed by all parties can be compared and reconciled. Lump sum estimates are not acceptable.

- 3.4.11 During the preparations of cost estimates, the Construction Manager shall notify the Principal Representative if it appears that the Estimate of Construction will exceed the applicable portion of the Project Budget or Fixed Limit of Construction Cost, as may be applicable, satisfactorily demonstrate the accuracy of its estimate in such detail as shall be reasonably required by the Principal Representative, and make reasonable recommendations for corrective action consistent with the Project Budget or Fixed Limit of Construction Cost, as may be applicable. The Construction Manager shall submit Estimates of Construction Cost to the Principal Representative for review and acceptance at each design milestone and other times as required by the Principal Representative to analyze various building systems and components. Concurrently, the Construction Manager shall provide copies to the Architect/Engineer for review and verification.
- 3.4.12 The Principal Representative shall reasonably cooperate with the Construction Manager to keep the Work within the applicable portions of the Project Budget or Fixed Limit of Construction Cost, as may be applicable, including but not limited to the giving of appropriate and reasonable consideration to all reasonable recommendations of the Construction Manager, approving redesign, only for Principal Representative directed scope changes, deductive alternatives or reductions in Work, requesting additional Value Engineering, making modifications to the Contract Documents or exercising such other rights or remedies as may be available elsewhere under this Agreement including termination for convenience. However, the Principal Representative shall be under no duty to reduce the Work to accommodate for any projected costs over or beyond the Guaranteed Maximum Price that is the responsibility of the Construction Manager or allow access to the construction contingency to cover costs to correct errors, omissions, mistakes, rejected Work or warranty Work.
- 3.4.13 Architect/Engineer/Construction Manager Cooperation: The Architect/Engineer, by the terms of its agreement with the Principal Representative, is obligated to provide reasonable cooperation to the Construction Manager in the development of Estimates of Construction Cost and the Guaranteed Maximum Price. Conversely, the Construction Manager, by the terms of this Agreement is obligated to provide reasonable cooperation to the Architect/Engineer in their development of Statements of Probable Construction Cost and the Guaranteed Maximum Price. Additionally, both Architect/Engineer and Construction Manager are obligated to reconcile their respective cost estimates at the completion of each design phase of the Work including the Guaranteed Maximum Price in a timely manner so as not to negatively impact the Project Schedule.

3.5 OTHER PRECONSTRUCTION SERVICES

- 3.5.1 The Construction Manager shall perform those items designated as Required Services as set forth in the Designated Services and Method of Payment schedule designated as **Exhibit A**. In addition, and not in limitation, the Construction Manager shall also perform the other Preconstruction Services designated in this Article 3 together with such other services as are normally and customarily provided by a Construction Manager.
- 3.5.2 Meeting Attendance: The Construction Manager shall attend all regular meetings with the Principal Representative and such additional meetings as the Principal Representative may request. All regular meetings shall be scheduled by the Architect/Engineer with the Construction Manager and approval of the Principal Representative. All additional meetings shall be requested by the Principal Representative.

- 3.5.3 Copies for Review: The Principal Representative through the Architect/Engineer and consistent with the Principal Representative's contract with the Architect/Engineer, shall furnish the Construction Manager a sufficient quantity of documents required for the Preconstruction Services.
- 3.5.4 The Construction Manager shall make recommendations to the Principal Representative and the Architect/Engineer regarding the division of Work in the Drawings and Specifications to facilitate the bidding and awarding of subcontracts, allowing for phased construction and funding, if applicable, taking into consideration such factors as time of performance, availability of labor, overlapping trade jurisdictions, provisions for temporary facilities, etc.
- 3.5.5 The Construction Manager shall review Drawings and Specifications with the Architect/Engineer to (1) eliminate areas of conflict, overlapping trade jurisdictions, and overlapping in the Work to be performed by the various Subcontractors, (2) endeavor to confirm that all Work has been included, and (3) allow for phased construction as applicable.
- 3.5.6 The Construction Manager shall participate in Project design review sessions at the close of the Schematic Design Phase, the Design Development Phase, and as Construction Documents are finalized for each Bid Package. The Project design review sessions shall be attended by the Architect/Engineer and representatives of the Principal Representative. The purposes of the Project design review sessions are to (1) assure consistency with the design intent; (2) confirm complete, coordinated, constructible and cost-effective designs for all disciplines (e.g. architectural, structural, mechanical); (3) assure that the design documents are code compliant per **Exhibit K** Building Code Compliance Policy: Coordination of Approved Building Codes Plan Reviews and Building Inspections; (4) confirm that all Work has been included and described in sufficient detail to assure complete pricing of Work; and (5) allow for phased construction. The Architect/Engineer shall collect all design review comments from the various participants, provide reports to the Principal Representative, and confirm that with the issuance of each progress set of design documents all comments have either been incorporated or resolved to the satisfaction of the Principal Representative.
- 3.5.7 The Construction Manager recognizes that the Principal Representative is a Governmental Body with certain procedural requirements to be satisfied. The Construction Manager has and shall make reasonable allowance in its performance of the Work for such additional time as may be required for approvals and decisions by the Principal Representative, in addition to the times specifically provided in paragraph 3.5.8.
- 3.5.8 In the review process of the final Design Development Documents and Construction Documents for each Bid Package, the Construction Manager expressly agrees to the following review times by the Principal Representative:
- a) A period of fourteen (14) days following submission by the Architect/Engineer to the Principal Representative for the review of the Design Development Documents; and
 - b) A period of fourteen (14) days prior to completion of the Construction Documents together with an additional seven (7) days after receipt of all bid documents for each Bid Package, commencing with the date of receipt by the Principal Representative of all documents and any other items which are required to be furnished to the Principal

Representative by the terms of the Principal Representative's contract with the Architect/Engineer.

- 3.5.9 As part of the Schematic Design review and estimating tasks, the Construction Manager shall develop a preliminary detailed Critical Path Method (CPM) Project Schedule as described in Article 12 of the General Conditions of the Agreement (SC-6.51), that is coordinated with the milestone dates specified in **Exhibit H.2**, tSchedule of Bid Package Descriptions and Issuance Dates, the date of completion ("Date of Completion") specified in paragraph 4.2.1, the scope of Work described within the Contract Documents, and the Work described within the Schematic Design Documents. The Construction Manager shall utilize the Project Management Software as defined in paragraph 3.6.4 to develop and manage the schedule.
- 3.5.10 Principal Representative Purchasing: The Construction Manager shall investigate and recommend materials and equipment that could be purchased by the Principal Representative; consider long lead time procurement and mass purchasing power in making such recommendations; recommend a schedule for such purchases after coordination with the schedule for preparation of Contract Documents; and expedite and coordinate delivery of these purchases to facilitate their delivery by the required dates.
- 3.5.11 The Construction Manager shall prepare necessary bidding information, bidding forms, and pre-qualification criteria for bidders; develop Subcontractor interest in the Project; establish bidding schedules; advertise for bids; and conduct pre-bid conferences to familiarize bidders with the bidding documents and management techniques and with any special systems, materials, or methods. As soon as the Construction Manager becomes aware prior to any bid date that less than three (3) pre-qualified Subcontractors plan to bid any portion of any Bid Package or that anticipated bids from previously approved or pre-qualified Subcontractors listed on **Exhibit F**, are likely to exceed the then current Schedule of Values or Estimate of Construction Cost, the Construction Manager shall promptly notify the Principal Representative and Principal Representative shall be entitled to Subcontractor substitution pursuant to Article 15.5 of the General Conditions of the Agreement (SC-6.51)
- 3.5.12 The Construction Manager shall receive and open bids when advertised, prepare a bid analysis, conduct pre-award conferences, and notify the Principal Representative concerning which bids shall be accepted. The Principal Representative shall be notified in advance of the time and place of all bid openings and may elect to attend such openings with their representatives. Should the Construction Manager submit a proposal for subcontract Work (Work not included in the Construction Manager's Construction Phase Fee and/or General Conditions) herein referred to as "Self Performed Work", the proposal conditions shall be the same as for all Subcontractor proposals. These Construction Manager proposals for Self Performed Work shall be submitted to the Principal Representative twenty-four (24) hours prior to receipt of other Subcontractor proposals and all opened with the other proposals. The Construction Manager's team performing such work may include its employees, material providers, and Subcontractors. If the Construction Manager is chosen to perform the Work, then such Self Performed Work shall be performed for the Construction Manager's bid amount on the basis of a stipulated lump sum. A proposal to accept other than a low bid shall be justified in writing by the

Construction Manager and subject to prior written approval by the Principal Representative.

3.5.13 The Construction Manager shall provide the requirements and assignment of responsibilities for safety precautions and programs as required for the execution of the Work, temporary Project facilities and for equipment, materials and services for common use of Subcontractors and verify that all are included in the Contract Documents.

3.5.14 The Construction Manager shall provide not later than the first of each month, unless requested otherwise by the Principal Representative, a monthly report utilizing the Project Management Software defined in paragraph 3.6.4 documenting the current status of the Project's schedule, costs, requests for information, submittals, manpower, safety, and other pertinent information. The report shall include a narrative discussion of the progress achieved, activities anticipated for the next month, and issues that are affecting the rate of progress. Photos shall be required when requested by the Principal Representative. These progress photographs should be attached/included. This monthly report shall be provided in Construction Phases of the Project. The schedule status shall include the following minimum items:

- a) Cost report showing activity dollar value, dollar value of Work in place to-date and dollar value for current period.
- b) Cost report showing activity dollar value, dollar value of Work in place to-date, and dollar value for current period summarizing to Schedule of Values.
- c) Resource report showing labor allocations by specific trade on each activity.
- d) Variance report comparing current dates to target dates.
- e) Cash flow report showing monthly projections of expenditures.

A narrative schedule report shall document:

- a) Description of the actual Work accomplished during the reporting period.
- b) Description of any problem areas.
- c) Description of current and anticipated delays with recommended corrective actions to mitigate such delays.
- d) A list of proposed modifications, additions, deletions, and changes in logic to the approved schedule.

CONSTRUCTION PHASE SERVICES

3.6 CONTROL OF THE WORK

3.6.1 The Construction Manager shall supervise and direct the Work of its Subcontractors and shall coordinate the Work with the activities and responsibilities of the Principal Representative to complete the Project in accordance with the Principal Representative's objectives of cost, time and quality and subject to the terms and conditions of the General Conditions of the Agreement (SC-6.51).

3.6.2 The Construction Manager shall establish on-site organization and lines of authority in order to carry out the overall plans of the Construction Team.

- 3.6.3 The Construction Manager shall schedule and conduct weekly progress meetings at which the Principal Representative, Construction Manager, Architect/Engineer, and Architect/Engineer's Consultants, can discuss jointly such matters as procedures, progress, schedule, costs, quality control and problems. The Construction Manager shall record and distribute minutes of all construction meetings within 48 hours of the meeting.
- 3.6.4 A contract-control/project-management software (hereafter "Project Management Software") approved by the Principal Representative, shall be used as a primary tool for Project control, communication and documentation control by all the Project participants, to include the Principal Representative, the Construction Manager and the Architect/Engineer. The Construction Manager shall utilize the Project Management Software to implement a cost forecasting, monitoring, control and reporting system for the Project. The Project Management Software shall be maintained throughout the project, both during the Preconstruction and construction phases. Cost analyses shall be based upon data analyses as developed/described within Section 3.3 and shall include analyses of all trades and Project components making a significant contribution for total Project costs. The Project Management Software shall provide for development of a Project cost model, monitoring the design process and periodic reviews of the cost estimates/forecasts to identify variances from the cost model. Additionally, the Project Management Software shall identify variances between actual and budgeted costs and the Fixed Limit of Construction Cost and the Contract Sum.

The Construction Manager shall use the Project Management Software for the major contract administration processes to include, but not limited to:

- 3.6.4.1 Submittals: Construction Manager shall create a Submittal log and Submittal schedule. Submittals shall be directly submitted to the Architect/Engineer and Principal Representative and directly returned from the Architect/Engineer.
- 3.6.4.2 Requests for Information: Construction Manager shall submit requests for information using the Project Management Software. Architect/Engineer shall answer requests for information via the Project Management Software. Requests for Information responses that have cost impact will have corresponding Change Order Bulletin (Form SC-6.311) issued by the Architect/Engineer.
- 3.6.4.3 Change Management: Entire change management process including Notices, and Change Orders shall be managed using the Project Management Software and utilizing Contract Amendment (Form SC-6.0A,B or C), Change Order (Form SC-6.31B), Change Order Bulletin (Form SC-6.311), Change Order Proposal (Form SC-6.312) and change order log.
- 3.6.4.4 Pay Applications: Construction Manager shall be responsible for creating and distributing pay application in the Project Management Software using an earned-value calculation through the CPM Schedule & utilizing Application and Certificate for Contractor's Payment (SBP-7.2).
- 3.6.4.5 Meeting Minutes: Construction Manager shall be responsible for creating and distributing construction-meeting minutes in the Project Management Software.
- 3.6.4.6 Reports: Construction Manager shall be responsible to prepare and distribute reports in the Project Management Software.

- 3.6.4.7 Insurance Certificate: Construction Manager shall responsible for storing all the insurance related information of Subcontractors in the Project Management Software.
- 3.6.4.8 Punch list: Construction Manager shall be responsible to update the Substantial Completion punch list status using the Project Management Software.
- 3.6.4.9 Construction Schedule: Critical Path Method as described in Article 12 of the General Conditions of the Agreement (SC-6.51).
- 3.6.4.10 All project correspondence with Principal Representative shall be in the Project Management Software.
- 3.6.4.11 The Construction Manager shall propose and implement an approved procedure for coordinating and tracking all required Code Compliance Building Inspections as indicated on the Building Inspection Record (BIR) as provided by the State Buildings Program approved Code Review Agent at the appropriate Construction Phase(s) as described in the attached **Exhibit K** Building Code Compliance Policy: Coordination of Approved Building Codes, Plan Reviews, and Building Inspections.

3.7 SCHEDULE AND COORDINATION

3.7.1 The Construction Manager shall begin the construction Work upon receiving the Notice to Proceed to Commence Construction Phase (SBP-7.26), in accordance with Article 4.1. The Construction Manager shall schedule and coordinate the Work of all of its Subcontractors on the Project including their use of the site. The Construction Manager shall keep the Subcontractors informed of the Project construction schedule to enable the Subcontractors to plan and perform the Work properly. The Construction Manager shall carry the Work forward expeditiously with adequate forces and shall achieve completion of the Work prior to the Date of Completion specified in Section 4.2, as adjusted by Change Orders and Amendments.

3.7.2 Schedule Management

3.7.2.1 Schedule Modifications: If, as a result of the monthly schedule update the Project Schedule no longer represents the actual / logical progression of the Work or the Construction Manager's plan for prosecution and progress of the Work, the Principal Representative shall require the Construction Manager to submit a revision to the Project Schedule. Such revisions to the Schedule shall not alter any of the Project Milestone dates.

3.7.2.2 Schedule Impacts, Schedule Delays, Time Extensions: During the course of the Project, it may be appropriate to revise the Schedule to incorporate impacts or delay issues into the Project Schedule. If the Construction Manager determines it has encountered schedule impacts that may warrant a time extension, the Construction Manager shall present an Impacted Schedule in accordance with Article 38 of the General Conditions of the Agreement (SC-6.51), to the Principal Representative supporting its claim. Note that time extension change order requests, due to weather or other construction delays, do not necessarily or automatically translate into budgetary change order increases.

3.7.2.3 Recovery Schedule: In the event progress falls behind schedule dates, the Construction Manager shall prepare a recovery schedule indicating its revised plan to assure the

timely completion of the Work. The recovery schedule shall be subject to the Principal Representative's approval.

3.8 AMENDMENTS AND CHANGE ORDERS

3.8.1 The Construction Manager shall assist in developing and implementing a system for the preparation, processing and tracking of Amendments and Change Orders using the Project Management Software as described in paragraph 3.6.4 and recommend necessary or desirable changes to the Principal Representative. Fully executed and approved Change Orders shall constitute obligations of the Principal Representative to pay as part of the Contract Sum the amounts identified by such modifications so long as such amounts do not exceed the Guaranteed Maximum Price. Change Orders shall only be used to effect changes in the Work which apply to bidding and construction contingency amounts set forth in paragraphs 3.4. 1 through 3.4.5. Any Changes in the Work that result in an increase in said contingencies shall be added to this Agreement by an Amendment pursuant to Article 35 of the General Conditions of the Agreement (SC-6.51).

3.9 PRINCIPAL REPRESENTATIVE CONSULTANTS

3.9.1 If required, the Construction Manager shall assist the Principal Representative in selecting and retaining the professional services including but not limited to a surveyor, geotechnical, testing and inspection and other special consultants, and coordinate these services, without assuming any responsibility or liability of or for these consultants.

3.10 START UP

3.10.1 The Construction Manager, with the Principal Representative's maintenance staff and/or consultant, shall direct the checkout of utilities, operations, systems and equipment for readiness and assist in their initial start-up and testing/commissioning as required in the Scope Narrative with the Subcontractors of all tiers.

3.10.2 Prior to the Date of Completion of the Work or earlier date for phased occupation of the Work as requested by the Principal Representative, the Construction Manager shall schedule and conduct with the Principal Representative and the Architect/Engineer a complete review, commissioning, demonstration, start-up and operational testing of all equipment and mechanical and electrical systems installed by the Construction Manager or its Subcontractors on the Project, and shall also review the operation and maintenance of such systems with the Principal Representative's maintenance personnel.

3.10.3 Subsequent to this review, the Construction Manager, with reasonable promptness and at no cost to the Principal Representative, shall make all adjustments or corrections required by the Principal Representative or the Architect/Engineer and shall balance all systems in order to make all equipment and systems perform as required by the Contract Documents and to reflect the actual use and occupancy of the Project. If necessary or requested by the Architect/Engineer or Principal Representative, the Construction Manager shall require the Subcontractor, supplier of material supplier to make adjustments, corrections or balancing required by this process, at no additional cost to the Principal Representative.

4 ARTICLE 4 TIME OF COMMENCEMENT AND COMPLETION

4.1 COMMENCEMENT

- 4.1.1 The Contract Time shall commence on the Effective Date of this Agreement but no Work shall be performed prior to the delivery of all bonds, and insurance certificates as required to be furnished by the Construction Manager and described on the Notice of Award.
- 4.1.2 The Construction Phase shall commence on the date the first Bid Package is added to this Agreement by Amendment as approved by the Principal Representative in accordance with Section 1.1.3.
- 4.1.3 The commencement of the Construction Phase is expressly conditioned upon and shall not commence until:
- a) The Guaranteed Maximum Price and Schedule of Values shall have been timely submitted (or such timeliness shall have been waived in writing by the Principal Representative and the State Architect) and shall have been approved and accepted by the Principal Representative;
 - b) The date for Completion of the Work has been approved and accepted by the Principal Representative;
 - c) All required Performance and Labor and Material Payment Bonds and insurance certificates have been approved and accepted by the Principal Representative; and
 - d) **Exhibit J**, Notice To Proceed to Commence Construction Phase (SBP-7.26) has been issued by the Principal Representative and made a part of the Contract Documents. If any of the preceding material conditions to be performed by the Construction Manager have not been fully satisfied by reason of any act or omission on the part of the Construction Manager through no fault of the Principal Representative, the Principal Representative shall give the Construction Manager written notice of any and all such deficiencies and allow ten (10) days from the date of such notice to correct and cure such deficiency or deficiencies, and in the event the deficiency or deficiencies are not fully corrected and cured within the ten (10) day period, the Principal Representative may declare the Construction Manager to be in default of this Agreement.

4.2 COMPLETION

- 4.2.1 The Construction Manager agrees to Substantially Complete the Project in the number of days established in Exhibit I.8, Detailed Critical Path Method Construction Schedules and as described in Article 12 of the General Conditions of the Agreement (SC-6.51). The Date of Completion may be revised by mutual Agreement. The Construction Manager shall perform the Work with due diligence to completion.

5 ARTICLE 5 COMPENSATION

5.1 CONSTRUCTION MANAGER'S FEE

- 5.1.1 Subject to the provisions of this Agreement and of the General Conditions of the Construction Agreement (SC-6.51), and in consideration of the performance of this

Agreement, the Principal Representative shall pay the Construction Manager in current funds as compensation for its services as listed below:

Construction Manager's Fee

1	Pre-Construction Services Phase Fee	\$	
2	Construction Services Phase Fee	\$	
3	Total Fee (1+2)	\$	0

General Conditions

4	Direct Personal Expenses of On-Site CM/GC Staff (Not to Exceed)	\$	
5	Other Reimbursable General Conditions (Not to Exceed per paragraph 5.1.3)	\$	
6	Total General Conditions (including Direct Personnel Expenses of Staff) (4+5)	\$	0
Total Fee and General Conditions (3+6)		\$	0

5.1.2 The Construction Manager's Fee shall include all job indirect costs, and General Conditions costs as defined in **Exhibit A**, Designated Services and Method of Payment, home office overhead, and profit, including but not limited to the following:

- a) Salaries or other compensation of the Construction Manager's employees at the principal office and branch offices;
- b) General operating expenses of the Construction Manager's principal and branch offices other than the field office;
- c) Any part of the Construction Manager's capital expenses necessary for the Project, including interest on the Construction Manager's capital employed for the Project;
- d) Overhead or general expenses of any kind;
- e) Salaries of the Construction Manager's employees engaged on the road in expediting the production or transportation of materials and equipment;
- f) Cost of all employee benefits and taxes for such items as unemployment compensation and social security, insofar as such cost is based on wages, salaries or other remuneration paid to employees of the Construction Manager and included in the fee under paragraphs 5.1.2.a through 5.1.2.f;
- g) All transportation, traveling, moving, and hotel expenses of the Construction Manager or its officers or employees incurred in discharge of duties connected with the Work;
- h) Costs, including transportation and maintenance, of all materials, supplies, equipment, temporary facilities, and hand tools not owned by the workmen, which are employed or consumed in the performance of the Work;
- i) Cost of the premium for all insurance which the Construction Manager is required to procure by this Agreement or is deemed necessary by the Construction Manager;

- j) Minor expenses such as facsimile messages, telegrams, long distance telephone call telephone service at the site, express mail, and similar petty cash items in connection with the Work;
- k) All other items set forth in **Exhibit A**, Designated Services and Method of Payment that are specifically designated as Preconstruction Services Fee, Construction Services Fee or General Conditions. All Items listed in the columns designated Direct Cost of Work shall be included in the separate Bid Packages.
- l) Except as expressly provided to the contrary elsewhere in this Agreement, approved costs in excess of the Guaranteed Maximum Price.

5.1.3 General Conditions items, as set forth in paragraph 5.1.2, shall include the cost of Construction Phase on-site construction management staff and those temporary facilities, services and equipment to support the Work of construction Subcontractors. General conditions items are more fully identified in **Exhibit A**, Designated Services and Methods of Payment, and shall be reimbursed at cost, without mark-up, based upon pre-approved not-to-exceed budgets. General Conditions (exclusive of the Construction Manager's staff) provided directly by the Construction Manager must be at market competitive rates. Each monthly request for progress payment shall be justified with reasonable support for expenses to include:

- a) Invoice or receipt for any vendors or suppliers for material, rented equipment, etc.
- b) Labor/timesheet reports (by task number) for direct labor, provide bare labor rate and itemized breakdown of labor burden prior to initial billing.
- c) Owned equipment shall be compensated per pre-negotiated rates established in accordance with the Colorado Procurement or applicable procurement code for institutions of higher education. In no case shall cumulative/total cost of owned equipment exceed the value of the equipment minus salvage value. The Principal Representative shall approve all rental rates and salvage values in writing prior to initial billing.
- d) Labor, material and equipment cost may be audited by the Principal Representative.
- e)

5.2 ADJUSTMENTS IN FEE

5.2.1 Adjustments in the Construction Phase fee shall be made as follows: If, after the total Guaranteed Maximum Price is accepted, in writing, by the Principal Representative, the Principal Representative directs additions to or other changes made in the Work, the Construction Manager's fee shall be adjusted as follows:

- a) If the changes in the aggregate increase the total Guaranteed Maximum Price, the Construction Manager's fee for any and all other changes in the Work shall be calculated at the rate of FOUR percent (4%) (plus appropriate General Condition costs) of the estimated cost of such work and shall be agreed upon between the Construction Manager and the Principal Representative as a fixed fee for the effect of the change (or changes), prior to starting the changed Work. The adjustments stated above shall only be deemed valid after the Principal Representative accepts the adjustments in writing and, are the only adjustments to the fee that shall be granted for changes authorized to the GMP. Adjustments to these fees beyond these values shall not be granted. However, General Condition costs directly attributable to time

extensions may be charged in accordance with Article 38 of the General Conditions of the Agreement (SC-6.51).

- 5.2.2 The Construction Manager shall also be paid an additional fee at the rate as set forth in paragraph 5.2.1 if the Construction Manager is placed in charge of the reconstruction of any insured loss.
- 5.2.3 If there is a material reduction in the scope of Work greater than fifteen percent (15%) of the Fixed Limit of Construction Cost, the Construction Manager's Fees shall be reduced proportionally after the fifteen percent (15%).

5.3 PAYMENT OF FEE

- 5.3.1 Preconstruction Services Phase Fee: For the performance of the Preconstruction Services ending with the execution of the first Amendment establishing and accepting the Guaranteed Maximum Price of the Work, the fee therefore as set forth in paragraphs 5.1.1 shall be paid monthly and as described in Article 31 of the General Conditions of the Agreement (SC-6.51) with the total payment not to exceed the fee for such services as set forth in paragraph 5.1.1.
- 5.3.2 Construction Services Phase Fee: For the Performance of the Construction Services after the execution of the first Amendment establishing and accepting the Guaranteed Maximum Price of the Work and with the addition of the second Amendment incorporating the first Bid Package and subsequent Amendments incorporating subsequent Bid Packages, the fee therefore as set forth in paragraph 5.1.1 shall be paid monthly as described in Article 31 of the General Conditions of the Agreement (SC-6.51) with the total payment not to exceed the fee for such services as set forth in paragraph 5.1.1. and the portion of the fee to be paid shall be equivalent to the ratio of the dollar value of each Bid Package to the Guaranteed Maximum Price including the premiums for the Performance and Labor and Materials Payment Bonds with coverage up to the value of the Contract Sum.

5.4 GUARANTEED MAXIMUM PRICE

- 5.4.1 At the conclusion of the Design Development Phase, the Construction Manager shall deliver to the Principal Representative, a Guaranteed Maximum Price proposal in which the Construction Manager shall agree to perform all of the Work even though all of the Construction Documents have not all been finalized and released for construction, and guarantee the maximum price to the Principal Representative for the entire cost of the Work, as adjusted by deductive alternates required to maintain the Guaranteed Maximum Price below the Fixed Limit of Construction Cost which has been previously approved by the Principal Representative pursuant to paragraph 3.2.1.a.
- 5.4.2 The Guaranteed Maximum Price shall include all of the Construction Manager's obligations to be performed pursuant to the terms of the Contract Documents and may include, but not be limited to, the total of the following:
 - a) The total of all prices already received for all items bid before the establishment of the Guaranteed Maximum Price;
 - b) The Construction Manager's estimate of the cost of all other Work to be performed but not yet bid, excluding the approved deductive alternates unless said Work can be incorporated into the Contract Documents by application of the contingency per the

provisions of paragraphs 3.4.1 through 3.4.5, with the consent of the Construction Manager which consent shall not be unreasonably withheld;

- c) The installation cost of items to be procured by the Principal Representative and assigned to the Construction Manager for installation, as defined in the Contract Documents;
- d) The estimated maximum cost of all Work to be performed by the Construction Manager;
- e) Construction Manager's fee as provided under this Agreement;
- f) The cost of all Performance and Labor and Material Payment Bonds furnished by the Construction Manager pursuant to Article 26 of the General Conditions of the Agreement (SC 6.51);
- g) The premiums for insurance to protect the Project pursuant to the Article 25 of the General Conditions of the Agreement (SC 6.51); and
- h) Authorized adjustments as set forth elsewhere in this Agreement, to include but may not be limited to: taxes; fees for licenses, and royalties; special conditions, commissioning, start-up services, and warranty support; and contingencies.

5.4.3 The Guaranteed Maximum Price proposal as set forth in Section 5.4 shall:

- a) Set forth a stated not to exceed dollar amount;
- b) Set forth the Schedule of Values therefore which shall be consistent with previously approved Schedules of Values, and adjusted as required pursuant to Design Development cost estimating;
- c) Contain no conditions or exceptions; except as set forth in the Guaranteed Maximum Price proposal;
- d) Not exceed the Fixed Limit of Construction Cost;
- e) Contain no allowances except for those set forth in **Exhibit H.4**, Allowance Schedule, of which all allowances are to be a not-to-exceed dollar amount; whenever costs are more than or less than allowances, the Guaranteed Maximum Price shall be adjusted accordingly by Amendment. The amount of the Amendment shall reflect the difference between actual costs and the allowances; and
- f) Be substantiated with complete supporting documentation acceptable to the Principal Representative, to clearly define the anticipated Work to be performed by the Construction Manager and facilitate a determination thereafter when final drawings and specifications are released for construction, as to whether or not there has been an increase in the Work required of the Construction Manager in the documents released for construction from the Design Development documents on which the Guaranteed Maximum Price was based. If at any time thereafter, any claim is asserted by the Construction Manager for an increase to the Contract Sum or Guaranteed Maximum Price and/or extension of the Contract Time because of an alleged increase in the Work to be performed by the Construction Manager as contained in the drawings or specifications released for construction, the Construction Manager shall be required to demonstrate the increase in the Work to the satisfaction of the Principal Representative; otherwise the Construction Manager shall be entitled to no increase in the Contract Sum, Guaranteed Maximum Price or extension of the Contract Time.

- 5.4.4 If, through no fault on the part of the Construction Manager, and after receiving reasonable cooperation by the Principal Representative, the Construction Manager submits a Guaranteed Maximum Price proposal contrary to the provisions of paragraphs 5.4.2 and 5.4.3, the proposal may be rejected by the Principal Representative; the Principal Representative shall be under no obligation to award subsequent Bid Packages; the Principal Representative may declare the Construction Manager to be in default; and payment may be withheld from the Construction Manager, excepting the Construction Manager's reasonable costs incurred, up and until an acceptable Guaranteed Maximum Price is furnished in accordance with the foregoing.
- 5.4.5 If, in developing a Guaranteed Maximum Price, the Construction Manager believes any documentation or information, consistent with the Design Development Phase level of documentation, is not sufficiently complete to clearly define the anticipated Work, the Construction Manager shall be responsible for making all necessary inquiries and requests to establish the same.
- 5.4.6 When the Guaranteed Maximum Price is agreed upon and accepted by the Principal Representative, it shall be made a part of the Contract Documents by Amendment, shall supersede updated summaries, and all documents relating to Schedules of Values and Estimates of Construction; and shall be subject to modification for Changes in the Work as provided in the Article 35 of the General Conditions of the Agreement (SC-6.51). If the Construction Manager, in good faith, furnishes the Principal Representative with a Guaranteed Maximum Price proposal which meets the criteria of paragraphs 5.4.1, 5.4.2, and 5.4.3 and the parties fail to mutually agree to that number as set forth above, the parties expressly agree that default termination of the Construction Manager shall not be a remedy therefore under this Agreement, and, the Principal Representative shall be entitled to proceed with the Project and Work as set forth elsewhere in this Agreement.
- 5.4.7 When the Construction Manager provides a Guaranteed Maximum Price, the trade contracts for the Work shall either be with the Construction Manager or shall contain the necessary provisions to allow the Construction Manager to control the performance of the Work. The Principal Representative shall also authorize the Construction Manager to take all steps necessary in the name of the Principal Representative to assure that any separate contractors, having separate contracts with the Principal Representative for the Project, perform their contracts in accordance with their terms.

5.5 CONTRACT SUM

- 5.5.1 Subject to the provisions of Article 3 and Article 5 of the Agreement and Article 50, of the General Conditions of the Agreement (SC-6.51) the Contract Sum shall be the total amount payable by the Principal Representative to the Construction Manager for the performance of all Work under the Contract Documents and equal to the total of:
- a) The Construction Costs as set forth in paragraphs 3.4.6 and 3.4.7; and
 - b) Authorized adjustments as set forth elsewhere in this Agreement;

6 ARTICLE 6 CONDITION PRECEDENT

6.1 FUTURE APPROPRIATIONS

Financial obligations of the Principal Representative payable after the current fiscal year are contingent upon funds for the purpose being appropriated, budgeted, and otherwise made available.

6.2 OBLIGATIONS

(At the time of the execution of this Agreement, there are sufficient funds budgeted and appropriated to compensate the Construction Manager only for performance of the Work through and including Insert the phases funded. Therefore, it shall be a condition precedent to the Construction Manager's performance of the remaining Work specified in (parts of Article 3) and the State's liability to pay for such performance, sufficient funding must be made available to the Principal Representative for the Project prior to _____ and, as a further condition precedent, a written Amendment to this Agreement is entered into in accordance with the State of Colorado Fiscal Rules, stating that additional funds are lawfully available for the Project. If either condition precedent is not satisfied by _____, the Construction Manager's obligation to perform Work for (scope of work) and the State obligation to pay for such Work is discharged without liability to each other. If funding is eventually made available after _____, the Construction Manager has no right to perform the Work under (parts of Article 3) of this Agreement and the State has no right to require the Construction Manager to perform said Work.)

7 ARTICLE 7 OPTIONAL PROVISIONS AND ELECTIONS

The provisions of this Article 7 alter or enlarge upon the following Articles of the General Conditions of the Agreement (SC-6.51).

7.1 MODIFICATION OF ARTICLE 2. EXECUTION, CORRELATION, INTENT OF DOCUMENTS, COMMUNICATION AND COOPERATION

If the box below is marked, certification of apprenticeship utilization is required for all mechanical, sheet metal, fire suppression, sprinkler fitting, electrical and plumbing work on the project.

☐ _____ Principal Representative initial

7.2 MODIFICATION OF ARTICLE 13: Shop Drawings, Product Data and Samples

If the box below is marked, this project meets the Statutory definition of Public Project and must comply with the requirements of the Buy Clean Colorado Act §24-92-117, C.R.S. (BCCO) and the BCCO policy established by the State's Office of the State Architect. The Contract Manager is responsible for submitting Environmental Product Declaration (EPD) information for all eligible materials to be used on the Project.

☐ _____ Principal Representative initial

7.3 MODIFICATION 1 OF ARTICLE 27. LABOR AND WAGES

If the box below is marked the Federal Davis-Bacon Act shall be applicable to the Project. The minimum wage rates to be paid on the Project shall be furnished by the Principal Representative and included in the Contract Documents.

☐ _____ Principal Representative initial

7.4 MODIFICATION 2 OF ARTICLE 27. LABOR AND WAGES

If the box below is marked, the State prevailing wage statute shall be applicable to the Project. The minimum wage rates to be paid on the Project shall be furnished by the Principal Representative and included in the Contract Documents.

☐ _____ Principal Representative initial

7.5 MODIFICATION OF ARTICLE 39. NON-BINDING DISPUTE RESOLUTION – FACILITATED NEGOTIATIONS

If the box below is marked, and initialed by the State as noted, the requirement to participate in facilitated negotiations shall be deleted from this Agreement. Article 39, Non-Binding Dispute Resolution – Facilitated Negotiations, shall be deleted in its entirety and all references to the right to the same where ever they appear in the Agreement shall be similarly deleted. The box may be marked only for projects with an estimated value of less than \$500,000.

☐ _____ Principal Representative initial

7.6 MODIFICATION OF ARTICLE 45. GUARANTEE INSPECTIONS AFTER COMPLETION

If the box below is marked the six month guarantee inspection is not required.

☐ _____ Principal Representative initial

7.7 MODIFICATION OF ARTICLE 46. TIME OF COMPLETION AND LIQUIDATED DAMAGES

If an amount is indicated immediately below, liquidated damages shall be applicable to this Project as, and to, the extent shown below. Where an amount is indicated below, liquidated damages shall be assessed in accordance with and pursuant to the terms of Article 46, Time of Completion and Liquidated Damages, in the amounts and as here indicated. The election of liquidated damages shall limit and control the Principal Representative's right to damages only to the extent noted.

7.7.1 For the inability to use the Project, for each day after the number of calendar days specified in the Construction Manager's proposal for the Project and the Agreement for achievement of Substantial Completion, until the day that the Project has achieved Substantial Completion and the Notice of Substantial Completion is issued, the Construction Manager agrees that an amount equal to Insert dollar value in words Dollars (\$_____); shall be assessed against Construction Manager from amounts due and payable to the Construction Manager under the Agreement, or the Construction Manager and the Construction Manager's Surety shall pay to the Principal Representative such sum for any deficiency, if amounts on account thereof are deducted from remaining amounts due, but amounts remaining are insufficient to cover the entire assessment.

7.7.2 For damages related to or arising from additional administrative, technical, supervisory and professional expenses related to and arising from the extended closeout period, for each day in excess of the number of calendar days specified in the Construction Manager's proposal for the Project and the Agreement to finally complete the Project as defined by the issuance of the Notice of Final Acceptance) after the issuance of the final Notice of Substantial Completion, the Construction Manager agrees that an amount equal to Insert dollar value in words Dollars (\$_____); shall be assessed against Construction

Manager from amounts due and payable to the Construction Manager under the Agreement, or the Construction Manager and the Construction Manager's Surety shall pay to the Principal Representative such sum for any deficiency, if amounts on account thereof are deducted from remaining amounts due but amounts remaining are insufficient to cover the entire assessment.

8 ARTICLE 8 NOTICE IDENTIFICATION

All Notices pertaining to the Agreement or the General Conditions of the Agreement (SC-6.51) or otherwise required to be given shall be transmitted in writing, to the individuals at the addresses listed below, and shall be deemed duly given when received by the parties at their addresses below or any subsequent persons or addresses provided to the other party in writing.

Notice to Principal Representative:

Insert Name of Individual acting on the PR behalf

Insert Street Address

City, State Zip Code

Insert email address

With copies to State Buildings Program (or Delegate:

Insert Name of Individual acting on the SBP behalf

Insert Street Address

City, State Zip Code

Insert email address

Notice to Contractor:

Insert Name of Individual acting on the Contractor's behalf

Insert Street Address

City, State Zip Code

Insert email address

With copies to:

File

**STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM**

**CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT
(STATE FORM SC-6.5)**

EXHIBIT A DESIGNATED SERVICES AND METHOD OF PAYMENT

**DESIGNATED SERVICES AND METHOD OF PAYMENT
(Attached)**

EXHIBIT A**Designated Services and Method of Payment**

PRECONSTRUCTION	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
ARCHITECTURAL SELECTION						X
CIVIL, STRUCTURAL, MECHANICAL, PLUMBING, ELECTRICAL AND OTHER SUB- CONSULTANTS AS APPLICABLE					1	2
SPECIAL CONSULTANT SELECTION						X
SURVEYOR SELECTION						X
SITE SELECTION RECOMMENDATIONS					2	1
REVIEW DESIGN CONCEPTS	X					
DEVELOP BID PACKAGES/SUB- CONTRACTING STRATEGY	1				2	
SITE USE RECOMMENDATIONS	2				1	
MATERIAL SELECTION RECOMMENDATIONS	2				1	
BUILDINGS SYSTEMS RECOMMENDATIONS	2				1	
BUILDING EQUIPMENT RECOMMENDATIONS (MOVEABLE)	2				2	1
BUILDING EQUIPMENT RECOMMENDATIONS (FIXED)	2	2			1	
CONSTRUCTION FEASIBILITY RECOMMENDATIONS	1				2	
PROJECT MASTER SCHEDULING	X					
BID PACKAGE RECOMMENDATIONS	1				2	
LIFE CYCLE COSTING ANALYSIS	2				1	
INFORMAL AND FORMAL VALUE ENGINEERING	X				2	
ENERGY USE ANALYSIS AND RECOMMENDATIONS	2				1	
PRELIMINARY TOTAL COST FEASIBILITY REVIEW	1				2	
LABOR AVAILABILITY REVIEW (SUBCONTRACTORS)	X					
MATERIAL EQUIPMENT AND CONTRACTOR AVAILABILITY	X					

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A**Designated Services and Method of Payment**

PROJECT BUDGETING AND COST CONTROL	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
TOTAL PROJECT COST BUDGET						X
CONSTRUCTION COST BUDGET	X					
CONSTRUCTION COST BUDGET ESTIMATES	X					
PRELIMINARY COST MODEL	X					
SCHEMATIC DESIGN PHASE ESTIMATES	X					
DESIGN DEVELOPMENT PHASE ESTIMATES	X					
BID PACKAGE/SUBCONTRACT ESTIMATES	X					
CASH FLOW PROJECTIONS	X					
PHASE FUNDING MODELING	X					
MATERIAL SURVEYS	X					
TRADE CONTRACTOR ESTIMATES	X					
CHANGE ORDER ESTIMATES			X			
SET-UP COST ACCOUNTING			X			
SET-UP REPORTING METHODS			X			
SET-UP PAYMENT PROCEDURES			2			1
SET-UP CHANGE ORDER PROCEDURES			1		2	1
CONTINUAL PROJECT COST MONITORING			1		2	1

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A

Designated Services and Method of Payment

SUB-CONTRACTING SELECTION AND PURCHASING	PRE- CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
SET PRE-QUALIFICATION CRITERIA	1					2
RECOMMEND SUBCONTRACTOR SELECTION METHODS	X					
RECOMMEND SUBCONTRACTOR AWARD SELECTION METHODS	X					
DEVELOP CONTRACTOR INTEREST	X					
PREPARE BIDDING SCHEDULES	X					
CONDUCT PRE-BID CONFERENCE AND ISSUE PLANS	X					
RECEIVE BIDS	1					2
ANALYZE BIDS	1					2
RECOMMEND AWARD	1				2	2
VERIFY UNIT COSTS	X					
NEGOTIATE UNION RATES AND MANPOWER COSTS REQUIRED	X					
CONDUCT PRE-AWARD CONFERENCES			X			
PREPARE CONTRACTS	X					
SUPPLIER AND SUBCONTRACTOR REVIEW	X					
ORIGINATE RFI'S AFTER SCREENING			X			
PREPARE CHANGE ORDERS			1		2	
VERIFY CORRECTNESS OF QUANTITIES AND PRICES OF CHANGE ORDERS			1		2	
COORDINATE OWNER-SUPPLIED FIXED EQUIPMENT			2		1	1

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A**Designated Services and Method of Payment**

CONTRACT DOCUMENTS COORDINATION	PRE- CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
FEASIBILITY REVIEW AND RECOMMENDATIONS	X					
CONSTRUCTIBILITY REVIEW AND RECOMMENDATIONS	X					
SUBCONTRACTOR WORK SCOPING	X					
RESPONSIBILITY FOR: SAFETY PRECAUTIONS			X			
SAFETY PROGRAMS			X			
TEMPORARY FACILITIES			X			
COMMON USE EQUIPMENT			X			
COMMON USE SERVICES			X			
REVIEW FOR: JURISDICTIONAL OVERLAP	X					
INCLUSION OF ALL WORK	X					
PHASE CONSTRUCTION COORD.	X					
IDENTIFY LONG LEAD ITEMS	X					
OBTAIN AGENCY APPROVALS					2	1
ASSIST IN OBTAINING PERMITS (AS NEEDED)			X			

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A**Designated Services and Method of Payment**

CONSTRUCTION PHASE STAFF	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
PROJECT MANAGER/ASSISTANT PROJECT MANAGER (AS REQUIRED)			X			
PROJECT SUPERINTENDENT (AS REQUIRED)			X			
ASSISTANT PROJECT SUPERINTENDENT			X			
MECHANICAL COORDINATOR (AS REQUIRED)			X			
ELECTRICAL COORDINATOR (AS REQUIRED)			X			
OFFICE ENGINEER (AS REQUIRED)			X			
ENGINEERING AND LAYOUT (AS REQUIRED)				X		
FIELD ENGINEER-LINE AND GRADE (AS REQUIRED)				X		
DRAWING CHECKER (AS REQUIRED)			X			
RODMAN AND HELPERS (AS REQUIRED)				X		
TIME KEEPER/CHECKER (AS REQUIRED)			X			
SCHEDULING ENGINEER (AS REQUIRED)			X			
PROJECT COORDINATOR			X			
COST ENGINEER (AS REQUIRED)			X			
CLERK-TYPIST (AS REQUIRED)			X			
SAFETY ENGINEER (AS REQUIRED)			X			

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A**Designated Services and Method of Payment**

TRAVEL AND LODGING	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
STAFF TRAVEL COST		X				
STAFF TRANSPORTATION		X				
PROJECT STAFF MOVING EXPENSES		X				
PROJECT STAFF SUBSISTENCE COSTS			X			

PHASE: TEMPORARY FACILITIES	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
SAFETY EQUIPMENT AND FIRST AID SUPPLIES			X			
HANDRAILS AND TOE BOARDS			X			
OPENING PROTECTION			X			
FIRE EXTINGUISHERS			X			
WATCHMAN SERVICE				X		
OFFICE OR TRAILER RENTAL			X			
HYDRATION STATION CUPS			X			
TEMPORARY STAIRS			X			
PROJECT SIGNS			X			
BULLETIN BOARDS			X			
CONSTRUCTION FENCING			X			
BARRICADES AND COVERED WALKWAYS (AS REQUIRED)				X		
SAFETY NETS (AS REQUIRED)				X		
A/E TEMPORARY OFFICE (AS REQUIRED)			X			
TEMPORARY TOILETS			X			

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A**Designated Services and Method of Payment**

ON-SITE UTILITIES AND SERVICES	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
TEMPORARY TELEPHONE INSTALLATION AND EXPENSE (INCLUDING LOCAL A/E)			X			
TEMPORARY POWER SERVICE			X			
POWER SERVICE			X			
TEMPORARY WATER AND HEATING SERVICE			X			
HEATING ENERGY CHARGES			X			
TEMPORARY WIRING				X		
LIGHT BULBS				X		
DAILY CLEAN-UP			1	2		
WEEKLY TRASH-REMOVAL			1	2		
FINAL CLEAN-UP			1	2		
DUMP PERMITS AND FEES				X		
DEBRIS HAULING/REMOVAL				X		
FLAGMAN/TRAFFIC CONTROL (AS REQUIRED)				X		
FUELS FOR INITIAL TANK FILLING				X		
TEMPORARY ROADS				X		
ROADWAY MAINTENANCE				X		
DUST CONTROLS				X		
TEMPORARY EROSION CONTROL				X		
TEMP. WATER /SEWER EXPENSE & WATER EXPENSES - SITE GRADING & COMPACTION				X		
TWO-WAY RADIO EQUIPMENT (AS REQUIRED)			X			
TRASH CHUTE AND HOPPERS (AS REQUIRED)				X		

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A

Designated Services and Method of Payment

ON-SITE EQUIPMENT	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
AUTOMOBILE AND FUEL (AS REQUIRED)			X			
PICK-UP TRUCK AND FUEL (AS REQUIRED)			X			
FLATBED TRUCK AND FUEL (AS REQUIRED)			X			
WATER TRUCK (AS REQUIRED)				X		
AIR COMPRESSOR AND FUEL (AS REQUIRED)				X		
DEWATERING EQUIPMENT AND FUEL (AS REQUIRED)				X		
TEMPORARY GENERATOR AND FUEL (AS REQUIRED)			X			
DEBRIS REMOVAL/HAULING EQUIPMENT (AS REQUIRED)				X		
SNOW REMOVAL (AS REQUIRED)			X			
TIRES AND MAINTENANCE COST (AS REQUIRED)			X			
FORKLIFT OPERATOR				X		
MATERIAL HOIST OPERATOR			X			
PERSONNEL OPERATOR			X			
FIXED CRANE OPERATOR				X		
TRAVEL CRANE OPERATOR				X		

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A**Designated Services and Method of Payment**

TEMPORARY HEATING	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
REMOVE SNOW AND ICE (AS REQUIRED)			X			
TEMPORARY ENCLOSURES (AS REQUIRED)				X		
PIPING COST IN BUILDING (AS REQUIRED)			X			
FUEL COST FOR HEATING (AS REQUIRED)			X			
POWER COST FOR HEATING (AS REQUIRED)			X			
FURNACE RENTAL (AS REQUIRED)			X			
HEATER RENTAL (AS REQUIRED)			X			
BOILER RENTAL (AS REQUIRED)			X			
OPERATOR - TEMPORARY SYSTEMS (AS REQUIRED)			X			
OPERATION FIRE WATCH (AS REQUIRED)				X		
CLEANING COST (AS REQUIRED)				X		
MAINTENANCE COST (AS REQUIRED)				X		
EXTENDED WARRANTY COST (AS REQUIRED)				X		
FILTER CHANGE (AS REQUIRED)				X		
TEMPORARY OFFICE HEATING (AS REQUIRED)			X			
TEMP WEATHER PROTECTION & HEATING FOR SUBCONTRACTORS (AS REQ'D)				X		

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A

Designated Services and Method of Payment

REPRODUCTION/PRINTING AND DATA PROCESSING	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
COST STUDY DOCUMENTS					X	
SYSTEMS STUDY DOCUMENTS					X	
BID PACKAGE SETS (SEE PARAGRAPH 3.5.9)	X					
BIDDING INSTRUCTIONS	X					
CONSTRUCTION DOCUMENTS ORIGINAL POSTAGE AND EXPRESS COSTS (CM/GC ISSUES PLANS)			X		X	
AS-BUILT SUB-DOCUMENTS				X		
AS-BUILT DOCUMENTS			X			
ACCOUNTING FORMS		X				
FIELD REPORTING FORMS			x			
SUBCONTRACT AGREEMENT FORMS	X					
SCHEDULE REPORT FORMS			X			
ESTIMATING FORMS	X					
COST REPORTING FORMS	X					
VALUE ANALYSIS STUDIES PRINTING	X					
DATA PROCESSING (MAIN OFFICE)		X				
REFERENCE MATERIALS			X			
SHOP DRAWING PRINTING				X		
ON-SITE FAX AND COPIER			X			
DATA PROCESSING (ON-SITE)			X			
MAINTENANCE MANUALS (FROM SUBS) AND OPERATIONS MANUALS (FROM SUBS)				X		

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A

Designated Services and Method of Payment

QUALITY CONTROL	PRE- CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
FIELD INSPECTOR (AS REQUIRED)			X			
INSPECTORS' OFFICE (AS REQUIRED)			X			
INSPECTORS' TRANSPORTATION (AS REQUIRED)			X			
INSPECTORS' EQUIPMENT (AS REQUIRED)			X			
SPECIAL INSPECTION CONSULTANTS						X
SPECIAL TESTING CONSULTANTS						X
CONCRETE SUBSTRUCTURE- OBSERVATIONS						X
CONCRETE TESTING						X
MASONRY TESTING						X
COMPACTION TESTING						X
WELDING TESTING						X
PIER INSPECTION/TESTING						X
SOILS INVESTIGATION						X
SPECIAL TESTING SERVICES (EXCEPT AS NOTED)						X
PROJECT PHOTOGRAPHS			X			
WARRANTY INSPECTIONS / REWORK		1			2	
AIR AND WATER BALANCING				X		
OPERATOR ON-SITE TRAINING			X			
PREPARE OPERATION/MAINTENANCE MANUALS			2	1		

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A**Designated Services and Method of Payment**

PERMITS AND SPECIAL FEES	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
STORAGE YARD RENTAL				X		
PARKING LOT RENTALS AND SHUTTLE EXPENSES (AS REQUIRED)				2		1
FIELD OFFICE STAFF PARKING FEES			X			
SIGN PERMITS			X			
STREET/CURB PERMIT				X		
BUILDING PERMITS						X
PLAN CHECK FEES						X
WATER SYSTEM DEV. FEE						x
SEWER USE & DRAINAGE PERMIT/DEV. FEE						X
STORM CONNECTION FEE						X
GAS AND POWER SERVICE CHARGE (PERMANENT)						x
GAS AND POWER SERVICE CHARGE (TEMPORARY)			X			
STEAM SERVICE CHARGE						X
CHILLER WATER SERVICE CHARGE						X
SPECIAL TAP FEES						X
CONTRACTORS LICENSES		X				
CONSTRUCTION EQUIPMENT LICENSES		X				
CONSTRUCTION EQUIPMENT PERMITS				X		

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A**Designated Services and Method of Payment**

INSURANCE AND BONDS	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
BUILDERS RISK INSURANCE			X			
GENERAL LIABILITY, INCLUDING AUTOMOBILE			X			
PRODUCT LIABILITY			X			
EXCESS LIABILITY COVERAGE			X			
WORKERS COMPENSATION (FIELD OFFICE STAFF)			X			
FICA INSURANCE (FIELD OFFICE STAFF)			X			
FEDERAL UNEMPLOYMENT (FIELD OFFICE STAFF)			X			
STATE UNEMPLOYMENT (FIELD OFFICE STAFF)			X			
CONSTRUCTION MANAGER'S PAYMENT BOND			X			
CONSTRUCTION MANAGER'S PERFORMANCE BOND			X			
STATE/LOCAL BONDS				X		
* SUBCONTRACTOR BONDS				X		

Responsibility:

x = Total

1 = Primary

2 = Secondary

* Only as mutually agreed upon between the principal representative and the
CONSTRUCTION MANAGER.

EXHIBIT A

Designated Services and Method of Payment

OTHER COSTS	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
CONSTRUCTION EQUIPMENT				X		
CONSTRUCTION SERVICES LABOR				X		
CONSTRUCTION MATERIALS				X		
COST OF DESIGN AND ENGINEERING					X	
A/E FAST TRACK COST EXTRAS					X	
PRELIMINARY SOILS INVESTIGATION						X
TITLE/DEVELOPMENT COST						X
BUILDING OPERATION AFTER MOVE-IN						X
BUILDING MAINTENANCE AFTER MOVE-IN						X
MOVING COORDINATION						X
MOVING COSTS						X
COSTS OF EMERGENCY WORK				X		
CONSTRUCTION MANAGER GENERAL OVERHEAD COST		X				
CONSTRUCTION MANAGER PROFIT MARGIN		X				
GMP FINANCIAL RESPONSIBILITIES		X				
STATE REQUIRED INSPECTIONS						X

Responsibility:

x = Total

1 = Primary

2 = Secondary

EXHIBIT A**Designated Services and Method of Payment**

OFF-SITE SERVICES	PRE-CONST SVCS FEE	CONST SVCS FEE	GEN CONDS.	DIRECT COST OF WORK	REQUIRED OF ARCH	REQUIRED OF OWNER
CORPORATE EXECUTIVES (AS REQUIRED)	X	X				
PRINCIPAL IN CHARGE (AS REQUIRED)	X	X				
PROJECT EXECUTIVE (AS REQUIRED)	X	X				
LEGAL - BASIC SERVICES (AS REQUIRED)	X	X				
ACCOUNTING (AS REQUIRED)		X				
PURCHASING (AS REQUIRED)	X					
SAFETY OFFICER (AS REQUIRED)		X				
EEO OFFICER (AS REQUIRED)	X	X				
SECRETARIAL AND CLERK-TYPIST (AS REQUIRED)	X	X				
BENEFITS AND VACATIONS FOR ABOVE	X	X				
STAFF BONUSES		X				

Responsibility:

x = Total

1 = Primary

2 = Secondary

STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM

CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT
(STATE FORM SC-6.5)

EXHIBIT B CONSTRUCTION MANAGER'S CERTIFICATION

CONSTRUCTION MANAGER'S CERTIFICATION

I hereby certify:

- a. That I am the _____ and duly authorized representative of the firm of:

_____;
and

- b. That the wage rates and other factual unit costs supporting the compensation to be paid by the State for these professional services and other services are accurate, complete, and current; and
- c. That I understand the original Agreement price and any additions shall be adjusted to exclude any significant sums by which the State determines the Agreement price had been increased due to inaccurate, incomplete, or non-current wage rates and other factual unit costs; and
- d. That all such Agreement adjustments shall be made within one year following the end of this Agreement.

CONSTRUCTION MANAGER

Signature

**STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM**

**CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT
(STATE FORM SC-6.5)**

EXHIBIT C REQUEST FOR PROPOSAL

**REQUEST FOR PROPOSAL
(Attached)**

**STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM**

**CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT
(STATE FORM SC-6.5)**

EXHIBIT D CONSTRUCTION MANAGER'S FEE PROPOSAL

CONSTRUCTION MANAGER'S FEE PROPOSAL

- D.1 Construction Manager's Fee Proposal
- D.2 Construction Manager's Certificate of Insurance
- D.3 Construction Manager's Direct Labor Burden Calculation

**STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM**

**CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT
(STATE FORM SC-6.5)**

EXHIBIT E SALES AND USE TAX FORM

**SALES AND USE TAX FORM
(Attach when executed)**

STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM

CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT
(STATE FORM SC-6.5)

EXHIBIT K BUILDING CODE COMPLIANCE POLICY

**BUILDING CODE COMPLIANCE POLICY: COORDINATION OF APPROVED BUILDING CODES, PLAN
REVIEWS, BUILDING INSPECTIONS AND STATE DEVELOPMENT REQUIREMENTS**

Refer to the Office of the State Architect's Building Codes Webpage for the *Building Code Compliance Policy* (Rev. July 2025)

Exhibit A: Approved Building Codes of the *Code Compliance Policy* dated July 2025 including the Amendments to the International Building Code and *Code Compliance Plan Review Procedures* (Rev. July 2025);

Exhibit B: Plan Review Procedures of the *Code Compliance Policy* dated July 2025

Exhibit I: State Development Requirements of the *Code Compliance Policy* dated July 2025

The State Buildings Program [Building Codes Webpage](https://osa.colorado.gov/state-buildings/building-codes) may be found at:
<https://osa.colorado.gov/state-buildings/building-codes>

**STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM**

**CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT
(STATE FORM SC-6.5)**

SUPPLEMENTARY GENERAL CONDITIONS: FEDERAL PROVISIONS

Supplementary General Conditions Federal Provisions

SLFRF Federal Funds: Contractor Terms and Conditions Certification

SLFRF Federal Funds: Contractor Terms and Conditions

**STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM**

THE GENERAL CONDITIONS OF THE CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC) AGREEMENT

(STATE FORM SC 6.51)

STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM

THE GENERAL CONDITIONS OF THE CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC)
AGREEMENT
(STATE FORM SC-6.51)

TABLE OF CONTENTS.....	Page
1 ARTICLE 1 DEFINITIONS	1
1.1 CONTRACT DOCUMENTS	1
1.2 DEFINITIONS OF WORDS AND TERMS USED	2
2 ARTICLE 2 EXECUTION, CORRELATION, INTENT OF DOCUMENTS, COMMUNICATION AND COOPERATION	8
2.1 EXECUTION	8
2.2 CORRELATION	8
2.3 INTENT OF DOCUMENTS	8
2.4 PARTNERING, COMMUNICATIONS AND COOPERATION	9
3 ARTICLE 3 COPIES FURNISHED	10
4 ARTICLE 4 OWNERSHIP OF DRAWINGS	10
5 ARTICLE 5 ARCHITECT/ENGINEER'S STATUS	10
6 ARTICLE 6 ARCHITECT/ENGINEER DECISIONS AND JUDGMENTS, ACCESS TO WORK AND INSPECTION	11
6.1 DECISIONS	11
6.2 JUDGMENTS	11
6.3 ACCESS TO WORK	11
6.4 INSPECTION	11
7 ARTICLE 7 CONSTRUCTION MANAGER'S SUPERINTENDENCE AND SUPERVISION	13
8 ARTICLE 8 MATERIALS AND EMPLOYEES	13
9 ARTICLE 9 SURVEYS, PERMITS, LAWS, TAXES AND REGULATIONS	14
9.1 SURVEYS	14
9.2 PERMITS AND LICENSES	14
9.3 TAXES	14
9.4 LAWS AND REGULATIONS	15
10 ARTICLE 10 PROTECTION OF WORK AND PROPERTY	15
10.1 GENERAL PROVISIONS	15
10.2 SAFETY PRECAUTIONS	15
10.3 EMERGENCIES	16
11 ARTICLE 11 DRAWINGS AND SPECIFICATIONS ON THE WORK	16
12 ARTICLE 12 REQUESTS FOR INFORMATION AND SCHEDULES	17
12.1 DETAIL DRAWINGS AND INSTRUCTIONS	17
12.2 SCHEDULES	17
13 ARTICLE 13 SHOP DRAWINGS, PRODUCT DATA AND SAMPLES	20
13.1 SUBMITTAL PROCESS	20
13.2 FABRICATION AND ORDERING	20
13.3 DEVIATIONS FROM DRAWINGS OR SPECIFICATIONS	20
13.4 CONSTRUCTION MANAGER REPRESENTATIONS	21

14	ARTICLE 14	SAMPLES AND TESTING	21
14.1	SAMPLES		21
14.2	TESTING - GENERAL		21
14.3	TESTING - CONCRETE AND SOILS		22
14.4	TESTING - OTHER		22
15	ARTICLE 15	SUBCONTRACTS	22
15.1	CONTRACT PERFORMANCE OUTSIDE OF THE UNITED STATES OR COLORADO		22
15.2	SUBCONTRACTOR PREQUALIFICATION		23
15.3	SUBCONTRACTOR PROPOSALS		23
15.4	SUBCONTRACT FORMS		23
15.5	SUBCONTRACTOR SUBSTITUTION		23
15.6	CONSTRUCTION MANAGER RESPONSIBLE FOR SUBCONTRACTORS		23
16	ARTICLE 16	RELATIONS OF CONSTRUCTION MANAGER AND SUBCONTRACTOR	24
17	ARTICLE 17	MUTUAL RESPONSIBILITY OF CONTRACTORS	24
18	ARTICLE 18	SEPARATE CONTRACTS	25
19	ARTICLE 19	USE OF PREMISES	25
20	ARTICLE 20	CUTTING, FITTING OR PATCHING	25
21	ARTICLE 21	UTILITIES	25
21.1	TEMPORARY UTILITIES		25
21.2	PROTECTION OF EXISTING UTILITIES		26
21.3	CROSSING OF UTILITIES		26
22	ARTICLE 22	UNSUITABLE CONDITIONS	26
23	ARTICLE 23	TEMPORARY FACILITIES	26
23.1	OFFICE FACILITIES		26
23.2	TEMPORARY HEAT		26
23.3	WEATHER PROTECTION		27
23.4	DUST PARTITIONS		27
23.5	BENCH MARKS		27
23.6	SIGN		27
23.7	SANITARY PROVISION		27
24	ARTICLE 24	CLEANING UP	27
25	ARTICLE 25	INSURANCE	28
25.1	GENERAL		28
25.2	COMMERCIAL GENERAL LIABILITY INSURANCE (CGL)		28
25.3	AUTOMOBILE LIABILITY INSURANCE		29
25.4	WORKERS' COMPENSATION INSURANCE		29
25.5	UMBRELLA LIABILITY INSURANCE:		29
25.6	BUILDER'S RISK INSURANCE		30
25.7	POLLUTION LIABILITY INSURANCE		31
25.8	ADDITIONAL MISCELLANEOUS INSURANCE PROVISIONS		31
26	ARTICLE 26	CONSTRUCTION MANAGER'S PERFORMANCE AND PAYMENT BONDS	31
27	ARTICLE 27	LABOR AND WAGES	32
27.1	LABOR		32
27.2	COLORADO WAGES		32
28	ARTICLE 28	ROYALTIES AND PATENTS	33
29	ARTICLE 29	ASSIGNMENT	33
30	ARTICLE 30	CORRECTION OF WORK BEFORE ACCEPTANCE	34
31	ARTICLE 31	APPLICATIONS FOR PAYMENTS	35

31.1	CONSTRUCTION MANAGER'S SUBMITTALS.....	35
31.2	ARCHITECT/ENGINEER CERTIFICATION	36
31.3	RETAINAGE WITHHELD	36
31.4	RELEASE OF RETAINAGE	36
32	ARTICLE 32 CERTIFICATES FOR PAYMENTS.....	37
33	ARTICLE 33 PAYMENTS WITHHELD	38
34	ARTICLE 34 DEDUCTIONS FOR UNCORRECTED WORK	38
35	ARTICLE 35 CHANGES IN THE WORK	39
35.1	THE VALUE OF CHANGED WORK	39
35.2	DETAILED BREAKDOWN.....	40
35.3	HAZARDOUS MATERIALS	42
35.4	EMERGENCY FIELD CHANGE ORDERED WORK	42
35.5	APPROPRIATION LIMITATIONS - § 24-91-103.6, C.R.S. as amended	43
36	ARTICLE 36 CLAIMS	44
37	ARTICLE 37 DIFFERING SITE CONDITIONS.....	46
37.1	NOTICE IN WRITING.....	46
37.2	LIMITATIONS.....	47
38	ARTICLE 38 DELAYS AND EXTENSIONS OF TIME	47
39	ARTICLE 39 NON-BINDING DISPUTE RESOLUTION – FACILITATED NEGOTIATIONS.....	48
40	ARTICLE 40 RIGHT OF OCCUPANCY	50
41	ARTICLE 41 COMPLETION, FINAL INSPECTION, ACCEPTANCE AND SETTLEMENT.....	51
41.1	NOTICE OF COMPLETION.....	51
41.2	FINAL INSPECTION	51
41.3	NOTICE OF SUBSTANTIAL COMPLETION.....	51
41.4	NOTICE OF ACCEPTANCE	53
41.5	SETTLEMENT	53
42	ARTICLE 42 GENERAL WARRANTY AND CORRECTION OF WORK AFTER ACCEPTANCE	55
43	ARTICLE 43 LIENS.....	55
44	ARTICLE 44 ONE-YEAR GUARANTEE AND SPECIAL GUARANTEES AND WARRANTIES.....	55
44.1	ONE-YEAR GUARANTEE OF THE WORK	55
44.2	SPECIAL GUARANTEES AND WARRANTIES	56
45	ARTICLE 45 GUARANTEE INSPECTIONS AFTER COMPLETION	56
46	ARTICLE 46 TIME OF COMPLETION AND LIQUIDATED DAMAGES	57
47	ARTICLE 47 DAMAGES	59
48	ARTICLE 48 STATE'S RIGHT TO DO THE WORK; TEMPORARY SUSPENSION OF WORK; DELAY DAMAGES	
	60	
48.1	STATE'S RIGHT TO DO THE WORK	60
48.2	TEMPORARY SUSPENSION OF WORK	60
48.3	DELAY DAMAGES	61
49	ARTICLE 49 STATE'S RIGHTS TO TERMINATE CONTRACT	61
49.1	GENERAL	61
49.2	CONDITIONS AND PROCEDURES	61
49.3	ADDITIONAL CONDITIONS	62
50	ARTICLE 50 TERMINATION FOR CONVENIENCE OF STATE.....	63
50.1	NOTICE OF TERMINATION	63
50.2	PROCEDURES	63
51	ARTICLE 51 CONSTRUCTION MANAGER'S RIGHT TO STOP WORK AND/OR TERMINATE CONTRACT	64
52	ARTICLE 52 COLORADO SPECIAL PROVISIONS.....	65

52.1	CONTROLLER’S APPROVAL, C.R.S. § 24-30-202(1).....	65
52.2	FUND AVAILABILITY, C.R.S. § 24-30-202(5.5)	65
52.3	GOVERNMENTAL IMMUNITY	65
52.4	INDEPENDENT CONTRACTOR	65
52.5	COMPLIANCE WITH LAW	66
52.6	CHOICE OF LAW, JURISDICTION, AND VENUE	66
52.7	PROHIBITED TERMS	66
52.8	SOFTWARE PIRACY PROHIBITION. SOFTWARE PIRACY PROHIBITION.....	66
52.9	EMPLOYEE FINANCIAL INTEREST/CONFLICT OF INTEREST	66
52.10	VENDOR OFFSET AND ERRONEOUS PAYMENTS.....	66
53	ARTICLE 53 MISCELLANEOUS PROVISIONS.....	67
53.1	PROFESSIONAL ASSOCIATION PERMITTED.....	67
53.2	DISSOLUTION OF PROFESSIONAL ASSOCIATION	67
53.3	WAGE RATES, in accordance with C.R.S. § 24-30-1404 (1).....	67
53.4	PUBLIC ART LAW	67
53.5	ASSIGNMENT	67
53.6	SUBCONTRACTS	67
53.7	BINDING EFFECT	68
53.8	AUTHORITY	68
53.9	CAPTIONS AND REFERENCES	68
53.10	COUNTERPARTS	68
53.11	ENTIRE UNDERSTANDING.....	68
53.12	DIGITAL SIGNATURES.....	68
53.13	MODIFICATION	68
53.14	STATUTES, REGULATIONS, FISCAL RULES AND OTHER AUTHORITY	68
53.15	EXTERNAL TERMS AND CONDITIONS	68
53.16	SEVERABILITY	69
53.17	SURVIVAL AND CERTAIN CONTRACT TERMS	69
53.18	TAXES	69
53.19	THIRD PARTY BENEFICIARIES	69
53.20	WAIVER	69
53.21	CORA DISCLOSURE.....	69
53.22	STANDARD AND MANNER OF PERFORMANCE.....	69
53.23	LICENSES, PERMITS, AND OTHER AUTHORIZATIONS	69
53.24	INDEMNIFICATION	70
53.25	ACCESSIBILITY	70
54	ARTICLE 54 CONFIDENTIAL INFORMATION-STATE RECORDS	71
54.1	CONFIDENTIALITY	71
54.2	OTHER ENTITY ACCESS AND NONDISCLOSURE AGREEMENTS	71
54.3	USE, SECURITY, AND RETENTION.....	71
54.4	INCIDENT NOTICE AND REMEDIATION	72
54.5	DATA PROTECTION AND HANDLING	72
54.6	SAFEGUARDING PERSONAL IDENTIFIABLE INFORMATION (PII)	72

**STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM**

**THE GENERAL CONDITIONS OF THE CONSTRUCTION MANAGER/GENERAL CONTRACTOR (CM/GC)
AGREEMENT
(STATE FORM SC-6.51)**

1 ARTICLE 1 DEFINITIONS

1.1 CONTRACT DOCUMENTS

The Contract Documents consist of the following some of which are procedural documents used in the administration and performance of the Agreement:

- a) Construction Manager/General Contractor (CM/GC) Agreement; (SC-6.5.);
- b) Construction Manager's Fee Proposal, All Appendices, Addenda and Clarifications
- c) The Request for Proposals, All Appendices, Addenda and Clarifications;
- d) Performance Bond (SC-6.22) and Labor and Material Payment Bond (SC-6.221);
- e) These General Conditions of the Construction Manager/General Contractor (CM/GC) Agreement (SC- 6.5.1) and if applicable, Supplementary General Conditions;
- f) Drawings, including all addenda issued prior to the Notice to Proceed to Commence Construction Phase (SBP-8.261);
- g) Change Orders (SC-6.31) and Amendments (SC-6.0B), if any, when properly executed;
- h) Notice of Award (SBP-6.15);
- i) Builder's Risk insurance certificates of insurance (ACORD 25-S);
- j) Liability and Workers' compensation certificates of insurance;
- k) Notice to Proceed to Commence Construction Phase (SBP-6.261);
- l) Notice of Approval of Occupancy/Use (SBP-01);
- m) Notice of Partial Substantial Completion (SBP-071);
- n) Notice of Substantial Completion (SBP-07);
- o) Notice of Partial Final Acceptance (SC-6.27);
- p) Notice of Final Acceptance (SBP-6.271);
- q) Notice of Partial Contractor's Settlement (SC-7.3);
- r) Notice of Contractor's Settlement (SBP-7.31);
- s) Application and Certificate for Contractor's Payment (SBP-7.2);
- t) Other procedural and reporting documents or forms referred to in the General Conditions, the Supplementary General Conditions, and the Specifications or required by the State Buildings Program or the Principal Representative, including but not necessarily limited to Pre-Acceptance Check List (SBP-05) and the Building Inspection Record (SBP-BIR). A list of the current standard State Buildings Program forms applicable to this Contract may be obtained from the Principal Representative on request.

1.2 DEFINITIONS OF WORDS AND TERMS USED

Agreement

The term "Agreement" shall mean the written agreement entered into by the State of Colorado acting by and through the Principal Representative and the Contractor for the performance of the Work and payment therefore, on State Form SC-6.50. The term Agreement when used without reference to State Form SC-6.50 may also refer to the entirety of the parties' agreement to perform the Work described in the Contract Documents or reasonably inferable there from. The term "Contract" shall be interchangeable with this latter meaning of the term Agreement.

Amendment

The term "Amendment" shall be defined as provided in Section 3.8 of the Agreement, Amendments and Change Orders.

Architect/Engineer

The term "Architect/Engineer" shall mean either the architect of record or the engineer of record under contract to the State of Colorado for the Project identified in the Contract Documents.

Bid Package

Bid Package describes all documents that relate to a specific scope of work, including the drawings, specifications, documents, estimates, bid forms and bid bonds relevant to a discrete portion of or a complete construction Project.

Change Order

The term "Change Order" means a written order directing the Construction Manager to make changes in the Work, in accordance with Section 35.1 of these General Conditions, The Value of Changed Work, and Section 3.8 of the Agreement (SC-6.5), Amendments and Change Orders.

Colorado Labor

The term "Colorado labor", as provided in § 8-17-101(2) (a), C.R.S. as amended, means any person who is a resident of the state of Colorado, at the time of the public Works project, without discrimination as to race, color, creed, sex, sexual orientation, marital status, national origin, ancestry, age, or religion except when sex or age is a bona fide occupational qualification. A resident of the state of Colorado is a person who can provide a valid Colorado driver's license, a valid Colorado state-issued photo identification, or documentation that he or she has resided in Colorado for the last thirty days.

Construction Manager/General Contractor

The term "Construction Manager / General Contractor" shall mean the person, company, firm, corporation or other legal entity entering into a contract with the State of Colorado acting by and through the Principal Representative. The Construction Manager/General Contractor may also be referred to as the "Construction Manager" or "Contractor" in the Agreement SC 6.5), these General Conditions, or in related exhibits, attachments, contract modification or procedural documents.

Construction Manager/General Contractor's Scope Narrative

The Construction Manager's "Scope Narrative" shall be defined as the bilateral agreement concerning final scope, which is developed cumulatively and simultaneously with each of the Bid Packages and is agreed upon during review of the final scope as it pertains to each Bid Package.

Consultant

The term “Consultant” shall mean a person, firm or corporation supplying design/consulting services for the Project. Design professionals and consultants are directly contracted to the Architect/Engineer or the Principal Representative.

Contract Time

The “Contract Time” shall commence as set forth in paragraph 4.1.1 of the Agreement (SC 6.5) and shall end on the date that the Project is finally complete.

CORA

The term “CORA” shall mean the Colorado Open Records Act, §§24-72-200.1, *et seq.*, C.R.S.

Days

The term “days” whether singular or plural shall mean calendar days unless expressly stated otherwise. Where the term “business days” is used it shall mean business days of the State of Colorado.

Direct Cost of Work

The term “Direct Cost of Work” shall mean those costs directly linked to the physical construction of the project including material, labor and equipment and Subcontractor costs and as further defined in Designated Services and Method of Payment, Exhibit A.

Drawings

The term “Drawings” shall mean all drawings approved by appropriate State officials which have been prepared by the Architect/Engineer showing the Work to be done, except that where a list of drawings is specifically enumerated in the Supplementary General Conditions or Division 1 of the Specifications, the term shall mean the drawings so enumerated, including all addenda drawings.

Emergency Field Change Order

The term “Emergency Field Change Order” shall mean a written change order for extra Work or a change in the Work necessitated by an emergency as defined in Section 35.4 of these General Conditions executed on State form SC 6.31 and identified as an Emergency Field Change Order. The use of such orders is limited to emergencies and to the amounts shown in Section 35.4.

Fast Track Construction

The term “Fast Track Construction” is a methodology where portions of the Work could have their design completed as separate Construction Phase(s) and may be under construction before other portions of the Work are fully designed.

Final Acceptance

The terms “final acceptance” or “finally complete” mean the stage in the progress of the Work, after substantial completion, when all remaining items of Work have been completed, all requirements of the Contract Documents are satisfied and the Notice of Acceptance can be issued. Discrete physical portions of the Project may be separately and partially deemed finally complete at the discretion of the Principal Representative when that portion of the Project reaches such stage of completion and a partial Notice of Acceptance can be issued.

Fixed Limit of Construction Cost

The term “Fixed Limit of Construction Cost” shall set forth a dollar amount available for the total Construction Cost of all elements of the Work as specified by the Principal Representative.

Guaranteed Maximum Price

The term "Guaranteed Maximum Price" shall mean the maximum amount for which the Work shall be accomplished and it shall be computed by the Construction Manager in accordance with the provisions of Section 5.4 of the Agreement and as approved by the Principal Representative.

Incident

The term "Incident" shall mean any accidental or deliberate event that results in or constitutes an imminent threat of the unauthorized access, loss, disclosure, modification, disruption, or destruction of any communications or information resources of the State, which are included as part of the Work, as described in §§24-37.5-401, *et seq.*, C.R.S. Incidents include, without limitation: (i) successful attempts to gain unauthorized access to a State system or State Records regardless of where such information is located; (ii) unwanted disruption or denial of service; (iii) the unauthorized use of a State system for the processing or storage of data; or (iv) changes to State system hardware, firmware, or software characteristics without the State's knowledge, instruction, or consent.

Notice

The term "Notice" shall mean any communication in writing from either contracting party to the other by such means of delivery that receipt cannot properly be denied. Notice shall be provided to the person identified to receive it in Article 8 of the Agreement. (SC 6.5), Notice Identification, or to such other person as either party identifies in writing to receive Notice. Notice by facsimile transmission where proper transmission is evidence shall be adequate where facsimile numbers are included in Article 8 of the Agreement, or to such other person as either party identifies in writing to receive Notice or in the absence of the identified party, a principal of the Construction Manager. Notice by facsimile transmission where proper transmission is evidenced shall be adequate where facsimile numbers are included in Article 8 of the Agreement. Notwithstanding an email delivery or return receipt, email Notice shall not be adequate. Acknowledgment of receipt of a voice message shall not be deemed to waive the requirement that Notice, where required, shall be in writing.

Occupancy

The term "Occupancy" means occupancy taken by the State as Owner after the Date of Substantial Completion at a time when a building or other discrete physical portion of the Project is used for the purpose intended. The Date of Occupancy shall be the date of such first use, but shall not be prior to the date of execution of the Notice of Approval of Occupancy/Use. Prior to the date of execution of a Notice of Approval of Occupancy/Use, the state shall have no right to occupy and the project may not be considered safe for occupancy for the intended use.

Owner

The term "Owner" shall mean the Principal Representative.

PHI

The term "PII" shall mean personally identifiable information including, without limitation, any information maintained by the State about an individual that can be used to distinguish or trace an individual's identity, such as name, social security number, date and place of birth, mother's maiden name, or biometric records; and any other information that is linked or linkable to an individual, such as medical, educational, financial, and employment information. PII includes, but is not limited to, all information defined as personally identifiable information in §§24-72-501 and 24-73-101, C.R.S. "PII" shall also mean "personal identifying information" as set forth at § 24-74-102, *et. seq.*, C.R.S.

PCI

The term “PCI” means payment card information including any data related to credit card holders’ names, credit card numbers, or other credit card information as may be protected by state or federal law.

PII

The term “PII” shall be defined as personally identifiable information including, without limitation, any information maintained by the State about an individual that can be used to distinguish or trace an individual’s identity, such as name, social security number, date and place of birth, mother’s maiden name, or biometric records; and any other information that is linked or linkable to an individual, such as medical, educational, financial, and employment information. PII includes, but is not limited to, all information defined as personally identifiable information in §§24-72-501 and 24-73-101, C.R.S. “PII” shall also mean “personal identifying information” as set forth at § 24-74-102, et. seq., C.R.S.

Preconstruction

The term “Preconstruction” shall mean the Work done by the Construction Manager in the management and definition of the project prior to the awarding of construction contracts for any bid package.

Principal Representative

The term “Principal Representative” shall be defined, as provided in § 24-30-1301(14), C.R.S. as the governing board of a state department, institution, or agency; or if there is no governing board, then the executive head of a state department, institution, or agency, as designated by the governor or the general assembly and as specifically identified in the Contract Documents, or shall have such other meaning as the term may otherwise be given in § 24-30-1301(14), C.R.S. as amended. The Principal Representative may delegate authority. The Construction Manager shall have the right to inquire regarding the delegated authority of any of the Principal Representative’s representatives on the project and shall be provided with a response in writing when requested.

Product Data

The term “Product Data” shall mean all submittals in the form of printed manufacturer’s literature, manufacturer’s specifications, and catalog cuts.

Project

The “Project” is the total construction of which the Work performed under the Contract Documents is a part, and may include construction by the Principal Representative or by separate contractors.

Punch List

The term “Punch List” shall mean the list of all final work items remaining to fulfill the requirements of the Contract Documents as defined in this Article.

Reasonably Inferable

The phrase “reasonably inferable” means that if an item or system is either shown or specified, all material and equipment normally furnished with such items or systems and needed to make a complete installation shall be provided whether mentioned or not, omitting only such parts as are specifically excepted, and shall include only components which the Construction Manager could reasonably anticipate based on their skill and knowledge using an objective, industry standard, not a subjective standard. This term takes into consideration the normal understanding that not every detail is to be given on the Drawings and Specifications. If there is a difference of opinion, the Principal Representative shall make the determination as to the standards of what is reasonably inferable.

Samples

The term "Samples" shall mean examples of materials or Work provided to establish the standard by which the Work will be judged.

SBP

The term "SBP" means "State Buildings", which is used in connection with labeling applicable State form documents (e.g., "SBP-01" is the form number for Notice of Approval of Occupancy/Use).

SC

The term "SC" means "State Contract" which is used in connection with labeling applicable State form documents (e.g. "SC 6.51" is the State form number for these General Conditions of the Construction Manager/General Contractor's (CM/GC) Agreement).

Schedule of Values

The term "Schedule of Values" is defined as the itemized listing of description of the Work by Construction Specification Institute Division and Section of the Specifications. The format shall be similar to the Application and Certificate for Contractor's Payment (SC-7.2). Included shall be the material costs, and the labor and other costs plus the sum of both.

Shop Drawings

The term "Shop Drawings" shall mean any and all detailed drawings prepared and submitted by Construction Manager, Subcontractor at any tier, vendors or manufacturers providing the products and equipment specified on the Drawings or called for in the Specifications.

Specifications

The term "Specifications" shall mean the requirements of the CSI divisions of the project manual prepared by the Architect/Engineer describing the Work to be accomplished.

State Buildings Program

The term "State Buildings Program" shall refer to the Office of the State Architect within the Department of Personnel & Administration of Colorado State government responsible for project administration, review, approval and coordination of plans, construction procurement policy, contractual procedures, and code compliance and inspection of all buildings, public Works and improvements erected for state purposes; except public roads and highways and projects under the supervision of the division of wildlife and the division of parks and outdoor recreation as provided in C.R.S. § 24-30-1301, *et seq.* The term State Buildings Program shall also mean that individual within a State Department agency or institution, including institutions of higher education, who has signed an agreement accepting delegation to perform all or part of the responsibilities and functions of State Buildings Program.

State Confidential Information

The term "State Confidential Information" shall mean any and all State Records not subject to disclosure under CORA. State Confidential Information shall include, but is not limited to, Personal Identifiable Information, and State personnel records not subject to disclosure under CORA. State Confidential Information shall not include information or data concerning individuals that is not deemed confidential but nevertheless belongs to the State, which has been communicated, furnished, or disclosed by the State to Contractor which (i) is subject to disclosure pursuant to CORA; (ii) is already known to Contractor without restrictions at the time of its disclosure to Contractor; (iii) is or subsequently becomes publicly available without breach of any obligation owed by Contractor to the State; (iv) is disclosed to Contractor, without confidentiality obligations, by a third party who has the right to disclose such information; or (v) was independently developed without reliance on any State Confidential Information.

State Fiscal Rules

"State Fiscal Rules" shall mean the fiscal rules promulgated by the Colorado State Controller pursuant to §24-30-202(13)(a), C.R.S. or where applicable, the Fiscal Rules of the contracting institution of higher education.

State Records

The term "State Records" shall mean any and all State data, information, and records, regardless of physical form, including, but not limited to, information subject to disclosure under CORA.

Subconsultant

The term "Subconsultant" shall mean a person, firm or corporation supplying design/consulting services for the Project. Design and other professionals directly contracted to the Architect/Engineers are considered Subconsultants.

Subcontractor

The term "Subcontractor" shall mean a person, firm or corporation supplying labor, materials, equipment and/or Services for Work at the site of the Project for, and under separate contract or agreement with the Construction Manager.

Submittals

The term "submittals" means drawings, lists, tables, documents and samples prepared by the Construction Manager to facilitate the progress of the Work as required by these General Conditions or the Drawings and Specifications. They consist of Shop Drawings, Product Data, Samples, and various administrative support documents including but not limited to lists of subcontractors, construction progress schedules, schedules of values, applications for payment, inspection and test results, requests for information, various document logs, and as-built drawings. Submittals are *required* by the Contract Documents, but except to the extent expressly specified otherwise are not themselves a part of the Contract Documents.

Substantial Completion

The terms "substantial completion" or "substantially complete" mean the stage in the progress of the Work when the construction is sufficiently complete, in accordance with the Contract Documents as modified by any Change Orders, so that the Work, or at the discretion of the Principal Representative, any designated portion thereof, is available for its intended use by the Principal Representative and a Notice of Substantial Completion can be issued. Portions of the Project may, at the discretion of the Principal Representative, be designated as substantially complete.

Supplier

The term "Supplier" shall mean any manufacturer, fabricator, distributor, material man or vendor.

Surety

The term "Surety" shall mean the company providing the labor and material payment and performance bonds for the Construction Manager as obligor.

Value Engineering

"Value Engineering" or "VE" is defined as an analysis and comparison of cost versus value of building materials, equipment, and systems. VE considers the initial cost of construction, coupled with the estimated cost of maintenance, energy use, life expectancy and replacement cost. VE related to this Project shall include the analysis and comparison of building elements in an effort to reduce overall Project costs, while maintaining or enhancing the quality of the design intent, whenever possible.

Work

The term "Work" shall mean all or part of the labor, materials, equipment, and other services required by the Contract Documents or otherwise required to be provided by the Construction Manager to meet the Construction Manager's obligations under the Contract.

Work Product

The term "Work Product" shall mean the tangible and intangible results of the Work, whether finished or unfinished, including drafts. Work Product includes, but is not limited to, documents, text, software (including source code), research, reports, proposals, specifications, plans, notes, studies, data, images, photographs, negatives, pictures, drawings, designs, models, surveys, maps, materials, ideas, concepts, know-how, and any other results of the Work. "Work Product" does not include any material that was developed prior to the Effective Date that is used, without modification, in the performance of the Work.

2 ARTICLE 2 EXECUTION, CORRELATION, INTENT OF DOCUMENTS, COMMUNICATION AND COOPERATION

2.1 EXECUTION

The Construction Manager, within ten (10) days from the date of Notice of Award, will be required to:

- a) Execute the Agreement, State Form SC-6.5.
- b) Furnish fully executed Performance and Labor and Material Payment Bonds on State Forms SC-6.22 and SC-6.221; and
- c) Furnish certificates of insurance evidencing all required insurance on standard Acord forms designed for such purpose.
- d) Furnish certified copies of any insurance policies requested by the Principal Representative.
- e) If Section 7.1 of the Agreement (SC-6.5) applies, Modification of Article 2, furnish documentation that identifies the Subcontractors that will be used for all mechanical, sheet metal, fire suppression, sprinkler fitting, electrical, and plumbing work required on the project and certify that that all firms identified participate in apprenticeship programs registered with the United States Department of Labor's Employment and Training Administration or state apprenticeship councils recognized by the United States Department of Labor and have a proven record of graduating a minimum of fifteen percent of its apprentices for at least three of the past five years.

2.2 CORRELATION

By execution of the Agreement the Construction Manager represents that the Construction Manager has visited the site, has become familiar with local conditions and local requirements under which the Work is to be performed, including the building code programs of the State Buildings Program as implemented by the Principal Representative, and has correlated personal observations with the requirements of the Contract Documents.

2.3 INTENT OF DOCUMENTS

The Contract Documents are complementary, and what is called for by any one document shall be as binding as if called for by all. The intention of the documents is to include all labor, materials, equipment and transportation necessary for the proper execution of the Work. Words describing

materials or Work which have a well-known technical or trade meaning shall be held to refer to such recognized standards.

In any event, if any error exists, or appears to exist, in the requirements of the Drawings or Specifications, or if any disagreement exists as to such requirements, the Construction Manager shall submit a request for information to the Architect/Engineer before proceeding with the Work in question. In the event of the Construction Manager's failure to give prior written Notice of any such errors or disagreements of which the Construction Manager or the Subcontractors at any tier are aware, the Construction Manager shall, at no additional cost to the Principal Representative, make good any damage to, or defect in, Work which is caused by such omission.

Where a conflict occurs between or within standards, Specifications or Drawings, which is not resolved by reference to the precedence between the Contract Documents, the more stringent or higher quality requirements shall apply so long as such more stringent or higher quality requirements are reasonably inferable. The Principal Representative, or the Architect/Engineer with consent of the Principal Representative, shall decide which requirements will provide the best installation.

With the exception noted in the following paragraph, the precedence of the Contract Documents is in the following sequence:

- a) The Supplementary General Conditions, if any;
- b) The Minimum Requirements of the Request for Proposals;
- c) The Construction Manager's Fee Proposals;
- d) The Agreement (SC-6.5);
- e) These General Conditions (SC-6.51);
- f) Drawings and Specifications, all as modified by any addenda; and
- g) Any additional Exhibit to this agreement.

Change Orders and Amendments, if any, to the Contract Documents take precedence over the original Contract Documents.

Notwithstanding the foregoing order of precedence, the Colorado Special Provisions of Article 52 of these General Conditions, shall take precedence, rule and control over all other provisions of the Contract Documents.

Unless the context otherwise requires, form numbers in this document are for convenience only. In the event of any conflict between the form required by name or context and the form required by number, the form required by name or context shall control. The Construction Manager may obtain State forms from the Principal Representative upon request.

2.4 PARTNERING, COMMUNICATIONS AND COOPERATION

In recognition of the fact that conflicts, disagreements and disputes often arise during the performance of construction contracts, the Construction Manager and the Principal Representative aspire to encourage a relationship of open communication and cooperation between the employees and personnel of both, in which the objectives of the Contract may be better achieved and issues resolved in a more fully informed atmosphere.

The Construction Manager and the Principal Representative each agree to assign an individual who shall be fully authorized to negotiate and implement a voluntary partnering plan for the purpose of facilitating open communications between them. Within thirty days (30) of the Notice to Proceed, the assigned individuals shall meet to discuss development of an informal agreement to accomplish these goals.

The assigned individuals shall endeavor to reach an informal agreement, but shall have no such obligation. Any plans these parties voluntarily agree to implement shall result in no change to the contract amount, and no costs associated with such plan or its development shall be recoverable under any contract clause. In addition, no plan developed to facilitate open communication and cooperation shall alter, amend or waive any of the rights or duties of either party under the Contract unless and except by written Amendment to the Contract, nor shall anything in this clause or any subsequently developed partnering plan be deemed to create fiduciary duties between the parties unless expressly agreed in a written Amendment to the Contract. It is also recognized that projects with relatively low contract values may not justify the expense or special efforts required. In the case of small projects with an initial Contract value under \$500,000, the requirements of the preceding paragraph shall not apply.

3 ARTICLE 3 COPIES FURNISHED

The Construction Manager will be furnished, free of charge, the number of copies of Drawings and Specifications as specified in the Contract Documents, or if no number is specified, all copies reasonably necessary for the execution of the Work.

4 ARTICLE 4 OWNERSHIP OF DRAWINGS

Drawings or Specifications, or copies of either, furnished by the Architect/Engineer, are not to be used on any other Work. At the completion of the Work, at the written request of the Architect/Engineer, the Construction Manager shall endeavor to return all Drawings and Specifications.

The Construction Manager may retain the Construction Manager's Contract Document set, copies of Drawings and Specifications used to contract with others for any portion of the Work, and a marked up set of as-built drawings.

5 ARTICLE 5 ARCHITECT/ENGINEER'S STATUS

The Architect/Engineer is the representative of the Principal Representative for purposes of administration of the Contract, as provided in the Contract Documents and the Agreement. In case of termination of employment or the death of the Architect/Engineer, the Principal Representative will appoint a capable Architect/Engineer against whom the Construction Manager makes no reasonable objection, whose status under the Contract shall be the same as that of the former Architect/Engineer.

6 ARTICLE 6 ARCHITECT/ENGINEER DECISIONS AND JUDGMENTS, ACCESS TO WORK AND INSPECTION

6.1 DECISIONS

The Architect/Engineer shall, within a reasonable time, make decisions on all matters relating to the execution and progress of the Work or the interpretation of the Contract Documents, and in the exercise of due diligence shall be reasonably available to the Construction Manager to timely interpret and make decisions with respect to questions relating to the design or concerning the Contract Documents.

6.2 JUDGMENTS

The Architect/Engineer is, in the first instance, the judge of the performance required by the Contract Documents as it relates to compliance with the Drawings and Specifications and quality of Workmanship and materials.

The Architect/Engineer shall make judgments regarding whether directed Work is extra or outside the scope of Work required by the Contract Documents at the time such direction is first given. If, in the Construction Manager's judgment, any performance directed by the Architect/Engineer is not required by the Contract Documents or if the Architect/Engineer does not make the judgment required, it shall be a condition precedent to the filing of any claim for additional cost related to such directed Work that the Construction Manager, before performing such Work, shall first obtain in writing, the Architect/Engineer's written decision that such directed Work is included in the performance required by the Contract Documents. If the Architect/Engineer's direction to perform the Work does not state that the Work is within the performance required by the Contract Documents, the Construction Manager shall, in writing, request the Architect/Engineer to advise in writing whether the directed Work will be considered extra Work or Work included in the performance required by the Contract Documents.

The Architect/Engineer shall respond to any such written request for such a decision within three (3) business days and if no response is provided, or if the Architect/Engineer's written decision is to the effect that the Work is included in the performance required by the Contract Documents, the Construction Manager may file with the Principal Representative and the Architect/Engineer a Notice of claim in accordance with Article 36, Claims. Whether or not a Notice of claim is filed, the Construction Manager shall proceed with the ordered Work. Disagreement with the decision of the Architect/Engineer shall not be grounds for the Construction Manager to refuse to perform the Work directed or to suspend or terminate performance.

6.3 ACCESS TO WORK

The Architect/Engineer, the Principal Representative and representatives of State Buildings Program shall at all times have access to the Work. The Construction Manager shall provide proper facilities for such access and for their observations or inspection of the Work.

6.4 INSPECTION

The Architect/Engineer has agreed to make, or that structural, mechanical, electrical engineers or other consultants will make, periodic visits to the site to generally observe the progress and quality of the Work to determine in general if the Work is proceeding in accordance with the Contract Documents. Observation may extend to all or any part of the Work and to the preparation, fabrication or manufacture of materials.

Without in any way meaning to be exclusive or to limit the responsibilities of the Architect/Engineer or the Construction Manager, the Architect/Engineer has agreed to observe, among other aspects of the Work, the following for compliance with the Contract Documents:

- a) Compaction testing reports based upon the findings and recommendations of the Principal Representative's testing consultant;
- b) Bearing surfaces of excavations before concrete is placed based upon the findings and recommendations of the Principal Representative's soils engineering consultant;
- c) Reinforcing steel after installation and before concrete is poured;
- d) Structural concrete;
- e) Laboratory reports on all concrete testing based upon the findings and recommendations of the Principal Representative's testing consultant;
- f) Structural steel during and after erection and prior to its being covered or enclosed;
- g) Steel welding; Principal Representative will furnish steel welding inspection consultant/agency if required or necessary for the project;
- h) Mechanical and plumbing Work following its installation and prior to its being covered or enclosed;
- i) Electrical Work following its installation and prior to its being covered or enclosed; and
- j) Any special or quality control testing required in the Contract Documents provided by the Principal Representative's testing consultant.

If the Specifications, the Architect/Engineer's instructions, laws, ordinances of any public authority require any Work to be specifically tested or approved, the Construction Manager shall give the Principal Representative, Architect/Engineer and appropriate testing agency (if necessary) timely notice of its readiness for observation by the Architect/Engineer or inspection by another authority, and if the inspection is by another authority, of the date fixed for such inspection, required certificates of inspection being secured by the Construction Manager. The Construction Manager shall give all required Notices to the Principal Representative or their designee for inspections required for the building inspection program. It shall be the responsibility of the Construction Manager to determine the Notice required by the State pursuant to Building Inspection Record for the Project, according to State form SBP-B.I.R., or the equivalent form required by the Principal Representative as approved by the State Buildings Program. If any portion of the Work should be covered contrary to the reasonable request of the Architect/Engineer, or to requirements specifically expressed in the Contract Documents, it must, if required in writing by the Architect/Engineer, be uncovered for its observation and shall be replaced at the Construction Manager's expense.

If any other portion of the Work has been covered which the Architect/Engineer has not specifically requested to observe prior to its being covered, it may request to see such work and it shall be uncovered by the Construction Manager. If such work is found in accordance with the Contract Documents, the cost of uncovering and replacement shall, by appropriate Amendment or Change Order, be charged to the Principal Representative. If such work is found not in accordance with the Contract Documents, the Construction Manager shall pay such costs unless it is found that this condition was caused by the Principal Representative or a separate construction manager as provided in Article 18 of these General Conditions, in which event, the Principal Representative shall be responsible for the payment of such costs.

7 ARTICLE 7 CONSTRUCTION MANAGER'S SUPERINTENDENCE AND SUPERVISION

The Construction Manager shall employ, and keep present (as applicable) on the Project during its progress, a competent project manager as satisfactory to the Principal Representative. The project manager shall not be changed except with the consent of the Principal Representative, unless the project manager proves to be unsatisfactory to the Construction Manager and ceases to be in their employ. The project manager shall represent the Construction Manager for the Project, and in the absence of the Construction Manager, all directions given to the project manager shall be as binding as if given to the Construction Manager. Directions received by the project manager shall be documented by the project manager and communicated in writing with the Construction Manager.

The Construction Manager shall employ, and keep present on the Project during its progress, a competent superintendent and any necessary assistants, all satisfactory to the Architect/Engineer and the Principal Representative. The superintendent shall not be changed except with the consent of the Architect/Engineer and the Principal Representative, unless the superintendent proves to be unsatisfactory to the Project Manager/Construction Manager and ceases to be in their employ. The superintendent shall represent the Project Manager/Construction Manager in their absence and all directions given to the superintendent shall be as binding as if given to the Project Manager/Construction Manager. Directions received by the superintendent shall be documented by the superintendent and confirmed in writing with the Project Manager/Construction Manager.

The Construction Manager shall give efficient supervision to the Work, using their best skill and attention. He or she shall carefully study and compare all Drawings, Specifications and other written instructions and shall without delay report any error, inconsistency or omission which he or she may discover in writing to the Architect/Engineer. The Construction Manager shall not be liable to the Principal Representative for damage to the extent it results from errors or deficiencies in the Contract Documents or other instructions by the Architect/Engineer, unless the Construction Manager knew or had reason to know, that damage would result by proceeding and the Construction Manager fails to so advise the Architect/Engineer.

The superintendent shall see that the Work is carried out in accordance with the Contract Documents and in a uniform, thorough and first-class manner in every respect. The Construction Manager's superintendent shall establish all lines, levels, and marks necessary to facilitate the operations of all concerned in the Construction Manager's Work. The Construction Manager shall lay out all Work in a manner satisfactory to the Architect/Engineer, making permanent records of all lines and levels required for excavation, grading, foundations, and for all other parts of the Work.

8 ARTICLE 8 MATERIALS AND EMPLOYEES

Unless otherwise stipulated, the Construction Manager shall provide and pay for all materials, labor, water, tools, equipment, light, power, transportation and other facilities necessary for the execution and completion of the Work.

Unless otherwise specified, all materials shall be new and both workmanship and materials shall be first class and of uniform quality. The Construction Manager shall, if required, furnish satisfactory evidence as to the kind and quality of materials.

The Construction Manager is fully responsible for all acts and omissions of the Construction Manager's employees and shall at all times enforce strict discipline and good order among employees on the site. The Construction Manager shall not employ on the Work any person reasonably deemed unfit by the Principal Representative or anyone not skilled in the Work assigned to him.

9 ARTICLE 9 SURVEYS, PERMITS, LAWS, TAXES AND REGULATIONS

9.1 SURVEYS

The Principal Representative shall furnish all surveys, property lines and bench marks deemed necessary by the Architect/Engineer, unless otherwise specified.

9.2 PERMITS AND LICENSES

Permits and licenses necessary for the prosecution of the Work shall be secured and paid for by the Construction Manager. Unless otherwise specified in the Specifications, no local municipal or county building permit shall be required. However, State Buildings Program requires each Principal Representative to administer a building code inspection program, the implementation of which may vary at each agency or institution of the State. The Construction Managers' employees shall become personally familiar with these local conditions and requirements and shall fully comply with such requirements. State electrical and plumbing permits are required, unless the requirement to obtain such permits is altered by State Buildings Program. The Construction Manager shall obtain and pay for such permits.

Easements for permanent structures or permanent changes in existing facilities shall be secured and paid for by the Principal Representative, unless otherwise specified.

9.3 TAXES

9.3.1 Refund of Sales and Use Taxes

The Construction Manager shall pay all local taxes required to be paid, including but not necessarily limited to all sales and use taxes. If requested by the Principal Representative prior to issuance of the Notice to Proceed or directed in the Supplementary General Conditions or the Specifications, the Construction Manager shall maintain records of such payments in respect to the Work, which shall be separate and distinct from all other records maintained by the Construction Manager, and the Construction Manager shall furnish such data as may be necessary to enable the State of Colorado, acting by and through the Principal Representative, to obtain any refunds of such taxes which may be available under the laws, ordinances, rules or regulations applicable to such taxes. When so requested or directed, the Construction Manager shall require Subcontractors at all tiers to pay all local sales and use taxes required to be paid and to maintain records and furnish the Construction Manager with such data as may be necessary to obtain refunds of the taxes paid by such Subcontractors. No State sales and use taxes are to be paid on material to be used in this Project. On application by the purchaser or seller, the Department of Revenue shall issue to a Construction Manager or to a Subcontractor at any tier, a certificate or certificates of exemption per § 39-26-703(2)(b), C.R.S. and § 39-26-708 C.R.S.

9.3.2 Federal Taxes

The Construction Manager shall exclude the amount of any applicable federal excise or manufacturers' taxes from the proposal. The Principal Representative will furnish the Construction Manager, on request exemption certificates.

9.4 LAWS AND REGULATIONS

The Construction Manager shall give all notices and comply with all laws, ordinances, rules and regulations bearing on the conduct of the Work as drawn or specified. If the Construction Manager observes that the Drawings or Specifications require Work which is at variance therewith, the Construction Manager shall without delay notify the Architect/Engineer in writing and any necessary changes shall be adjusted as provided in Article 35, Changes in the Work of these General Conditions.

The Construction Manager shall bear all costs arising from the performance of Work required by the Drawings or Specifications that the Construction Manager knows to be contrary to such laws, ordinances, rules or regulations, if such Work is performed without giving Notice to the Architect/Engineer.

10 ARTICLE 10 PROTECTION OF WORK AND PROPERTY

10.1 GENERAL PROVISIONS

The Construction Manager shall continuously maintain adequate protection of all Work and materials, protect the property from injury or loss arising in connection with this Contract and adequately protect adjacent property as provided by law and the Contract Documents. The Construction Manager shall make good any damage, injury or loss, except to the extent:

- a) Directly due to errors in the Contract Documents;
- b) Caused by agents or employees of the Principal Representative; and,
- c) Due to causes beyond the Construction Manager's control and not to fault or negligence; provided such damage, injury or loss would not be covered by the insurance required to be carried by the Construction Manager.

10.2 SAFETY PRECAUTIONS

The Construction Manager shall take all necessary precautions for the safety of employees on the Project, and shall comply with all applicable provisions of federal, State and municipal safety laws and building codes to prevent accidents or injury to persons on, about or adjacent to the premises where the Work is being performed. The Construction Manager shall erect and properly maintain at all times, as required by the conditions and progress of the Work, all necessary safeguards for the protection of workers and the public and shall post danger signs warning against the hazards created by such features of construction as protruding nails, hoists, well holes, elevator hatchways, scaffolding, window openings, stairways and falling materials; and the Construction Manager shall designate a responsible member of its organization on the Project, whose duty shall be the prevention of accidents. The name and position of such person so designated shall be reported to the Architect/Engineer by the Construction Manager.

The Construction Manager shall provide all necessary bracing, shoring and tying of all structures, decks and framing to prevent any structural failure of any material which could result in damage

to property or the injury or death of persons; take all precautions to insure that no part of any structure of any description is loaded beyond its carrying capacity with anything that will endanger its safety at any time during the execution of this Contract; and provide for the adequacy and safety of all scaffolding and hoisting equipment. The Construction Manager shall not permit open fires within the building enclosure. The Construction Manager shall construct and maintain all necessary temporary drainage and do all pumping necessary to keep excavations and floors, pits and trenches free of water. The Construction Manager shall be solely responsible for all construction means, methods, techniques, sequences and procedures, and for coordinating all portions of the Work, except as otherwise noted.

The Construction Manager shall take due precautions when obstructing sidewalks, streets or other public ways in any manner, and shall provide, erect and maintain barricades, temporary walkways, roadways, trench covers, colored lights or danger signals and any other devices necessary or required to assure the safe passage of pedestrians and automobiles.

10.3 EMERGENCIES

In an emergency affecting the safety of life or of the Work or of adjoining property, the Construction Manager without special instruction or authorization from the Architect/Engineer or Principal Representative, is hereby permitted to act, at Construction Manager' discretion, to prevent such threatened loss or injury; and they shall so act, without appeal, if so authorized or instructed. Provided the Construction Manager has no responsibilities for the emergency, if the Construction Manager incurs additional cost not otherwise recoverable from insurance or others on account of any such emergency Work, the Contract sum shall be equitably adjusted in accordance with Article 35 of these General Conditions, Changes in the Work.

11 ARTICLE 11 DRAWINGS AND SPECIFICATIONS ON THE WORK

The Construction Manager shall keep on the job site one copy of the Contract Documents in good order, including current copies of all Drawings and Specifications for the Work, and any approved Shop Drawings, Product Data or Samples, and as-built drawings. As-built drawings shall be updated weekly by the Construction Manager and Subcontractors to reflect actual constructed conditions including dimensioned locations of underground Work and the Construction Manager's failure to maintain such updates may be grounds to withhold portions of payments otherwise due in accordance with Article 33, of these General Conditions, Payments Withheld. All such documents shall be available to the Architect/Engineer and representatives of the State. In addition, the Construction Manager shall keep on the job site one copy of all approved addenda, Change Orders and requests for information issued for the Work.

The Construction Manager shall develop procedures to insure the currency and accuracy of as-built drawings and shall maintain on a current basis a log of requests for information and responses thereto, a Shop Drawing and Product Data submittal log, and a Sample submittal log to record the status of all necessary and required submittals.

12 ARTICLE 12 REQUESTS FOR INFORMATION AND SCHEDULES

12.1 DETAIL DRAWINGS AND INSTRUCTIONS

The Architect/Engineer shall furnish additional instructions with reasonable promptness, by means of drawings or otherwise, necessary for the proper execution of the Work. All such drawings and instructions shall be consistent with the Contract Documents and reasonably inferable therefrom. The Architect/Engineer shall determine what additional instructions or drawings are necessary for the proper execution of the Work.

The Work shall be executed in conformity with such instructions and the Construction Manager shall do no Work without proper drawings, specifications or instructions. If the Construction Manager believes additional instructions, specifications or drawings are needed for the performance of any portion of the Work, the Construction Manager shall give Notice of such need in writing through a request for information furnished to the Architect/Engineer sufficiently in advance of the need for such additional instructions, specifications or drawings to avoid delay and to allow the Architect/Engineer a reasonable time to respond. The Construction Manager shall maintain a log of the requests for information and the responses provided.

The Construction Manager, the Architect/Engineer, and the Principal Representative shall jointly prepare a schedule, subject to change from time to time in accordance with the progress of the Work, fixing the dates at which the various detail drawings will be required, and the Architect/Engineer shall furnish them in accordance with that schedule. Under like conditions, a schedule shall be prepared, fixing the dates for the submission of shop drawings, for the beginning of manufacture and installation of materials and for the completion of the various parts of the Work.

The Principal Representative may consent with such instructions by the Architect/Engineer or amend/revise such instructions at the discretion of the Principal Representative.

12.2 SCHEDULES

12.2.1 Submittal Schedules

Prior to the Notice to Proceed to Commence Construction for the first construction phase, a schedule shall be prepared which may be preliminary to the extent required, fixing the dates for the submission and initial review of required Shop Drawings, Product Data and Samples for the beginning of manufacture and installation of materials, and for the completion of the various parts of the Work. It shall be prepared so as to cause no delay in the Work or in the Work of any other contractor engaged by the Principal Representative. The schedule shall be subject to change from time to time in accordance with the progress of the Work, and it shall be subject to the review and approval by the Architect/Engineer. It shall fix the dates at which the various Shop Drawings Product Data and Samples will be required from the Architect/Engineer. The Architect/Engineer, after review and agreement as to the time provided for initial review, shall review and comment on the Shop Drawings, Product Data and Samples in accordance with that schedule. The schedule shall be finalized, prepared and submitted with respect to each of the elements of the Work in time to avoid delay, considering reasonable periods for review, manufacture or installation.

At the time the schedule is prepared, the Construction Manager, the Architect/Engineer and Principal Representative shall jointly identify the Shop Drawing, Product Data and Samples, if any, which the Principal Representative shall receive simultaneously with the Architect/Engineer for

the purposes of owner coordination with existing facility standards and systems. The Construction Manager shall furnish a copy for the Principal Representative when so requested. Transmittal of Shop Drawings and Product Data copies to the Principal Representative shall be solely for the convenience of the Principal Representative and shall neither create nor imply responsibility or duty of review by the Principal Representative.

The Construction Manager may also, or at the direction of the Principal Representative at any time shall, prepare and maintain a schedule, which may also be preliminary and subject to change to the extent required, fixing the dates for the initial responses to requests for information or for detail drawings which will be required from the Architect/Engineer to allow the beginning of manufacture, installation of materials and for the completion of the various parts of the Work. The schedule shall be subject to review and approval by the Architect/Engineer. The Architect/Engineer shall, after review and agreement, furnish responses and detail drawings in accordance with that schedule. Any such schedule shall be prepared and approved in time to avoid delay, considering reasonable periods for review, manufacture or installation, but so long as the request for information schedule is being maintained, it shall not be deemed to transfer responsibility to the Construction Manager for errors or omissions in the Contract Documents where circumstances make timely review and performance impossible.

The Architect/Engineer shall not unreasonably withhold approval of the Construction Manager's schedules and shall inform the Construction Manager and the Principal Representative of the basis of any refusal to agree to the Construction Manager's schedules. The Principal Representative shall attempt to resolve any disagreements.

12.2.2 Schedule of Values

Prior to the Notice to Proceed to Commence Construction for the first construction phase, the Construction Manager shall submit to the Architect/Engineer and Principal Representative, for approval, and to the State Buildings Program when specifically requested, a complete itemized schedule of the values of the various parts of the Work, as estimated by the Construction Manager, aggregating the total price. The schedule of values shall be in such detail as the Architect/Engineer or the Principal Representative shall require, prepared on forms acceptable to the Principal Representative. It shall, at a minimum, identify on a separate line each division of the Specifications including the general conditions costs to be charged to the Project. The Construction Manager shall revise and resubmit the schedule of values for approval when, in the opinion of the Architect/Engineer or the Principal Representative, such resubmittal is required due to changes or modifications to the Contract Documents or the Contract sum.

The total cost of each line item so separately identified shall, when requested by the Architect/Engineer or the Principal Representative, be broken down into reasonable estimates of the value as indicated in paragraph 3.4.6 of the Agreement (SC-6.5).

The cost of subcontracts shall be incorporated in the Construction Manager's schedule of values, and when requested by the Architect/Engineer or the Principal Representative, shall be separately shown as line items.

The Architect/Engineer shall review the proposed schedules and approve it after consultation with the Principal Representative, or advise the Construction Manager of any required revisions within ten (10) days of its receipt. In the event no action is taken on the submittal within ten days,

the Construction Manager may utilize the schedule of values as its submittal for payment until it is approved or until revisions are requested.

When the Architect/Engineer deems it appropriate to facilitate certification of the amounts due to the Construction Manager, further breakdown of subcontracts, including breakdown by labor and materials, may be directed.

This schedule of values, when approved, will be used in preparing Construction Manager's applications for payment on State Form SC-7.2, Application for Payment.

12.2.3 Construction Schedules

Prior to the Notice to Proceed to Commence Construction for the first construction phase, the Construction Manager shall submit to the Architect/Engineer and the Principal Representative, and to the State Buildings Program when specifically requested, on a form acceptable to them, an overall timetable of the construction schedule for the Project. Unless the Supplementary General Conditions or the Specifications allow scheduling with bar charts or other less sophisticated scheduling tools, the Construction Manager's schedule shall be a critical-path method (CPM) construction schedule. The CPM schedule shall start with the date of the Notice to Proceed to Commence Construction for the first construction phase and include submittals activities, the various construction activities, change order Work (when applicable), close-out, testing, demonstration of equipment operation when called for in the Specifications, and acceptance. The CPM schedule shall at a minimum correlate to the schedule of values line items and shall be cost loaded if requested by the Architect/Engineer or Principal Representative. The completion time shall be the time specified in the Agreement and all Project scheduling shall allocate float utilizing the full period available for construction as specified in the Agreement, without indication of early completion, unless such earlier completion is approved in writing by the Principal Representative and State Building Programs.

The time shown between the starting and completion dates of the various elements within the construction schedule shall represent one hundred per cent (100%) completion of each element.

All other elements of the CPM schedule shall be as required by the Specifications. In addition, the Construction Manager shall submit monthly updates or more frequently, if required by the Principal Representative, updates of the construction schedule. These updates shall reflect the Construction Manager's "Work in place" progress.

When requested by the Architect/Engineer, the Principal Representative or the State Buildings Program, the Construction Manager shall revise the construction schedule to reflect changes in the schedule of values.

When the testing of materials is required by the Specifications, the Construction Manager shall also prepare and submit to the Architect/Engineer and the Principal Representative a schedule for testing in accordance with Article 14, Samples and Testing.

13 ARTICLE 13 SHOP DRAWINGS, PRODUCT DATA AND SAMPLES

13.1 SUBMITTAL PROCESS

The Construction Manager shall check and field verify all dimensions. The Construction Manager shall check, approve and submit to the Architect/Engineer in accordance with the schedule described in Article 12 of these General Conditions, Requests for Information and Schedules, all Shop Drawings, Product Data and Samples required by the specifications or required by the Construction Manager for the Work of the various trades. All Drawings and Product Data shall contain identifying nomenclature and each submittal shall be accompanied by a letter of transmittal identifying in detail all enclosures. The number of copies of Shop Drawings and Product Data to be submitted shall be as specified in the Specifications and if no number is specified then three copies shall be submitted.

The Architect/Engineer shall review and comment on the Shop Drawings and Product Data within the time provided in the agreed upon schedule for conformance with information given and the design concept expressed in, or reasonably inferred from, the Contract Documents. The nature of all corrections to be made to the Shop Drawings and Product Data, if any, shall be clearly noted, and the submittals shall be returned to the Construction Manager for such corrections. If a change in the scope of the Work is intended by revisions requested to any Shop Drawings and Product Data, the Construction Manager shall be requested to prepare a change proposal in accordance with Article 35 of these General Conditions, Changes in the Work. On resubmitted Shop Drawings, Product Data or Samples, the Construction Manager shall direct specific attention in writing on the transmittal cover to revisions other than those corrections requested by the Architect/Engineer on any previously checked submittal. The Architect/Engineer shall promptly review and comment on, and return, the resubmitted items.

The Construction Manager shall thereafter furnish such other copies in the form approved by the Architect/Engineer as may be needed for the prosecution of the Work.

13.1.1 Buy Clean Colorado (BCCO) Act

If applicable in Article 7 of the Agreement (SC-6.21), the Contractor shall submit products that comply with the State's Environmental Product Declaration (EPD) for each eligible material within the Project specifications. The BCCO Act EPD Submittal form (EE-5.2) shall be used to certify that all applicable materials have been considered. The Contractor is responsible for submitting the eligible product-specific EPDs to the Architect/Engineer for approval. Each EPD must reference the associated Product Category Rule (PCR), indicate third-party verification (Type III), and reference all ISO Standards (ISO 14025:2006, ISO 14040:2006, and ISO 14044:2006).

Contractor shall maintain and organize all approved project EPDs and waivers to be submitted in a zip folder as part of the closeout documentation.

13.2 FABRICATION AND ORDERING

Fabrication shall be started by the Construction Manager only after receiving approved Shop Drawings from the Architect/Engineer. Materials shall be ordered in accordance with approved Product Data. Work which is improperly fabricated, whether through incorrect Shop Drawings, faulty workmanship or materials, will not be acceptable.

13.3 DEVIATIONS FROM DRAWINGS OR SPECIFICATIONS

The review and comments of the Architect/Engineer of Shop Drawings, Product Data or Samples shall not relieve the Construction Manager from responsibility for deviations from the Drawings

or Specifications, unless the Construction Manager has in writing called the attention of the Architect/Engineer to such deviations at the time of submission, nor shall it relieve the Construction Manager from responsibility for errors of any sort in Shop Drawings or Product Data. Review and comments on Shop Drawings or Product Data containing identified deviations from the Contract Documents shall not be the basis for a Change Order or a claim based on a change in the scope of the Work unless Notice is given to the Architect/Engineer and Principal Representative of all additional costs, time and other impacts of the identified deviation by bringing it to their attention in writing at the time the submittals are made, and any subsequent change in the Contract sum or the Contract time shall be limited to cost, time and impacts so identified.

13.4 CONSTRUCTION MANAGER REPRESENTATIONS

By preparing, approving, and/or submitting Shop Drawings, Product Data and Samples, the Construction Manager represents that the Construction Manager has determined and verified all materials, field measurements, and field construction criteria related thereto, and has checked and coordinated the information contained within each submittal with the requirements of the Work, the Project and the Contract Documents and prior reviews and approvals.

14 ARTICLE 14 SAMPLES AND TESTING

14.1 SAMPLES

The Construction Manager shall furnish for approval, with such promptness as to cause no delay in their Work or in that of any other Construction Manager, all Samples as directed by the Architect/Engineer. The Architect/Engineer shall check and approve such Samples, with reasonable promptness, but only for conformance with the design intent of the Contract Documents and the Project, and for compliance with any submission requirements given in the Contract Documents.

14.2 TESTING - GENERAL

The Construction Manager shall provide such equipment and facilities as the Architect/Engineer may require for conducting field tests and for collecting and forwarding samples to be tested. Samples themselves shall not be incorporated into the Work after approval without the permission of the Architect/Engineer.

All materials or equipment proposed to be used may be tested at any time during their preparation or use. The Construction Manager shall furnish the required samples without charge and shall give sufficient Notice of the placing of orders to permit the testing thereof. Products may be sampled either prior to shipment or after being received at the site of the Work.

Tests shall be made by an accredited testing laboratory. Except as otherwise provided in the Specifications, sampling and testing of all materials, and the laboratory methods and testing equipment, shall be in accordance with the latest standards and tentative methods of the American Society of Testing Materials (ASTM). The cost of testing which is in addition to the requirements of the Specifications shall be paid by the Construction Manager if so directed by the Architect/Engineer, and the Contract sum shall be adjusted accordingly by Change Order; provided however, that whenever testing shows portions of the Work to be deficient, all costs of

testing including that required to verify the adequacy of repair or replacement Work shall be the responsibility of the Construction Manager.

14.3 TESTING - CONCRETE AND SOILS

Unless otherwise specified or provided elsewhere in the Contract Documents, the Principal Representative will contract for and pay for the testing of concrete and for soils compaction testing through an independent laboratory or laboratories selected and approved by the Principal Representative. The Construction Manager shall assume the responsibility of arranging, scheduling and coordinating the concrete sample collection efforts and soils compaction efforts in an efficient and cost effective manner. Testing shall be performed in accordance with the requirements of the Specifications, and if no requirements are specified, the Construction Manager shall request instructions and testing shall be as directed by the Architect/Engineer or the soils engineer, as applicable, and in accordance with standard industry practices.

The Principal Representative and the Architect/Engineer shall be given reasonable advance notice of each concrete pour and reserve the right to either increase or decrease the number of cylinders or the frequency of tests.

Soil compaction testing shall be at random locations selected by the soils engineer. In general, soils compaction testing shall be as directed by the soils engineer and shall include all substrate prior to backfill or construction.

14.4 TESTING - OTHER

Additional testing required by the Specifications will be accomplished and paid for by the Principal Representative in a manner similar to that for concrete and soils unless noted otherwise in the Specifications. In any case, the Construction Manager will be responsible for arranging, scheduling and coordinating additional tests. Where the additional testing will be contracted and paid for by the Principal Representative the Construction Manager shall give the Principal Representative not less than one (1)-month advance written Notice of the date the first such test will be required.

15 ARTICLE 15 SUBCONTRACTS

15.1 CONTRACT PERFORMANCE OUTSIDE OF THE UNITED STATES OR COLORADO

After the contract is awarded, Construction Manager is required to provide written notice to the Principal Representative no later than twenty (20) days after deciding to perform services under this contract outside the United States or Colorado or to subcontract services under this contract to a Subcontractor that will perform such services outside the United States or Colorado. The written notification must include, but need not be limited to, a statement of the type of services that will be performed at a location outside the United States or Colorado and the reason why it is necessary or advantageous to go outside the United States or Colorado to perform the services. All notices received by the State pursuant to outsourced services shall be posted on the Colorado Department of Personnel & Administration's website. *If Construction Manager knowingly fails to notify the Principal Representative of any outsourced services as specified herein, the Principal Representative, at its discretion, may terminate this contract as provided in the Colorado Procurement Code or the applicable procurement code for institutions of higher education (Does not apply to any project that receives federal moneys).*

15.2 SUBCONTRACTOR PREQUALIFICATION

Prior to the Notice to Proceed to Commence Construction for the first and subsequent construction phases, the Construction Manager shall submit to the Principal Representative and State Buildings Program a complete list of all known Subcontractors, planned for the Work. The list shall be supplemented as other Subcontractors are determined by the Construction Manager and any such supplemental list shall be submitted to the Principal Representative and State Buildings Program not less than ten (10) days before the Subcontractors commence Work.

15.3 SUBCONTRACTOR PROPOSALS

If Construction Manager utilizes any Subcontractor on this Project, Construction Manager shall request and receive proposals from the Subcontractors and subcontracts will be awarded after the proposals are tabulated in a pre-approved format which compares to the Fixed Limit of Construction Cost budgeted by line item, as indicated in the finalized Construction Manager's Fee Proposal, and, reviewed by the Construction Manager, and Principal Representative.

Should the Construction Manager submit a proposal for subcontract Work, the proposal conditions used shall be the same as for all Subcontractor proposals. These Construction Manager proposals for subcontract Work shall be submitted to the Principal Representative twenty-four (24) hours prior to receipt of other Subcontractor proposals and be opened with the other proposals.

15.4 SUBCONTRACT FORMS

All subcontracts will be between Construction Manager and the Subcontractors. The form of subcontracts shall be furnished to the Principal Representative for review and consent as to form, which consent shall not be unreasonably withheld.

15.5 SUBCONTRACTOR SUBSTITUTION

The substitution of any Subcontractor listed in the Construction Manager's bid shall be justified in writing not less than ten (10) days after the date of the Notice to Proceed to Commence Construction for the first and subsequent construction phases, and shall be subject to the approval of the Principal Representative. For reasons such as the Subcontractor's refusal to perform as agreed, subsequent unavailability or later discovered bid errors, or other similar reasons, but not including the availability of a lower Subcontract price, such substitution may be approved. The Construction Manager shall bear any additional cost incurred by such substitutions.

15.6 CONSTRUCTION MANAGER RESPONSIBLE FOR SUBCONTRACTORS

The Construction Manager shall not employ any Subcontractor that the Architect/Engineer, within ten (10) days after the date of receipt of the Construction Manager's list of Subcontractors or any supplemental list, objects to in writing as being unacceptable to either the Architect/Engineer, the Principal Representative or State Buildings Program. If a Subcontractor is deemed unacceptable, the Construction Manager shall propose a substitute Subcontractor and the Contract sum shall be adjusted by any demonstrated difference between the Subcontractor's bids, except where the Subcontractor has been debarred by the State or fails to meet qualifications of the Contract Documents to perform the Work proposed.

The Construction Manager shall be fully responsible to the Principal Representative for the acts and omissions of Subcontractors and of persons either directly or indirectly employed by them.

All instructions or orders in respect to Work to be done by Subcontractors shall be given to the Construction Manager.

15.7 SUBCONTRACTOR RESPONSIBILITY TO OTHERS

Pursuant to C.R.S. § 24-91-103 (2), if a subcontractor fails to make payments to their suppliers, sub-subcontractors, and laborers interest in the same manner as described in Section 31.5 regarding payments to the contractor to the subcontractor. At the time the subcontractor submits a request for payment to the contractor, the subcontractor shall also submit to the contractor a list of the subcontractor's suppliers, sub-subcontractors, and laborers. The contractor shall be relieved of the requirements regarding payment and interest payment until the subcontractor submits such list. If the contractor fails to make timely payments to the subcontractor as required by Section 31.5 the contractor shall pay the subcontractor interest as specified by contract or at the rate of fifteen percent per annum whichever is higher, on the amount of the payment, which was not made in a timely manner. The interest shall accrue for the period from the required payment date to the date on which payment is made.

15.8 The Contractor shall be responsible for coordinating State Prevailing Wage requirements as described in Article 27

16 ARTICLE 16 RELATIONS OF CONSTRUCTION MANAGER AND SUBCONTRACTOR

The Construction Manager agrees to bind each Subcontractor to the terms of these General Conditions and to the requirements of the Drawings and Specifications, and any Addenda thereto, and also all the other Contract Documents, so far as applicable to the Work of such Subcontractor. The Construction Manager further agrees to bind each Subcontractor to those terms of the General Conditions which expressly require that Subcontractors also be bound, including without limitation, requirements that Subcontractors waive all rights of subrogation, provide adequate general commercial liability and property insurance, automobile insurance and workers' compensation insurance as provided in Article 25 of these General Conditions, Insurance.

Nothing contained in the Contract Documents shall be deemed to create any contractual relationship whatsoever between any Subcontractor and the State of Colorado acting by and through its Principal Representative.

17 ARTICLE 17 MUTUAL RESPONSIBILITY OF CONTRACTORS

Should the Construction Manager cause damage to any separate contractor on the Work, the Construction Manager agrees, upon due Notice, to settle with such contractor by agreement, if the contractors will so settle. If such separate contractor sues the Principal Representative on account of any damage alleged to have been so sustained, the Principal Representative shall notify the Construction Manager, who shall defend such proceedings if requested to do so by Principal Representative. If any judgment against the Principal Representative arises there from, the Construction Manager shall pay or satisfy it and pay all costs and reasonable attorney fees incurred by the Principal Representative, in accordance with Section 53.24 of these General Conditions, Indemnification, provided the Construction Manager was given due Notice of an opportunity to settle.

18 ARTICLE 18 SEPARATE CONTRACTS

The Principal Representative reserves the right to enter into other contracts in connection with the Project or the Contract. The Construction Manager shall afford other contractors reasonable opportunity for the introduction and storage of their materials and the execution of their Work, and shall properly connect and coordinate their Work with theirs. If any part of the Construction Manager's Work depends, for proper execution or results, upon the Work of any other contractor, the Construction Manager shall inspect and promptly report to the Architect/Engineer any defects in such Work that render it unsuitable for such proper execution and results. Failure of the Construction Manager to so inspect and report shall constitute an acceptance of the other contractor's Work as fit and proper for the reception of Work, except as to defects which may develop in the other Construction Manager's Work after the execution of the Construction Manager's Work.

To insure the proper execution of subsequent Work, the Construction Manager shall measure Work already in place and shall at once report to the Architect/Engineer any discrepancy between the executed Work and the Drawings.

19 ARTICLE 19 USE OF PREMISES

The Construction Manager shall confine apparatus, the storage of materials and the operations of workmen to limits indicated by law, ordinances, permits and any limits lines shown on the Drawings. The Construction Manager shall not unreasonably encumber the premises with materials.

The Construction Manager shall enforce all of the Architect/Engineer's instructions and prohibitions regarding, without limitation, such matters as signs, advertisements, fires, smoking and security.

20 ARTICLE 20 CUTTING, FITTING OR PATCHING

The Construction Manager shall do all cutting, fitting or patching of Work that may be required to make its several parts come together properly and fit it to receive or be received by Work of other contractors shown upon, or reasonably inferred from, the Drawings and Specifications for the complete structure, and shall provide for such finishes to patched or fitted Work as the Architect/Engineer may direct. The Construction Manager shall not endanger any Work by cutting, excavating or otherwise altering the Work and shall not cut or alter the Work of any other contractor save with the consent of the Architect/Engineer.

21 ARTICLE 21 UTILITIES

21.1 TEMPORARY UTILITIES

Unless otherwise specifically stated in the Specifications or on the Drawings, the Principal Representative shall be responsible for the locations of all utilities as shown on the Drawings or indicated elsewhere in the Specifications, subject to the Construction Manager's compliance with all statutory or regulatory requirements to call for utility locates. When actual conditions deviate

from those shown the Construction Manager shall comply with the requirements of Article 37 of these General Conditions, Differing Site Conditions. The Construction Manager shall provide and pay for the installation of all temporary utilities required to supply all the power, light and water needed by them and other contractors for their Work and shall install and maintain all such utilities in such manner as to protect the public and Workmen and conform with any applicable laws and regulations. Upon completion of the Work, the Construction Manager shall remove all such temporary utilities from the site. The Construction Manager shall pay for all consumption of power, light and water used by them and the other contractors, without regard to whether such items are metered by temporary or permanent meters. The Superintendent shall have full authority over all trades and Subcontractors at any tier to prevent waste. The cut-off date on permanent meters shall be either the agreed date of the date of the Notice of Substantial Completion or the Notice of Approval of Occupancy/Use of the Project.

21.2 PROTECTION OF EXISTING UTILITIES

Where existing utilities, such as water mains, sanitary sewers, storm sewers and electrical conduits, are shown on the Drawings, the Construction Manager shall be responsible for the protection thereof, without regard to whether any such utilities are to be relocated or removed as a part of the Work. If any utilities are to be moved, the moving must be conducted in such manner as not to cause undue interruption or delay in the operation of the same.

21.3 CROSSING OF UTILITIES

When new construction crosses highways, railroads, streets, or utilities under the jurisdiction of State, city or other public agency, public utility or private entity, the Construction Manager shall secure proper written permission before executing such new construction. The Construction Manager will be required to furnish a proper release before final acceptance of the Work.

22 ARTICLE 22 UNSUITABLE CONDITIONS

The Construction Manager shall not Work at any time, or permit any Work to be done, under any conditions contrary to those recommended by manufacturers or industry standards which are otherwise proper, unsuited for proper execution, safety and performance. Any cost caused by ill-timed Work shall be borne by the Construction Manager unless the timing of such Work shall have been directed by the Architect/Engineer or the Principal Representative, after the award of the Contract, and the Construction Manager provided Notice of any additional cost.

23 ARTICLE 23 TEMPORARY FACILITIES

23.1 OFFICE FACILITIES

The Construction Manager shall provide and maintain without additional expense for the duration of the Project temporary office facilities, as required and as specified, for its own use and the use of the Architect/Engineer, representatives of the Principal Representative and State Buildings Program.

23.2 TEMPORARY HEAT

The Construction Manager shall furnish and pay for all the labor, facilities, equipment, fuel and power necessary to supply temporary heating, ventilating and air conditioning, except to the extent otherwise specified, and shall be responsible for the installation, operation, maintenance and removal of such facilities and equipment. Unless otherwise specified, the permanent HVAC

system shall not be used for temporary heat in whole or in part. If the Construction Manager desires to put the permanent system into use, in whole or in part, the Construction Manager shall set it into operation and furnish the necessary fuel and manpower to safely operate, protect and maintain that HVAC system. Any operation of all or any part of the permanent HVAC system including operation for testing purposes shall not constitute acceptance of the system, nor shall it relieve the Construction Manager of their one-year guarantee of the system from the date of the Notice of Substantial Completion of the entire Project, and if necessary due to prior operation, the Construction Manager shall provide manufacturers' extended warranties from the date of the Construction Manager's use prior to the date of the Notice of Substantial Completion.

23.3 WEATHER PROTECTION

The Construction Manager shall, at all times, provide protection against weather, so as to maintain all Work, materials, apparatus and fixtures free from injury or damages. The Construction Manager shall provide weather-tight storage on substantial floors at least six (6) inches off the ground for all materials requiring protection from the weather.

23.4 DUST PARTITIONS

If the Work involves work in an occupied existing building, the Construction Manager shall erect and maintain during the progress of the Work, suitable dust-proof temporary partitions, or more permanent partitions as specified, to protect such building and the occupants thereof.

23.5 BENCH MARKS

The Construction Manager shall maintain any site bench marks provided by the Principal Representative and shall establish any additional benchmarks specified by the Architect/Engineer as necessary for the Construction Manager to layout the Work and ascertain all grades and levels as needed.

23.6 SIGN

The Construction Manager shall erect and permit one 4' x 8' sign only at the site to identify the Project as specified or directed by the Architect/Engineer, which shall be maintained in good condition during the life of the Project.

23.7 SANITARY PROVISION

The Construction Manager shall provide and maintain suitable, clean, temporary sanitary toilet facilities for any and all workmen engaged on the Work, for the entire construction period, in strict compliance with the requirement of all applicable codes, regulations, laws and ordinances, and no other facilities, new or existing, may be used by any person on the Project. When the Project is complete, the Construction Manager shall promptly remove them from the site, disinfect, and clean or treat the areas as required. If any new construction surfaces in the Project other than the toilet facilities provided for herein are soiled at any time, the entire areas so soiled shall be completely removed from the Project and rebuilt. In no event may present toilet facilities of any existing building at the site of the Work be used by employees of the Construction Manager or any Subcontractors.

24 ARTICLE 24 CLEANING UP

The Construction Manager shall keep the building and premises free from all surplus material, waste material, dirt and rubbish caused by employees or Work, and at the completion of the Work, shall remove all such surplus material, waste material, dirt, and rubbish, as well as all tools,

equipment and scaffolding, and shall wash and clean all window glass and plumbing fixtures, perform cleanup and cleaning required by the Specifications and leave all of the Work clean unless more exact requirements are specified.

25 ARTICLE 25 INSURANCE

25.1 GENERAL

The Construction Manager shall procure and maintain all insurance requirements and limits as set forth below, at their own expense, for the length of time set forth in Contract requirements. The Construction Manager shall continue to provide evidence of such coverage to the Principal Representative on an annual basis during the aforementioned period including all of the terms of the insurance and indemnification requirements of these General Conditions. All below insurance policies shall include a provision preventing cancellation without thirty (30) days' prior notice by certified mail. A completed Certificate of Insurance shall be filed with the Principal Representative and State Buildings Program within ten (10) days after the date of the Notice of Award, said Certificate to specifically state the inclusion of the coverages and provisions set forth herein and shall state whether the coverage is "claims made" or "per occurrence".

25.2 COMMERCIAL GENERAL LIABILITY INSURANCE (CGL)

This insurance must protect the Construction Manager from all claims for bodily injury, including death and all claims for destruction of or damage to property (other than the Work itself), arising out of or in connection with any operations under this Contract, whether such operations be by the Construction Manager or by any Subcontractor under them or anyone directly or indirectly employed by the Construction Manager or by a Subcontractor. All such insurance shall be written with limits and coverages as specified below and shall be written on an occurrence form.

General Aggregate	\$2,000,000
Products – Completed Operations Aggregate	\$2,000,000
Each Occurrence	\$1,000,000
Personal Injury	\$1,000,000

The following coverages shall be included in the CGL:

- a) Per project general aggregate (CG 25 03 or similar).
- b) Additional Insured status in favor of the State of Colorado and any other parties as outlined in The Contract and must include both ONGOING Operations AND COMPLETED Operations per CG 2010 07/04 and CG 2037 07/04 , or equivalent as permitted by law.
- c) The policy shall be endorsed to be **primary and non-contributory** with any insurance maintained by Additional Insureds.
- d) A waiver of Subrogation in favor of all Additional Insured parties.
- e) Personal Injury Liability.
- f) Contractual Liability coverage to support indemnification obligation per Section 53.24 of these General Conditions.
- g) Explosion, collapse and underground (xcu).

The following exclusionary endorsements are prohibited in the CGL policy:

- a) Damage to Work performed by Subcontract/Vendor (CG 22-94 or similar).

- b) Contractual Liability Coverage Exclusion modifying or deleting the definition of an “insured contract” from the unaltered SO CG 0001 1001 policy from (CG 24 26 or similar).
- c) If applicable to the Work to be performed: Residential or multi-family.
- d) If applicable to the Work to be performed: Exterior insulation finish systems.
- e) If applicable to the Work to be performed: Subsidence or Earth Movement.

The Construction Manager shall maintain general liability coverage including Products and Completed Operations insurance, and the Additional Insured with primary and non-contributory coverage as specified in this Contract for three (3) years after completion of the project.

25.3 AUTOMOBILE LIABILITY INSURANCE

Automobile liability insurance and business auto liability covering liability arising out of any auto (including owned, hired and non-owned autos).

Combined Bodily Injury and Property Damage Liability (Combined Single Limit):	\$1,000,000 each accident
--	---------------------------

Coverages:	Specific waiver of subrogation
------------	--------------------------------

25.4 WORKERS' COMPENSATION INSURANCE

The Construction Manager shall procure and maintain Workers' Compensation Insurance at their own expense during the term of this Contract, including occupational disease provisions for all employees per statutory requirements. Policy shall contain a waiver of subrogation in favor of the State of Colorado.

The Construction Manager shall also require each Subcontractor to furnish Workers' Compensation Insurance, including occupational disease provisions for all of the latter's employees, and to the extent not furnished, the Construction Manager accepts full liability and responsibility for Subcontractors' employees.

In cases where any class of employees engaged in hazardous Work under this Contract at the site of the Project is not protected under the Workers' Compensation statute, the Construction Manager shall provide, and shall cause each Subcontractor to provide, adequate and suitable insurance for the protection of employees not otherwise protected.

25.5 UMBRELLA LIABILITY INSURANCE:

For construction projects exceeding \$10,000,000, provide the following coverage: The Construction Manager shall maintain umbrella/excess liability insurance on an occurrence basis in excess of the underlying insurance described in Sections 25.2 through 25.4 above. Coverage shall follow the terms of the underlying insurance, included the additional insured and waiver of subrogation provisions. The amounts of insurance required in Sections 25.2 through 25.4 may be satisfied by the Construction Manager purchasing coverage for the limits specified or by any combination of underlying and umbrella limits, so long as the total amount of insurance is not less than the limits specified in each section previously mentioned.

Each occurrence	\$5,000,000
Aggregate	\$5,000,000

25.6 BUILDER'S RISK INSURANCE

Unless otherwise expressly stated in the Supplementary General Conditions (e.g. where the State elects to provide for projects with a completed value of less than \$1,000,000), the Construction Manager shall purchase and maintain, in a company or companies lawfully authorized to do business in the jurisdiction in which the Project is located, property insurance written on a builder's risk "all-risk" or equivalent policy form in the amount of the initial Contract Sum, plus value of subsequent Contract Modifications and cost of materials supplied or installed by others, comprising total value for the entire Project at the site on a replacement cost basis without optional deductibles. Such property insurance shall be maintained, unless otherwise provided in the Contract Documents or otherwise agreed in writing by all persons and entities who are beneficiaries of such insurance, until final payment has been made or until no person or entity other than the Owner has an insurable interest in the property, or the Date of Notice specified on the Notice of Acceptance, State Form SBP-6.27 or whichever is later to occur.

This insurance shall include interests of the Owner, the Construction Manager, Subcontractors and Sub-subcontractors in the Project as named insureds.

All associated deductibles shall be the responsibility of the Construction Manager. Such policy may have a deductible clause but not to exceed ten thousand dollars (\$10,000.00).

Property insurance shall be on an "all risk" or equivalent policy form and shall include, without limitation, insurance against the perils of fire (with extended coverage) and physical loss or damage including, without duplication of coverage, theft, vandalism, malicious mischief, collapse, earthquake, flood, windstorm, false Work, testing and startup, temporary buildings and debris removal including demolition occasioned by enforcement of any applicable legal requirements, and shall cover reasonable compensation for Architect/Engineer's and Construction Manager's services and expenses required as a result of such insured loss.

Construction Manager shall maintain Builders Risk coverage including partial use by Owner.

The Construction Manager shall waive all rights of subrogation as regards to the State of Colorado and the Principal Representative, its officials, its officers, its agents and its employees, all while acting within the scope and course of their employment for damages caused by fire or other causes of loss to the extent covered by property insurance obtained pursuant to this Section or other property insurance applicable to the Work. The Construction Manager shall require all Subcontractors at any tier to similarly waive all such rights of subrogation and shall expressly include such a waiver in all subcontracts.

Upon request, the amount of such insurance shall be increased to include the cost of any additional Work to be done on the Project, or materials or equipment to be incorporated in the Project, under other independent contracts let or to be let. In such event, the Construction Manager shall be reimbursed for this cost as their share of the insurance in the same ratio as the ratio of the insurance represented by such independent contracts let or to be let to the total insurance carried.

The Principal Representative, with approval of the State Controller, (or comparable position at a contracting institution of higher education) shall have the power to adjust and settle any loss.

Unless it is agreed otherwise, all monies received shall be applied first on rebuilding or repairing the destroyed or injured Work.

25.7 POLLUTION LIABILITY INSURANCE

If Construction Manager is providing directly or indirectly Work with pollution/environmental hazards, the Construction Manager must provide or cause those conducting the Work to provide Pollution Liability Insurance coverage. The Pollution Liability policy must include contractual liability coverage. State of Colorado must be included as additional insureds on the policy. The policy limits shall be in the amount of \$1,000,000 with maximum deductible of \$25,000 to be paid by the Construction Manager or applicable Subcontractor.

25.8 ADDITIONAL MISCELLANEOUS INSURANCE PROVISIONS

Certificates of Insurance and/or insurance policies required under this Contract shall be subject to the following stipulations and additional requirements:

- 25.8.1 Any and all deductibles or self-insured retentions contained in any Insurance policy shall be assumed by and at the sole risk of the Construction Manager;
- 25.8.2 If any of the said policies shall fail at any time to meet the requirements of the Contract Documents as to form or substance, or if a company issuing any such policy shall be or at any time cease to be approved by the Division of Insurance of the State of Colorado, or be or cease to be in compliance with any stricter requirements of the Contract Documents, the Construction Manager shall promptly obtain a new policy, submit the same to the Principal Representative and State Buildings Program for approval if requested, and submit a Certificate of Insurance as hereinbefore provided. Upon failure of the Construction Manager to furnish, deliver and maintain such insurance as provided herein, this Contract, in the sole discretion of the State of Colorado, may be immediately declared suspended, discontinued, or terminated. Failure of the Construction Manager in obtaining and/or maintaining any required insurance shall not relieve the Construction Manager from any liability under the Contract, nor shall the insurance requirements be construed to conflict with the obligations of the Construction Manager concerning indemnification;
- 25.8.3 All requisite insurance shall be obtained from financially responsible insurance companies, authorized to do business in the State of Colorado and acceptable to the Principal Representative; and
- 25.8.4 Receipt, review or acceptance by the Principal Representative of any insurance policies or certificates of insurance required by this Contract shall not be construed as a waiver or relieve the Construction Manager from its obligation to meet the insurance requirements contained in these General Conditions.

26 ARTICLE 26 CONSTRUCTION MANAGER'S PERFORMANCE AND PAYMENT BONDS

The Construction Manager shall furnish a Performance Bond and a Labor and Material Payment Bond on State Forms SC-6.22, Performance Bond, and SC-6.221, Labor and Material Payment Bond, or such other forms as State Buildings Program may approve for the Project, executed by a corporate Surety authorized to do business in the State of Colorado and in the full amount of the Contract sum. The expense of these bonds shall be borne by the Contractor and the bonds shall be filed with the Principal Representative and State Buildings Program.

If, at any time, a Surety on such a bond is found to be, or ceases to be in strict compliance with any qualification requirements of the Contract Documents or the bid documents, or loses its right to do business in the State of Colorado, another Surety will be required, which the Construction Manager shall furnish to the Principal Representative and State Buildings Program within ten (10) days after receipt of Notice from the Principal Representative or after the Construction Manager otherwise becomes aware of such conditions.

27 ARTICLE 27 LABOR AND WAGES

27.1 LABOR

In accordance with laws of Colorado, § 8-17-101(1), C.R.S., as amended, Colorado labor shall be employed to perform at least eighty percent of the Work. If the Federal Davis-Bacon Act shall be applicable to the Project, as indicated in Section 7.3 of the Agreement (SC-6.5), Modification of Article 27, the minimum wage rates to be paid on the Project will be specified in the Contract Documents.

27.2 COLORADO WAGES

In accordance with laws of Colorado, § 24-92, C.R.S. Part 2, if prevailing wage rates are applicable as indicated in Section 7.4 of the Agreement (SC-6.5), Modification of Article 27, to this project:

27.2.1 The Construction Manager shall in conspicuous places on the project post an owner provided poster with the current prevailing rate of payments as provided in the project solicitation.

A Construction Manager who fails to comply shall be deemed guilty of a petty offense and shall pay the State one hundred dollars (\$100) for each calendar day of noncompliance as determined by the State.

27.2.2 The Construction Manager and any Subcontractors shall pay all the employees employed directly on the site of the work, unconditionally and not less often than once a week, and without subsequent deduction or rebate on any account, the full amounts accrued at time of payment computed at wage rates not less than those stated in the competitive solicitation, regardless of any contractual relationships that may be alleged to exist between the Construction Manager or Subcontractor and the employees.

27.2.3 The Construction Manager and any Subcontractors shall prepare and submit electronic payroll reports to the Principal Representative in a format approved by State Buildings Program on a monthly basis that disclose all relevant payroll information, including the name and address of any entities to which fringe benefits are paid.

27.2.4 The Construction Manager and any Subcontractors shall maintain on the site where public projects are being constructed a daily log of employees employed each day on the public project. The log shall include, at a minimum, for each employee their name, primary job title, and employer, and shall be kept on a form prescribed by the State Buildings Program. The log shall be available for inspection on the site at all times by the Principal Representative and the State.

27.2.5 If the Construction Manager or any Subcontractor fails to pay wages as are required by the contract, the Principal Representative shall not approve a warrant or demand for payment to the Construction Manager until the Construction Manager furnishes the Principal Representative evidence satisfactory to such agency of government that such wages have been paid; except that the Principal Representative shall approve and pay any portion of a warrant or demand for payment to the Construction Manager to the extent the Principal Representative has been

furnished satisfactory evidence that the Construction Manager or one or more Subcontractors has paid such wages required by the Contract, even if the Construction Manager has not furnished evidence that all of the Subcontractors have paid wages as required by the Contract. The Construction Manager or Subcontractor may use the following procedure in order to satisfy the requirements of this section:

- 27.2.5.1 The Construction Manager or subcontractor may submit to the State, for each employee to whom such wages are due, a check payable to that employee or to the State so it is negotiable by either party. Each such check shall be in an amount representing the difference between the accrued wages required to be paid to that employee by the contract and the wages actually paid by the Construction Manager or subcontractor.
- 27.2.5.2 If any check submitted cannot be delivered to the employee within a reasonable period, then it shall be negotiated by the State and the proceeds deposited in the unclaimed property trust fund created in §38-13-116.6., C.R.S. Nothing in this Section 27.2.5 of these General Conditions shall be construed to lessen the responsibility of the Construction Manager or Subcontractor to attempt to locate and pay any employee to whom wages are due.

28 ARTICLE 28 ROYALTIES AND PATENTS

The Construction Manager shall be responsible for assuring that all rights to use of products and systems have been properly arranged and shall take such action as may be necessary to avoid delay, at no additional charge to the Principal Representative, where such right is challenged during the course of the Work. The Construction Manager shall pay all royalties and license fees required to be paid and shall defend all suits or claims for infringement of any patent rights and shall save the State of Colorado harmless from loss on account thereof, in accordance with Section 53.24, of these General Conditions, Indemnification; provided, however, the Construction Manager shall not be responsible for such loss or defense for any copyright violations contained in the Contract Documents prepared by the Architect/Engineer or the Principal Representative of which the Construction Manager is unaware, or for any patent violations based on specified processes that the Construction Manager is unaware are patented or that the Construction Manager should not have had reason to believe were patented.

29 ARTICLE 29 ASSIGNMENT

Except as otherwise provided hereafter, the Construction Manager shall not assign the whole or any part of this Contract without the prior written consent of the Principal Representative. This provision shall not be construed to prohibit assignments of the right to payment to the extent permitted by § 4-9-406, C.R.S. et. seq., as amended, provided that written Notice of assignment adequate to identify the rights assigned is received by the Principal Representative and the controller for the agency, department, or institution executing this Contract (as distinguished from the State Controller). Such assignment of the right to payment shall not be deemed valid until receipt by the Principal Representative and such controller and the Construction Manager assumes the risk that such written Notice of assignment is received by the Principal Representative and the controller for the agency, department, or institution involved. In case the Construction Manager assigns all or part of any moneys due or to become due under this Contract, the instrument of assignment shall contain a clause substantially to the effect that it is agreed that the right of the assignee in and to any moneys due or to become due to the Construction Manager shall be subject to all claims of all persons, firms, and corporations for services rendered

or materials supplied for the performance of the Work called for in this Contract, whether said service or materials were supplied prior to or after the assignment. Nothing in this Article shall be deemed a waiver of any other defenses available to the Principal Representative against the Construction Manager or the assignee.

30 ARTICLE 30 CORRECTION OF WORK BEFORE ACCEPTANCE

The Construction Manager shall promptly remove from the premises all Work or materials condemned or declared irreparably defective as failing to conform to the Contract Documents on receipt of written Notice from the Architect/Engineer or the Principal Representative, whether incorporated in the Work or not. If such materials shall have been incorporated in the Work, or if any unsatisfactory Work is discovered, the Construction Manager shall promptly replace and re-execute their Work in accordance with the requirements of the Contract Documents without expense to the Principal Representative, and shall also bear the expense of making good all Work of other contractors destroyed or damaged by the removal or replacement of such defective material or Work.

Should any defective Work or material be discovered during the process of construction, or should reasonable doubt arise as to whether certain material or Work is in accordance with the Contract Documents, the value of such defective or questionable material or Work shall not be included in any application for payment, or if previously included, shall be deducted by the Architect/Engineer from the next application submitted by the Construction Manager.

If the Construction Manager does not perform repair, correction and replacement of defective Work, in lieu of proceeding by issuance of a Notice of intent to remove condemned Work as outlined above, the Principal Representative may, not less than seven (7) days after giving the original written Notice of the need to repair, correct, or replace defective Work, deduct all costs and expenses of replacement or correction as instructed by the Architect/Engineer from the Construction Manager's next application for payment in addition to the value of the defective Work or material. The Principal Representative may also make an equitable deduction from the Contract sum by unilateral Change Order, in accordance with Article 33, Payments Withheld and Article 35, Changes in the Work, of these General Conditions.

If the Construction Manager does not remove such condemned or irreparably defective Work or material within a reasonable time, the Principal Representative may, after giving a second seven (7) day advance Notice to the Construction Manager and the Surety, remove them and may store the material at the Construction Manager's expense. The Principal Representative may accomplish the removal and replacement with its own forces or with another contractor. If the Construction Manager does not pay the expense of such removal and pay all storage charges within ten (10) days thereafter, the Principal Representative may, upon ten (10) days' written Notice, sell such material at auction or at private sale and account for the net proceeds thereof, after deducting all costs and expenses which should have been borne by the Construction Manager. If the Construction Manager shall commence and diligently pursue such removal and replacement before the expiration of the seven-day period, or if the Construction Manager shall show good cause in conjunction with submittal of a revised CPM schedule showing when the Work will be performed and why such removal of condemned Work should be scheduled for a later date, the Principal Representative shall not proceed to remove or replace the condemned Work.

If the Construction Manager disagrees with the Notice to remove Work or materials condemned or declared irreparably defective, the Construction Manager may request facilitated negotiation of the issue and the Principal Representative's right to proceed with removal and to deduct costs and expenses of repair shall be suspended and tolled until such time as the parties meet and negotiate the issue.

During construction, whenever the Architect/Engineer has advised the Construction Manager in writing, in the Specifications, by reference to Article 6 of these General Conditions, Architect/Engineer Decisions And Judgments, or elsewhere in the Contract Documents of a need to observe materials in place prior to their being permanently covered up, it shall be the Construction Manager's responsibility to notify the Architect/Engineer at least forty-eight (48) hours in advance of such covering operation. If the Construction Manager fails to provide such notification, Construction Manager shall, at their expense, uncover such portions of the Work as required by the Architect/Engineer for observation, and reinstall such covering after observation. When a covering operation is continued from day to day, notification of the commencement of a single continuing covering operation shall suffice for the activity specified so long as it proceeds regularly and without interruption from day to day, in which event the Construction Manager shall coordinate with the Architect/Engineer regarding the continuing covering operation.

31 ARTICLE 31 APPLICATIONS FOR PAYMENTS

31.1 CONSTRUCTION MANAGER'S SUBMITTALS

On or before the first day of each month and no more than five days prior thereto, the Construction Manager may submit applications for payment for the Work performed during such month covering the portion of the Work completed as of the date indicated, and payments on account of this Contract shall be due per § 24-30-202(24) C.R.S. (correct notice of amount due), within forty-five (45) days of receipt by the Principal Representative of application for payments that have been certified by the Architect/Engineer. The Construction Manager shall submit the application for payment to the Architect/Engineer on State forms SBP-7.2, Application and Certificate for Contractor's Payment, or such other format as the State Buildings Program shall approve, in an itemized format in accordance with the schedule of values or a cost loaded CPM schedule when required, supported to the extent reasonably required by the Architect/Engineer or the Principal Representative by receipts or other vouchers, showing payments for materials and labor, prior payments and payments to be made to Subcontractors and such other evidence of the Construction Manager's right to payments as the Architect/Engineer or Principal Representative may direct.

Amounts not paid by the State within 45 days of the State's acceptance of the invoice shall bear interest on the unpaid balance beginning on the 45th day at the rate of 1% per month, as required by §24-30-202(24)(a), C.R.S., until paid in full; provided, however, that interest shall not accrue on unpaid amounts that the State disputes in writing. Contractor shall invoice the State separately for accrued interest on delinquent amounts, and the invoice shall reference the delinquent payment, the number of day's interest to be paid and the interest rate.

If payments are made on account of materials not incorporated in the Work but delivered and suitably stored at the site, or at some other location agreed upon in writing, such payments shall

be conditioned upon submission by the Construction Manager of bills of sale or such other procedure as will establish the Principal Representative's title to such material or otherwise adequately protect the Principal Representative's interests, and shall provide proof of insurance whenever requested by the Principal Representative or the Architect/Engineer, and shall be subject to the right to inspect the materials at the request of either the Architect/Engineer or the Principal Representative.

All applications for payment, except the final application, and the payments there under, shall be subject to correction in the next application rendered following the discovery of any error.

31.2 ARCHITECT/ENGINEER CERTIFICATION

In accordance with the Architect/Engineer's agreement with the Principal Representative, the Architect/Engineer after appropriate observation of the progress of the Work shall certify to the Principal Representative the amount that the Construction Manager is entitled to, and forward the application to the Principal Representative. If the Architect/Engineer certifies an amount different from the amount requested or otherwise alters the Construction Manager's application for payment, a copy shall be forwarded to the Construction Manager.

If the Architect/Engineer is unable to certify all or portions of the amount requested due to the absence or lack of required supporting evidence, the Architect/Engineer shall advise the Construction Manager of the deficiency. If the deficiency is not corrected at the end of ten (10) days, the Architect/Engineer may either certify the remaining amounts properly supported to which the Construction Manager is entitled, or return the application for payment to the Construction Manager for revision with a written explanation as to why it could not be certified.

31.3 RETAINAGE WITHHELD

Unless otherwise provided in the Supplementary General Conditions, an amount equivalent to five percent (5%) of the amount shown to be due the Construction Manager on each application for payment shall be withheld until the Work required by the Contract has been performed. The withheld percentage of the contract price of any such Work, improvement, or construction shall be administered according to. § 24-91-103 C.R.S, as amended, and § 38-26-107, C.R.S. as amended, and Section 31.4 of these General Conditions, and, shall be retained until the Work or discrete portions of the Work, have been completed satisfactorily, finally or partially accepted, and advertised for final settlement as further provided in Article 41 of these General Conditions.

31.4 RELEASE OF RETAINAGE

The Construction Manager may, for satisfactory and substantial reasons shown to the Principal Representative's satisfaction, make a written request to the Principal Representative and the Architect/Engineer for release of part or all of the withheld percentage applicable to the Work of a Subcontractor which has completed the subcontracted Work in a manner finally acceptable to the Architect/Engineer, the Construction Manager, and the Principal Representative. Any such request shall be supported by a written approval from the Surety furnishing the Construction Manager's bonds and any surety that has provided a bond for the Subcontractor. The release of any such withheld percentage shall be further supported by such other evidence as the Architect/Engineer or the Principal Representative may require, including but not limited to, evidence of prior payments made to the Subcontractor, copies of the Subcontractor's contract with the Construction Manager, any applicable warranties, as-built information, maintenance manuals and other customary close-out documentation. Neither the Principal Representative nor

the Architect Engineer shall be obligated to review such documentation nor shall they be deemed to assume any obligations to third parties by any review undertaken.

The Construction Manager's obligation under these General Conditions to guarantee Work for one year from the date of the Notice of Substantial Completion or the date of any Notice of Partial Substantial Completion of the applicable portion or phase of the Project, shall be unaffected by such partial release; unless a Notice of Partial Substantial Completion is issued for the Work subject to the release of retainage.

Any rights of the Principal Representative which might be terminated by or from the date of any final acceptance of the Work, whether at common law or by the terms of this Contract, shall not be affected by such partial release of retainage prior to any final acceptance of the entire Project.

The Construction Manager remains fully responsible for the Subcontractor's Work and assumes any risk that might arise by virtue of the partial release to the Subcontractor of the withheld percentage, including the risk that the Subcontractor may not have fully paid for all materials, labor and equipment furnished to the Project.

If the Principal Representative considers the Construction Manager's request for such release satisfactory and supported by substantial reasons, the Architect/Engineer shall make a "final inspection" of the applicable portion of the Project to determine whether the Work has been completed in accordance with the Contract Documents. A final Punch List shall be made for the Subcontractor's Work and the procedures of Article 41 of these General Conditions, Completion, Final Inspection, Acceptance and Settlement, shall be followed for that portion of the Work, except that advertisement of the intent to make final payment to the Subcontractor shall be required only if the Principal Representative has reason to believe that a supplier or Subcontractor to the Subcontractor for which the request is made, may not have been fully paid for all labor and materials furnished to the Project.

31.5 CONTRACTOR'S RESPONSIBILITY TO PAY SUBCONTRACTORS

Pursuant to C.R.S. § 24-91-103 (2) when the contractor receives payment, If the subcontractor is satisfactorily performing under his contract with the contractor, payment to subcontractors shall be made within seven (7) calendar days from receipt of payment. The subcontractor shall pay all suppliers, sub-subcontractors, laborers, and any other persons who provide goods, materials, labor, or equipment the subcontractor any amounts actually received which were included in the subcontractor's request for payment to the contractor.

32 ARTICLE 32 CERTIFICATES FOR PAYMENTS

State Form SBP-7.2, Certificate For Contractor's Payment, and its continuation detail sheets, when submitted, shall constitute the Construction Manager's Application for Payment, and shall be a representation by the Construction Manager to the Principal Representative that the Work has progressed to the point indicated, the quality of the Work is in accordance with the Contract Documents, and materials for which payment is requested have been incorporated into the Project except as noted in the application. If requested by the Principal Representative, the Certificate of Contractor's Application for Payment shall be sworn under oath and notarized.

33 ARTICLE 33 PAYMENTS WITHHELD

The Architect/Engineer, the Principal Representative or State Buildings Program may withhold, or on account of subsequently discovered evidence nullify, the whole or any part of any application on account of, but not limited to any of the following:

- a) Defective Work not remedied;
- b) Claims filed or reasonable evidence indicating probable filing of claims;
- c) Failure of the Construction Manager to make payments to Subcontractors for material or labor;
- d) A reasonable doubt that the Contract can be completed for the balance of the contract price then unpaid;
- e) Damage or injury to another contractor or any other person, persons or property except to the extent of coverage by a policy of insurance;
- f) Failure to obtain necessary permits or licenses or to comply with applicable laws, ordinances, codes, rules or regulations or the directions of the Architect/Engineer;
- g) Failure to submit a monthly construction schedule;
- h) Failure of the Construction Manager to keep Work progressing in accordance with the time schedule;
- i) Failure to keep a superintendent on the Work;
- j) Failure to maintain as built drawings of the Work in progress;
- k) Unauthorized deviations by the Construction Manager from the Contract Documents; or
- l) On account of liquidated damages.

In addition, the Architect Engineer, Principal Representative or State Buildings Program may withhold or nullify the whole or any part of any application for any reason noted elsewhere in these General Conditions of the Construction Manager/General Contractor (CM/GC) Agreement. Nullification shall mean reduction of amounts shown as previously paid on the application. The amount withheld or nullified may be in such amount as the Architect/Engineer or the Principal Representative estimates to be required to allow the Principal Representative to accomplish the Work, cure the failure and cover any damages or injuries, including an allowance for attorneys' fees and costs where appropriate. When the grounds for such withholding or nullifying are removed, payment shall be made for the amounts thus withheld or nullified on such grounds.

34 ARTICLE 34 DEDUCTIONS FOR UNCORRECTED WORK

If the Architect/Engineer and the Principal Representative deem it inexpedient to correct Work damaged or not performed in accordance with the Contract Documents, the Principal Representative may, after consultation with the Architect/Engineer, and ten (10) days' Notice to the Construction Manager of intent to do so, make reasonable reductions from the amounts otherwise due the Construction Manager on the next application for payment. Notice shall specify the amount or terms of any contemplated reduction. The Construction Manager may during this period correct or perform the Work. If the Construction Manager does not correct or perform the Work, an equitable deduction from the Contract sum shall be made by Change Order, in accordance with Article 35 of these General Conditions, Changes in the Work, unilaterally if

necessary. If either party elects' facilitation of this issue after Notice is given, the ten-day (10) notice period shall be extended and tolled until facilitation has occurred.

35 ARTICLE 35 CHANGES IN THE WORK

The Principal Representative may designate, without invalidating the Agreement, and with the approval of State Buildings Program and the State Controller, may order extra Work or make changes with or without the consent of the Construction Manager as hereafter provided, by altering, adding to or deducting from the Work, the Contract sum being adjusted accordingly. All such changes in the Work shall be within the general scope of and be executed under the conditions of the Contract, except that any claim for extension of time made necessary due to the change or any claim of other delay or other impacts caused by or resulting from the change in the Work shall be presented by the Construction Manager and adjusted by Change Order to the extent known at the time such change is ordered and before proceeding with the extra or changed Work. Any claims for extension of time or of delay or other impacts, and any costs associated with extension of time, delay or other impacts, which are not presented before proceeding with the change in the Work, and which are not adjusted by Change Order to the extent known, shall be waived.

The Architect/Engineer shall have authority to make minor changes in the Work, not involving extra cost, and not inconsistent with the intent of the Contract Documents, but otherwise, except in an emergency endangering life or property, no extra Work or change in the Contract Documents shall be made unless by 1) a written Change Order, approved by the Principal Representative, State Buildings Program, and the State Controller (or comparable position at the contracting institution of higher education, where applicable) prior to proceeding with the changed Work; or 2) by an Emergency Field Change Order approved by the Principal Representative and State Buildings Program as hereafter provided in Section 35.4 of these General Conditions, Emergency Field Change Order Work; or 3) by an allocation in writing of any allowance already provided in the encumbered contract amount, the Contract sum being later adjusted to decrease the Contract sum by any unallocated or unexpended amounts remaining in such allowance. No change to the Contract sum shall be valid unless so ordered.

35.1 THE VALUE OF CHANGED WORK

35.1.1 The value of any extra Work or changes in the Work shall be determined by agreement in one or more of the following ways:

- a) By estimate and acceptance of a lump-sum amount;
- b) By unit prices specified in the Agreement, or subsequently agreed upon, that are extended by specific quantities; and
- c) By actual cost plus a fixed fee in a lump sum amount for profit, overhead and all indirect and off-site home office costs, the latter amount agreed upon in writing prior to starting the extra or changed Work.

35.1.2 Where the Construction Manager and the Principal Representative cannot agree on the value of extra Work, the Principal Representative may order the Construction Manager to perform the changes in the Work and a Change Order may be unilaterally issued based on an estimate of the change in the Work prepared by the Architect/Engineer. The value of the change in the Work shall be the Principal Representative's determination of the amount of equitable adjustment attributable to the extra Work or change. The Principal Representative's determination shall be

subject to appeal by the Construction Manager pursuant to the claims process in Article 36 of these General Conditions, Claims.

- 35.1.3 Except as otherwise provided in Section 35.2 of these General Conditions, Detailed Breakdown, below, the Cost Principles of the Colorado Procurement Code or the applicable procurement code for institutions of higher education, shall govern all Contract changes.

35.2 DETAILED BREAKDOWN

In all cases where the value of the extra or changed Work is not known based on unit prices in the Construction Manager's bid or the Agreement, a detailed change proposal shall be submitted by the Construction Manager on a Change Order Proposal (SC-6.312), or in such other format as the State Buildings Program approves, with which the Principal Representative may require an itemized list of materials, equipment and labor, indicating quantities, time and cost for completion of the changed Work.

Such detailed change proposals shall be stated in lump sum amounts and shall be supported by a separate breakdown, which shall include estimates of all or part of the following when requested by the Architect/Engineer or the Principal Representative:

- a) Materials, indicating quantities and unit prices including taxes and delivery costs if any (separated where appropriate into general, mechanical and electrical and/or other Subcontractors' Work; and the Principal Representative may require in its discretion any significant subcontract costs to be similarly and separately broken down).
- b) Labor costs, indicating hourly rates and time and labor burden to include Social Security and other payroll taxes such as unemployment, benefits and other customary burdens.
- c) Costs of project management time and superintendence time of personnel stationed at the site, and other field supervision time, but only where a time extension, other than a weather delay, is approved as part of the Change Order, and only where such project management time and superintendence time is directly attributable to and required by the change; provided however that additional cost of on-site superintendence shall be allowable whenever in the opinion of the Architect/Engineer the impact of multiple change requests to be concurrently performed will result in inadequate levels of supervision to assure a proper result unless additional superintendence is provided.
- d) Construction equipment (including small tools). Expenses for equipment and fuel shall be based on customary commercially reasonable rental rates and schedules. Equipment and hand tool costs shall not include the cost of items customarily owned by workers.
- e) Workers' compensation costs, if not included in labor burden.
- f) The cost of commercial general liability and property damage insurance premiums but only to the extent charged the Construction Manager as a result of the changed Work.
- g) Overhead and profit, as hereafter specified.
- h) Builder's risk insurance premium costs.
- i) Bond premium costs.
- j) Testing costs not otherwise excluded by these General Conditions.
- k) Subcontract costs.

Adjustments to the construction services fee, as defined in Exhibit A of the Agreement shall be per Section 5.2 of the Agreement.

Unless modified in the Supplementary General Conditions, overhead and profit shall not exceed the percentages set forth in the table below.

	OVERHEAD	PROFIT	COMMISSION
To the Construction Manager or to Subcontractors for the portion of Work performed with their own forces:	10%	5%	0%
To the Construction Manager or to Subcontractors for Work performed by others at a tier immediately below either of them:	5%	0%	5%

Overhead shall include: a) insurance premium for policies not purchased for the Project and itemized above, b) home office costs for office management, administrative and supervisory personnel and assistants, c) estimating and change order preparation costs, d) incidental job burdens, e) legal costs, f) data processing costs, g) interest costs on capital, h) general office expenses except those attributable to increased rental expenses for temporary facilities, and all other indirect costs, but shall not include the Social Security tax and other direct labor burdens. The term "Work" as used in the proceeding table shall include labor, materials and equipment and the "Commission" shall include all costs and profit for carrying the subcontracted Work at the tiers below except direct costs as listed in items a. through k. above, if any.

On proposals for Work involving both additions and credits in the amount of the Contract sum, the overhead and profit will be allowed on the net increase only. On proposals resulting in a net deduct to the amount of the Contract sum, profit on the deducted amount shall be returned to the Principal Representative at fifty percent (50%) of the rate specified. The inadequacy of the profit specified shall not be a basis for refusal to submit a proposal.

Except in the case of Change Orders or Emergency Field Change Orders agreed to on the basis of a lump sum amount or unit prices as described in paragraphs 35.1.1 of these General Conditions, The Value of Changed Work, the Construction Manager shall keep and present a correct and fully auditable account of the several items of cost, together with vouchers, receipts, time cards and other proof of costs incurred, summarized on a Change Order form (SC-6.31) using such format for supporting documentation as the Principal Representative and State Buildings Program approve. This requirement applies equally to Work done by Subcontractors. Only auditable costs shall be reimbursable on Change Orders where the value is determined on the basis of actual cost plus a fixed fee pursuant to paragraph 35.1.3 of these General Conditions above, or where unilaterally determined by the Principal Representative on the basis of an equitable adjustment in accordance with the Procurement Rules, as described in Section 35.1, The Value Of Changed Work.

Except for proposals for Work involving both additions and credits, changed Work shall be adjusted and considered separately for Work either added or omitted. The amount of adjustment for Work omitted shall be estimated at the time it is directed to be omitted, and when reasonable to do so, the agreed adjustment shall be reflected on the schedule of values used for the next Construction Manager's application for payment.

The Principal Representative reserves the right to contract with any person or firm other than the Construction Manager for any or all extra Work; however, unless specifically required in the Contract Documents, the Construction Manager shall have no responsibility without additional compensation to supervise or coordinate the Work of persons or firms separately contracted by the Principal Representative.

35.3 HAZARDOUS MATERIALS

The Principal Representative represents that it has undertaken an examination of the site of the Work and has determined that there are no hazardous substances, as defined below, which the Construction Manager could reasonably encounter in its performance of the Work. In the event the Principal Representative so discovers hazardous substances, the Principal Representative shall render harmless such hazards before the Construction Manager commences the Work.

In the event the Construction Manager encounters any materials reasonably believed to be hazardous substances which have not been rendered harmless, the Construction Manager shall immediately stop Work in the area affected and report the condition to the Principal Representative, in writing. For purposes of this Agreement, "hazardous substances" shall include asbestos, lead, polychlorinated biphenyl (PCB) and any or all of those substances defined as "hazardous substance", "hazardous waste", or "dangerous or extremely hazardous wastes" as those terms are used in the Comprehensive Environmental Response, Compensation and Liability Act (CERCLA) and the Resource Conservation and Recovery Act (RCRA), and shall also include materials regulated by the Toxic Substances Control Act (TSCA), the Clean Air Act, the Air Quality Act, the Clean Water Act, and the Occupational Safety and Health Act. The Work in the affected area shall not therefore be resumed except by written agreement of the Principal Representative and the Construction Manager, if in fact materials that are hazardous substances have not been rendered harmless. The Work in the affected area shall be resumed only in the absence of the hazardous substances or when it has been rendered harmless or by written agreement of the Principal Representative and the Construction Manager.

The Construction Manager shall not be required to perform Work without consent in any areas where it reasonably believes hazardous substances that have not been rendered harmless are present.

35.4 EMERGENCY FIELD CHANGE ORDERED WORK

The Principal Representative, without invalidating the Agreement, and with the approval of State Buildings Program and without the approval of the State Controller (or comparable position at the contracting institution of higher education, where applicable), may order extra Work or make changes in the case of an emergency that is a threat to life or property or where the likelihood of delays in processing a normal Change Order will result in substantial delays and/or significant cost increases for the Project. Emergency Field Orders are not to be used solely to expedite normal Change Order processing absent a clear showing of a high potential for significant and substantial cost or delay. Such changes in the Work may be directed through issuance of an Emergency Field Change Order signed by the Construction Manager, the Principal Representative (or by a designee specifically appointed to do so in writing), and approved by the Office of the State Architect or their delegate. The change shall be directed using an Emergency Field Change Order form (SC-6.31E).

If the amount of the adjustment of the Contract price and time for completion can be determined at the time of issuance of the Emergency Field Change Order, those adjustments shall be reflected on the face of the Emergency Field Change Order. Otherwise, the Emergency Field Change Order shall reflect a not to exceed (NTE) amount for any schedule adjustment (increasing or decreasing the time for completion) and an NTE amount for any adjustment to Contract sum, which NTE amount shall represent the maximum amount of adjustment to which the Construction Manager will be entitled, including direct and indirect costs of changed Work, as well as any direct or indirect costs attributable to delays, inefficiencies or other impacts arising out of the change. Emergency Field Change Orders directed in accordance with this provision need not bear the approval signatures of the State Controller (or comparable position at the contracting institution of higher education, where applicable).

On Emergency Field Change Orders where the price and schedule have not been finally determined, the Construction Manager shall submit final costs for adjustment as soon as practicable. No later than seven (7) days after issuance, except as otherwise permitted, and every seven days thereafter, the Construction Manager shall report all costs to the Principal Representative and the Architect/Engineer. The final adjustment of the Emergency Field Change Order amount and the adjustment to the Project time for completion shall be prepared on a normal Change Order from (SC-6.31) in accordance with the procedures described in Section 35.1, The Value of Changed Work, and Section 35.2, Detailed Breakdown, of these General Conditions. Unless otherwise provided in writing signed by the Director of State Buildings Program to the Principal Representative and the Construction Manager, describing the extent and limits of any greater authority, individual Emergency Field Change Orders shall not be issued for more than \$25,000, nor shall the cumulative value of Emergency Field Change Orders exceed an amount of \$100,000.

35.5 APPROPRIATION LIMITATIONS - § 24-91-103.6, C.R.S. as amended

The amount of money appropriated, as shown on the Agreement (SC-6.5), is equal to or in excess of the Contract amount. No Change Order, Emergency Field Change Order, or other type of order or directive shall be issued by the Principal Representative, or any agent acting on their behalf, which directs additional compensable Work to be performed, which Work causes the aggregate amount payable under the Contract to exceed the amount appropriated for the original Contract, as shown on the Agreement (SC-6.5), unless one of the following occurs: (1) the Construction Manager is provided written assurance from the Principal Representative that sufficient additional lawful appropriations exist to cover the cost of the additional Work; or (2) the Work is covered by a Construction Manager remedy provision under the Contract, such as a claim for extra cost. By way of example only, no assurance is required for any order, directive or instruction by the Architect/Engineer or the Principal Representative to perform Work which is determined to be within the performance required by the Contract Documents; the Construction Manager's remedy shall be as described elsewhere in these General Conditions.

Written assurance shall be in the form of an Amendment to the Contract reciting the source and amount of such appropriation available for the Project. No remedy granting provision of this Contract shall obligate the Principal Representative to seek appropriations to cover costs in excess of the amounts recited as available to pay for the Work to be performed.

36 ARTICLE 36 CLAIMS

It is the intent of these General Conditions to provide procedures for speedy and timely resolution of disagreements and disputes at the lowest level possible. In the spirit of on the job resolution of job site issues, the parties are encouraged to use the partnering processes of Section 2.4 of these General Conditions, Partnering, Communications and Cooperation, before turning to the more formal claims processes described in this Article 36, Claims. The use of non-binding dispute resolution, whether through the formal processes described in Article 39 of these General Conditions, Non-Binding Dispute Resolution – Facilitated Negotiations, or through less formal alternative processes developed as part of a partnering plan, are also encouraged. Where such process cannot resolve the issues in dispute, the claims process that follows is intended to cause the issues to be presented, decided and where necessary, documented in close proximity to the events from which the issues arise. To that end, and in summary of the remedy granting process that follows commencing with the next paragraph of this Article 36, Claims, the Construction Manager shall 1) first, seek a decision by the Architect/Engineer, and 2) shall second, informally present the claim to Principal Representative as described hereafter, and 3) failing resolution in the field, give Notice of intent to exercise statutory rights of review of a formal contract controversy, and 4) seek resolution outside the Contract as provided by the Colorado Procurement Code or the applicable procurement code for institutions of higher education.

If the Construction Manager claims that any instructions, by detailed drawings, or otherwise, or any other act or omission of the Architect/Engineer or Principal Representative affecting the scope of the Construction Manager's Work, involve extra cost, extra time or changes in the scope of the Work under this Contract, the Construction Manager shall have the right to assert a claim for such costs or time, provided that before either proceeding to execute such Work (except in an emergency endangering life or property), or filing a Notice of claim, the Construction Manager shall have obtained or requested a written decision of the Architect/Engineer following the procedures as provided in Article 6 of these General Conditions, Architect/Engineer Decisions and Judgments, respectively; provided, however, that in the case of a directed Change in the Work pursuant to Article 35 of these General Conditions, no written judgment or decision of the Architect/Engineer is required. If the Construction Manager is delayed by the lack of a response to a request for a decision by the Architect/Engineer, the Construction Manager shall give Notice in accordance with Article 38 of these General Conditions, Delays and Extensions of Time.

Unless it is the Architect/Engineer's judgment and determination that the Work is not included in the performance required by the Contract Documents, the Construction Manager shall proceed with the Work as originally directed. Where the Construction Manager's claim involves a dispute concerning the Value of Work unilaterally directed pursuant to Section 35.1.2 of these General Conditions the Construction Manager shall also proceed with the Work as originally directed while their claim is being considered.

The Construction Manager shall give the Principal Representative and the Architect/Engineer Notice of any claim promptly after the receipt of the Architect/Engineer's decision, but in no case later than three (3) business days after receipt of the Architect/Engineer's decision (or no later than ten (10) days from the date of the Construction Manager's request for a decision when the Architect/Engineer fails to decide as provided in Article 6 of these General Conditions, Architect/Engineer Decisions and Judgements. The Notice of claim shall state the grounds for the claim and the amount of the claim to the extent known in accordance with the procedures of Article 35 of these General Conditions, Changes in the Work. The period in which Notice must be

given may be extended by the Principal Representative if requested in writing by the Construction Manager with good cause shown, but any such extension to be effective shall be in writing.

The Principal Representative shall respond in writing, with a copy to the Architect/Engineer, within a reasonable time, and except where a request for facilitation of negotiation has been made as hereafter provided, in no case later than fourteen (14) business days (or at such other time as the Construction Manager and Principal Representative agree) after receipt of the Construction Manager's Notice of claim regarding such instructions or alleged act or omission. If no response to the Construction Manager's claim is received within fourteen (14) business days of Construction Manager's Notice (or at such other time as the Construction Manager and Principal Representative agree) and the instructions have not been retracted, it shall be deemed that the Principal Representative has denied the claim.

The Principal Representative may grant or deny the claim in whole or in part, and a Change Order shall be issued if the claim is granted. To the extent any portion of claim is granted where costs are not clearly shown, the Principal Representative may direct that the value of that portion of the Work be determined by any method allowed in Section 35.1 of these General Conditions, The Value of Changed Work. Except in the case of a deemed denial, the Principal Representative shall provide a written explanation regarding any portion of the Construction Manager's claim that is denied.

If the Construction Manager disagrees with the Principal Representative's judgment and determination on the claim and seeks an equitable adjustment of the Contract sum or time for performance, they shall give Notice of intent to exercise their statutory right to seek a decision on the contract controversy within ten (10) days of receipt of the Principal Representative's decision denying the claim. A "contract controversy," as such term is used in the Colorado Procurement Code or the applicable procurement code for institutions of higher education, shall not arise until the initial claim process described above in this Article 36 has been properly exhausted by the Construction Manager. The Construction Manager's failure to proceed with Work directed by the Architect/Engineer or to exhaust the claim process provided above in this Article 36, shall constitute an abandonment of the claim by the Construction Manager and a waiver of the right to contest the decision in any forum.

At the time of filing the Notice of intent to exercise their statutory right to seek a decision on the contract controversy, the Construction Manager may request that the Principal Representative defer a decision on the contract controversy until a later date or until the end of the Project. If the Principal Representative agrees, he or she shall so advise the Construction Manager in writing. If no such request is made, or if the Principal Representative does not agree to such a request, the Principal Representative shall render a written decision within twenty (20) business days and advise the Construction Manager of the reasons for any denial. Unless the claim has been decided by the Principal Representative (as opposed to delegates of the Principal Representative), the person who renders the decision on this statutory contract controversy shall not be the same person who decided the claim. To the extent any portion of the contract controversy is granted where costs are not clearly shown, the Principal Representative may direct that the value of that portion of the Work be determined by any method allowed in Section 35.1 of these General Conditions, The Value of Changed Work. In the event of a denial the Principal Representative shall give Notice to the Construction Manager of their right to administrative and judicial reviews as provided in the Colorado Procurement Code or the applicable procurement code for

institutions of higher education. If no decision regarding the contract controversy is issued within twenty (20) business days of the Construction Manager's giving Notice (or such other date as the Construction Manager and Principal Representative have agreed), and the instructions have not been retracted or the alleged act or omission have not been corrected, it shall be deemed that the Principal Representative has ruled by denial on the contract controversy. Except in the case of a deemed denial, the Principal Representative shall provide an explanation regarding any portion of the contract controversy that involves denial of the Construction Manager's claim.

Either the Construction Manager or the Principal Representative may request facilitation of negotiations concerning the claim or the contract controversy, and if requested, the parties shall consult and negotiate before the Principal Representative decides the issue. Any request for facilitation by the Construction Manager shall be made at the time of the giving of Notice of the claim or Notice of the contract controversy. Facilitation shall extend the time for the Principal Representative to respond by commencing the applicable period at the completion of the facilitated negotiation, which shall be the last day of the parties' meeting, unless otherwise agreed in writing.

Disagreement with the decision of the Architect/Engineer, or the decision of the Principal Representative to deny any claim or denying the contract controversy, shall not be grounds for the Construction Manager to refuse to perform the Work directed or to suspend or terminate performance. During the period that any claim or contract controversy decision is pending under this Article 36, Claims, the Construction Manager shall proceed diligently with the Work directed.

In all cases where the Construction Manager proceeds with the Work and seeks equitable adjustment by filing a claim and or statutory appeal, the Construction Manager shall keep a correct account of the extra cost, in accordance with Section 35.2 of these General Conditions, Detailed Breakdown supported by receipts. The Principal Representative shall be entitled to reject any claim or contract controversy whenever the foregoing procedures are not followed and such accounts and receipts are not presented.

The payments to the Construction Manager in respect of such extra costs shall be limited to reimbursement for the current additional expenditure by the Construction Manager made necessary by the change in the Work, plus a reasonable amount for overhead and profit, determined in accordance with Section 35.2 of these General Conditions, Detailed Breakdown, determined solely with reference to the additional Work, if any, required by the change.

37 ARTICLE 37 DIFFERING SITE CONDITIONS

37.1 NOTICE IN WRITING

The Construction Manager shall promptly, and where possible before conditions are disturbed, give the Architect/Engineer and the Principal Representative Notice in writing of:

- 37.1.1 Subsurface or latent physical conditions at the site differing materially from those indicated in or reasonably assumed from the information provided in the Contract Documents; and,
- 37.1.2 Unknown physical conditions at the site, of an unusual nature, differing materially from those ordinarily encountered and generally recognized as inherent in Work of the character provided for in the Contract Documents.

The Architect/Engineer shall promptly investigate the conditions, and if it is found that such conditions do materially so differ and cause an increase or decrease in the Construction Manager's costs of performance of any part of the Work required by the Contract Documents, whether or not such Work is changed as a result of such conditions, an equitable adjustment shall be made and the Contract sum shall be modified in accordance with Article 35 of these General Conditions, Changes In The Work.

If the time required for completion of the Work affected by such materially differing conditions will extend the Work on the critical path as indicated on the CPM schedule, the time for completion shall also be equitably adjusted.

37.2 LIMITATIONS

No claim of the Construction Manager under this Article 37 shall be allowed unless the Construction Manager has given the Notice required in Section 37.1, Notice in Writing. The time prescribed for presentation and adjustment in Articles 36, Claims and 38, Delays And Extensions Of Time, shall be reasonably extended by the Principal Representatives to the extent required by the nature of the differing conditions; provided, however, that even when so extended no claim by the Construction Manager for an equitable adjustment hereunder shall be allowed if not quantified and presented prior to the date the Construction Manager requests a final inspection pursuant to Section 41.1 of these General Conditions, Notice Of Completion.

38 ARTICLE 38 DELAYS AND EXTENSIONS OF TIME

If the Construction Manager is delayed at any time in the progress of the Work by any act or neglect of the State of Colorado or the Architect/Engineer, or of any employee or agent of either, or by any separately employed Construction Manager or by strikes, lockouts, fire, unusual delay in transportation, unavoidable casualties or any other causes beyond the Construction Manager's control, including weather delays as defined below, the time of Completion of the Work shall be extended for a period equal to such portion of the period of delays directly affecting the completion of the Work as the Construction Manager shall be able to show they could not have avoided by the exercise of due diligence.

The Construction Manager shall provide Notice in writing to the Architect/Engineer, the Principal Representative and State Buildings Program within three (3) business days from the beginning of such delay and shall file a written claim for an extension of time within seven (7) business days after the period of such delay has ceased, otherwise, any claim for an extension of time is waived.

Provided that the Construction Manager has submitted reasonable schedules for approval when required by Article 12 of these General Conditions, Requests for Information and Schedules, if no schedule is agreed to fixing the dates on which the responses to requests for information or detail drawings will be needed, or Shop Drawings, Product Data or Samples are to be reviewed as required or allowed by Section 12.2, Schedules, no extension of time will be allowed for the

Architect/ Engineer's failure to furnish such detail drawings as needed, or for the failure to initially review Shop Drawings, Product Data or Samples, except in respect of that part of any delay in furnishing detail drawings or instructions extending beyond a reasonable period after written demand for such detailed drawings or instructions is received by the Architect/Engineer. In any event, any claim for an extension of time for such cause will be recognized only to the extent of delay directly caused by failure to furnish detail drawings or instructions or to review Shop Drawings, Product Data or Samples pursuant to schedule, after such demand.

All claims for extension of time due to a delay claimed to arise or result from ordered changes in the scope of the Work, or due to instructions claimed to increase the scope of the Work, shall be presented to the Architect/Engineer, the Principal Representative and State Buildings Program as part of a claim for extra cost, if any, in accordance with Article 36 of these General Conditions, Claims, and in accordance with the Change Order procedures required by Article 35 of these General Conditions, Changes In The Work.

Except as otherwise provided in this Article 38, no extension of time shall be granted when the Construction Manager has failed to utilize a CPM schedule or otherwise identify the Project's critical path as specified in Article 12 of these General Conditions, Requests for Information and Schedules, or has elected not to do so when allowed by the Supplementary General Conditions or the Specifications to use less sophisticated scheduling tools, or has failed to maintain such a schedule. Delay directly affecting the completion of the Work shall result in an extension of time only to the extent that completion of the Work was affected by impacts to the critical path shown on Construction Manager's CPM schedule. Where the circumstances make it indisputable in the opinion of the Architect/Engineer that the delay affected the completion of the Work so directly that the additional notice of the schedule impact by reference to a CPM schedule was unnecessary, a reasonable extension of time may be granted.

Extension of the time for completion of the Work will be granted for delays due to weather conditions only when the Construction Manager demonstrates that such conditions were more severe and extended than those reflected by the ten-year average for the month, as evidenced by the Climatological Data, U. S. Department of Commerce, for the Project area.

Extensions of the time for completion of the Work due to weather will be granted on the basis of one and three tenths (1.3) calendar days for every day that the Construction Manager would have Worked but was unable to Work, with each separate extension figured to the nearest whole calendar day.

For weather delays and delays caused by events, acts or omissions not within the control of the Principal Representative or any person acting on the Principal Representative's behalf, the Construction Manager shall be entitled to an extension of time only and shall not be entitled to recovery of additional cost due to or resulting from such delays. This Article 38 does not, however, preclude the recovery of damages for delay by either party under other provisions in the Contract Documents.

39 ARTICLE 39 NON-BINDING DISPUTE RESOLUTION – FACILITATED NEGOTIATIONS

The Construction Manager and Principal Representative agree to designate one or more mutually acceptable persons willing and able to facilitate negotiations and communications for the

resolution of conflicts, disagreements or disputes between them at the specific request of either party with regard to any Project decision of either of them or any decision of the Architect/Engineer. The designation of such person(s) shall not carry any obligation to use their services except that each party agrees that if the other party requests the intervention of such person(s) with respect to any such conflict, dispute or disagreement, the non-requesting party shall participate in good faith attempts to negotiate a resolution of the issue in dispute. If the parties cannot agree on a mutually acceptable person to serve in this capacity one shall be so appointed; provided, however, that either party may request the State Architect or their delegate to appoint such a person, who, if appointed, shall be accepted for this purpose by both the Construction Manager and the Principal Representative.

The cost, if any, of the facilitative services of the person(s) so designated shall be shared if the parties so agree in any partnering plan; or in the absence of agreement, the cost shall be borne by the party requesting the facilitation of negotiation.

Any dispute, claim, question or disagreement arising from or relating to the Contract or an alleged breach of the Contract may be subject to a request by either party for facilitated negotiation subject to the limitations hereafter listed, and the parties shall participate by consultation and negotiation with each other, as guided by the facilitator and with recognition of their mutual interests, in an attempt to reach an equitable solution satisfactory to both parties.

The obligation to participate in facilitated negotiations shall be as described above and elsewhere in these General Conditions, as by way of example in Article 36, Claims, or Article 34, Deductions for Uncorrected Work, and to the extent not more particularly described or limited elsewhere, each party's obligations shall be as follows:

- a) A party shall not initiate communication with the facilitator regarding the issues in dispute; except that any request for facilitation shall be made in writing with copies sent, faxed or delivered to the other party;
- b) A party shall prepare a brief written description of its position if so requested by the facilitator (who may elect to first discuss the parties' positions with each party separately in the interest of time and expense);
- c) A party shall respond to any reasonable request for copies of documents requested by the facilitator, but such requests, if voluminous, may consist of an offer to allow the facilitator access to the parties' documents;
- d) A party shall review any meeting agenda proposed by a facilitator and endeavor to be informed on the subjects to be discussed;
- e) A party shall meet with the other party and the facilitator at a mutually acceptable place and time, or, if none can be agreed to, at the time and place designated by the facilitator for a period not to exceed four hours unless the parties agree to a longer period;
- f) A party shall endeavor to assure that any facilitation meeting shall be attended by any other persons in their employ that the facilitator requests be present, if reasonably available, including the Architect/Engineer;
- g) Each party shall participate in such facilitated face-to-face negotiations of the issues in dispute through persons fully authorized to resolve the issue in dispute;

- h) Each party shall be obligated to participate in negotiations requested by the other party and to perform the specific obligations described in paragraphs (a) through (j) this Article 39, Facilitated Negotiation, no more than three times during the course of the Project;
- i) Neither party shall be under any obligation to resolve any issue by facilitated negotiation, but each agrees to participate in good faith and the Principal Representative shall direct the Architect/Engineer to appropriately document any resolution or agreement reached and to execute any Amendment or Change Order to the Contract necessary to implement their agreement; and,
- j) Any discussions and documents prepared exclusively for use in the negotiations shall be deemed to be matters pertaining to settlement negotiations and shall not be subsequently available in further proceedings except to the extent of any documented agreement.

In accordance with State Fiscal Rules and Section 52.7 of these General Conditions, Prohibited Terms, nothing in this Article 39 shall be deemed to call for arbitration or otherwise obligate the State to participate in any form of binding alternative dispute resolution.

A partnering plan developed as described in Section 2.4 of these General Conditions, Partnering, Communications and Cooperation, may modify or expand the requirements of this Article but may not reduce the obligation to participate in facilitated negotiations when applicable. In the case of small projects estimated to be valued under \$500,000, the requirements of this Article may be deleted from this Contract by modification in Section 7.5 of the Agreement (SC-6.5), Modification of Article 39. When so modified, the references to the parties' right to elect facilitated negotiation elsewhere in these General Conditions shall be deleted.

40 ARTICLE 40 RIGHT OF OCCUPANCY

The Principal Representative shall have the right to take possession of and to use any completed or partially completed portions of the Work, even if the time for completing the entire Work or portions of the Work has not expired and even if the Work has not been finally accepted, and the Construction Manager shall fully cooperate with the Principal Representative to allow such possession and use. Such possession and use shall not constitute an acceptance of such portions of the Work.

Prior to any occupancy of the Project, an inspection shall be made by the Principal Representative, the Architect/Engineer, State Buildings Program and the Construction Manager. Such inspection shall be made for the purpose of ensuring that the building is secure, protected by operation safety systems as designed, operable exits, power, lighting and HVAC systems, and otherwise ready for the occupancy intended and the Notice of Substantial Completion has been issued for the occupancy intended. The inspection shall also document existing finish conditions to allow assessment of any damage by occupants. The Construction Manager shall assist the Principal Representative in completing and executing State Form SBP-01, Approval of Occupancy/Use, prior to the Principal Representative's possession and use. Any and all areas so occupied will be subject to a final inspection when the Construction Manager complies with Article 41 of these General Conditions, Completion, Final Inspection, Acceptance and Settlement.

41 ARTICLE 41 COMPLETION, FINAL INSPECTION, ACCEPTANCE AND SETTLEMENT

41.1 NOTICE OF COMPLETION

When the Work, or a discrete physical portion of the Work (as hereafter described) which the Principal Representative has agreed to accept separately, is substantially complete and ready for final inspection, the Construction Manager shall file a written Notice with the Architect/Engineer that the Work, or such discrete physical portion, in the opinion of the Construction Manager, is substantially complete under the terms of the Contract. The Construction Manager shall prepare and submit with such Notice a comprehensive list of items to be completed or corrected prior to final payment, which shall be subject to review and additions as the Architect/Engineer or the Principal Representative shall determine after inspection. If the Architect/Engineer or the Principal Representative believe that any of the items on the list of items submitted, or any other item of Work to be corrected or completed, or the cumulative number of items of Work to be corrected or completed, will prevent a determination that the Work is substantially complete, those items shall be completed by the Construction Manager and the Notice shall then be resubmitted.

41.2 FINAL INSPECTION

Within ten (10) days after the Construction Manager files written Notice that the Work is substantially complete, the Architect/Engineer, the Principal Representative, and the Construction Manager shall make a "final inspection" of the Project to determine whether the Work is substantially complete and has been completed in accordance with the Contract Documents. State Buildings Program shall be notified of the inspection not less than three (3) business days in advance of the inspection. The Construction Manager shall provide the Principal Representative and the Architect/Engineer an updated Punch List in sufficient detail to fully outline the following:

- a) Work to be completed, if any; and
- b) Work not in compliance with the Drawings or Specifications, if any.

A final Punch List shall be made by the Architect/Engineer in sufficient detail to fully outline to the Construction Manager:

- a) Work to be completed, if any;
- b) Work not in compliance with the Drawings or Specifications, if any; and
- c) Unsatisfactory Work for any reason, if any.

The required number of copies of the final Punch List will be countersigned by the authorized representative of the Principal Representative and will then be transmitted by the Architect/Engineer to the Construction Manager, the Principal Representative, and State Buildings Program. The Architect/Engineer's final Punch List shall control over the Construction Manager's preliminary Punch List.

41.3 NOTICE OF SUBSTANTIAL COMPLETION

Notice of Substantial Completion shall establish the date of substantial completion of the Project. The Construction Manager acknowledges and agrees that because the departments, agencies and institutions of the State of Colorado are generally involved with the business of the public at large, greater care must be taken in establishing the date of substantial completion than might otherwise be the case to confirm that a project or building or discrete physical portion of the Work

is fully usable and safe for public use, and that such care necessarily raises the standard by which the concept of substantial completion is applied for a public building.

The Notice of Substantial Completion shall not be issued until the following have been fully established:

- 41.3.1 All required building code inspections have been called for and the appropriate code officials have affixed their signatures to the Building Inspection Record indicating successful completion of all required code inspections;
- 41.3.2 All required corrections noted on the Building Inspection Record shall have been completed unless the Architect/Engineer, the Principal Representative and State Buildings Program, in their complete and absolute discretion, all concur that the condition requiring the remaining correction is not in any way life threatening, does not otherwise endanger persons or property, and does not result in any undue inconvenience or hardship to the Principal Representative or the public;
- 41.3.3 The building, structure or Project can be fully and comfortably used by the Principal Representative and the public without undue interference by the Construction Manager's employees and workers during the completion of the final Punch List taking into consideration the nature of the public uses intended and taking into consideration any stage or level of completion of HVAC system commissioning or other system testing required by the Specifications to be completed prior to issuance of the Notice of Substantial Completion;
- 41.3.4 The Project has been fully cleaned as required by these General Conditions, and as required by any stricter requirements of the Specifications, and the overall state of completion is appropriate for presentation to the public; and
- 41.3.5 The Construction Manager has provided a schedule for the completion of each and every item identified on the Punch List which specifies the Subcontractor or trade responsible for the Work, and the dates the completion or correction of the item will be commenced and finished; such schedule will show completion of all remaining final Punch List items within the period indicated in the Contract for final Punch List completion prior to Final Acceptance, with the exception of only those items which are beyond the control of the Construction Manager despite due diligence. The schedule shall provide for a reasonable Punch List inspection process. Unless liquidated damages have been specified in Article 7.6 of the Agreement (SC-6.50), the cost to the Principal Representative, if any, for re-inspections due to failure to adhere to the Construction Manager's proposed punch-list completion schedule shall be the responsibility of the Construction Manager and may be deducted by the Principal Representative from final amounts due to the Construction Manager.

Substantial completion of the entire Project shall not be conclusively established by a decision of the Principal Representative to take possession and use of a portion, or all of the Project, where portions of the Project cannot meet all the criteria noted above. Notice of Substantial Completion for the entire Project shall, however, only be withheld for substantial reasons when the Principal Representative has taken possession and uses all of the Project in accordance with the terms of Article 40 of the General Conditions, Right of Occupancy. Failure to furnish the required completion schedule shall constitute a substantial reason for withholding the issuance of any Notice of Substantial Completion.

The Construction Manager shall have the right to request a final inspection of any discrete physical portion of the Project when in the opinion of the Principal Representative, the Architect/Engineer and State Buildings Program a final Punch List can be reasonably prepared, without confusion as to which portions of the Project are referred to in any subsequent Notice of Partial Final Settlement which might be issued after such portion is finally accepted. Discrete physical portions of the Project may be, but shall not necessarily be limited to, such portions of the Project as separate buildings where a Project consists of multiple buildings. Similarly, an addition to an existing building where the Project also calls for renovation or remodeling of the existing building may constitute a discrete physical portion of the Project. In such circumstances, when in the opinion of the Principal Representative, the Architect/Engineer and State Buildings Program, the requirements for issuance of a Notice of Substantial Completion can be satisfied with respect to the discrete portion of the Project, a partial Notice of Substantial Completion may be issued for such discrete physical portion of the Project.

41.4 NOTICE OF ACCEPTANCE

The Notice of Acceptance shall establish the completion date of the Project. It shall not be authorized until the Construction Manager shall have performed all of the Work to allow completion and approval of the Pre-Acceptance Checklist (SBP-05).

Where partial Notices of Substantial Completion have been issued, partial Notices of Final Acceptance may be similarly issued when appropriate for that portion of the Work. Partial Notice of Final Acceptance may also be issued to exclude the Work described in Change Orders executed during late stages of the Project where a later completion date for the Change Ordered Work is expressly provided for in the Contract as amended by the Change Order, provided the Work can be adequately described to allow partial advertisement of any Notice of Partial Final Settlement to be issued without confusion as to the Work included for which final payment will be made.

41.5 SETTLEMENT

Final payment and settlement shall be made on the date fixed and published for such payment except as hereafter provided. The Principal Representative shall not authorize final payment until all items on the Pre-Acceptance check list (SBP-05) have been completed, the Notice of Acceptance issued, and the Notice of Contractors Settlement published. If the Work shall be substantially completed, but Final Acceptance and completion thereof shall be prevented through delay in correction of minor defects, or unavailability of materials or other causes beyond the control of the Construction Manager, the Principal Representative in their discretion may release all amounts due to the Construction Manager except such amounts as may be in excess of three times the cost of completing the unfinished Work or the cost of correcting the defective Work, as estimated by the Architect/Engineer and approved by State Buildings Program. Before the Principal Representative may issue the Notice of Contractor's Settlement and advertise the Project for final payment, the Construction Manager shall have corrected all items on the Punch List except those items for which delayed performance is expressly permitted, subject to withholding for the cost thereof, and shall have:

41.5.1 Delivered to the Principal Representative:

- a) All guarantees and warranties;
- b) All statements to support local sales tax refunds, if any;
- c) Required operating maintenance instructions as per the Principal Representative; and,

- d) One (1) set of hard copy as-built Contract Documents, and one (1) electronic copy showing all job changes.
- e) Demonstrated to the operating personnel of the Principal Representative the proper operation and maintenance of all equipment.
- f) A written disclosure of the Five Most Costly Goods incorporated into the project, including iron, steel, or related manufactured goods and the total cost and country of origin of those five goods and whether the project was subject to any existing domestic content preferences.
- g) All approved project Environmental Product Declarations (EPDs) and waivers for products incorporated into the project in a zip folder.

41.5.2 Demonstrated to the operating personnel of the Principal Representative the proper operation and maintenance of all equipment.

41.5.3 Delivered to the State of Colorado Department of Personnel & Administration in accordance with the Colorado Procurement Code or the applicable procurement code for institutions of higher education:

A written disclosure of the five most costly goods incorporated into the project, including iron, steel, or related manufactured goods and the total cost and country of origin of those five goods and whether the project was subject to any existing domestic content preferences.

Upon completion of the foregoing the Project shall be advertised in accordance with the Notice of Contractor's Settlement by publications of Notice, the publication appearing at least ten (10) days prior to the time of final settlement. Publication and final settlement should not be postponed or delayed solely by virtue of unresolved claims against the Project or from Subcontractors, suppliers or materialmen based on good faith disputes; the resolution of the question of payment in such cases being directed by statute.

Except as hereafter provided, on the date of final settlement thus advertised, provided the Construction Manager has submitted a written Notice to the Architect/Engineer that no claims have been filed, and further provided the Principal Representative shall have received no claims, final payments and settlement shall be made in full. If any unpaid claim for labor, materials, rental machinery, tools, supplies or equipment is filed before payment in full of all sums due the Construction Manager, the Principal Representative and the State Controller (or comparable position at the contracting institution of higher education, where applicable) shall withhold from the Construction Manager on the date established for final settlement, sufficient funds to insure the payment of such claim, until the same shall have been paid or withdrawn, such payment or withdrawal to be evidenced by filing a receipt in full or an order for withdrawal signed by the claimant or their duly authorized agent or assignee. The amount so withheld may be in the amount of 125% of the claims or such other amount as the Principal Representative reasonably deems necessary to cover expected legal expenses. Such withheld amounts shall be in addition to any amount withheld based on the cost to compete unfinished Work or the cost to repair defective Work. However, as provided by statute, such funds shall not be withheld longer than ninety (90) days following the date fixed for final settlement with the Construction Manager, as set forth in the published Notice of Contractor's Settlement, unless an action at law shall be commenced within that time to enforce such unpaid claim and a Notice of such action at law shall have been filed with the Principal Representative and the State Controller (or comparable position at the contracting institution of higher education, where applicable). At the expiration of the

ninety (90) day period, the Principal Representative shall authorize the State Controller (or comparable position at the contracting institution of higher education, where applicable) to release to the Construction Manager all other money not the subject of such action at law or withheld based on the cost to complete unfinished Work or the cost to repair defective Work.

Notices of Partial Final Settlement may be similarly advertised, provided all conditions precedent have been satisfied as though that portion of the Work affected stood alone, a Notice of Partial Acceptance has been issued, and the consent of surety to the partial final settlement has been obtained in writing. Thereafter, partial final payments may be made to the Construction Manager subject to the same conditions regarding unpaid claims.

42 ARTICLE 42 GENERAL WARRANTY AND CORRECTION OF WORK AFTER ACCEPTANCE

The Construction Manager warrants that the materials used and the equipment furnished shall be new and of good quality unless specified to the contrary. The Construction Manager further warrants that the Work shall, in all respects, be free from material defects not permitted by the Specifications and shall be in accordance with the requirements of the Contract Documents. Neither the final certificate for payment nor any provision in the Contract Documents shall relieve the Construction Manager of responsibility for defects or faulty materials or Workmanship. The Construction Manager shall be responsible to the Principal Representative for such warranties for the longest period permitted by any applicable statute of limitations.

In addition to these general warranties, and without limitation of these general warranties, for a period of one year after the date of any Notice of Substantial Completion, or any Notice of Partial Substantial Completion if applicable, the Construction Manager shall remedy defects, and faulty Workmanship or materials, and Work not in accordance with the Contract Documents which was not accepted at the time of the Notice of Final Acceptance, all in accordance with the provisions of Article 44 of these General Conditions, One-Year Guarantee And Special Guarantees And Warranties.

43 ARTICLE 43 LIENS

Colorado statutes do not provide for any right of lien against public buildings. In lieu thereof, § 38-26-107 C.R.S., provides adequate relief for any claimant having furnished labor, materials, rental machinery, tools, equipment, or services toward construction of the particular public Work in that final payment may not be made to a Construction Manager until all such creditors have been put on Notice by publication in the public press of such pending payment and given opportunity for a period of up to ninety (90) days to stop payment to the Construction Manager in the amount of such claims.

44 ARTICLE 44 ONE-YEAR GUARANTEE AND SPECIAL GUARANTEES AND WARRANTIES

44.1 ONE-YEAR GUARANTEE OF THE WORK

The Construction Manager shall guarantee to remedy defects and repair or replace the Work for a period of one year from the date of the Notice of Substantial Completion or from the dates of any partial Notices of Substantial Completion issued for discrete physical portions of the Work. The Construction Manager shall remedy any defects due to faulty materials or Workmanship and

shall pay for, repair and replace any damage to other Work resulting there from, which shall appear within a period of one year from the date of such Notice(s) of Substantial Completion. The Construction Manager shall also remedy any deviation from the requirements of the Contract Documents which shall later be discovered within a period of one year from the date of the Notice of Substantial Completion; provided, however, that the Construction Manager shall not be required to remedy deviations from the requirements of the Contract Documents where such deviations were obvious, apparent and accepted by the Architect/Engineer or the Principal Representative at the time of the Notice of Final Acceptance. The Principal Representative shall give Notice of observed defects or other Work requiring correction with reasonable promptness. Such Notice shall be in writing to the Architect/Engineer and the Construction Manager.

The one year guarantee of the Construction Manager's Work may run separately for discrete physical portions of the Work for which partial Notices of Substantial Completion have been issued, however, it shall run from the last Notice of Substantial Completion with respect to all or any systems common to the Work to which more than one Notice of Substantial Completion may apply.

This one-year guarantee shall not be construed to limit the Construction Manager's general warranty described in Article 42 of these General Conditions, General Warranty and Correction of Work After Acceptance, that all materials and equipment are new and of good quality, unless specified to the contrary, and that the Work shall in all respects be free from material defects not permitted by the Specifications and in accordance with the requirements of the Contract Documents.

44.2 SPECIAL GUARANTEES AND WARRANTIES

In case of Work performed for which product, manufacturers or other special warranties are required by the Specifications, the Construction Manager shall secure the required warranties and deliver copies thereof to the Principal Representative through the Architect/Engineer upon completion of the Work.

These product, manufacturers or other special warranties, as such, do not in any way lessen the Construction Manager's responsibilities under the Contract. Whenever guarantees or warranties are required by the Specifications for a longer period than one year, such longer period shall govern.

45 ARTICLE 45 GUARANTEE INSPECTIONS AFTER COMPLETION

The Architect/Engineer, the Principal Representative and the Construction Manager together shall make at least two (2) complete inspections of the Work after the Work has been determined to be substantially complete and accepted. One such inspection, the "Six-Month Guarantee Inspection," shall be made approximately six (6) months after date of the Notice of Substantial Completion, unless in the case of smaller projects valued under \$500,000 this inspection is declined in Section 7.2, of the Agreement (SC-6.5), Modification of Article 45, in which case the inspection to occur at six months shall not be required. Another such inspection, the "Eleven-Month Guaranty Inspection" shall be made approximately eleven (11) months after the date of the Notice of Substantial Completion. The Construction Manager shall schedule and so notify all parties concerned, and the Principal Representative shall so notify State Buildings Program, of

these inspections. If more than one Notice of Substantial Completion has been issued at the reasonable discretion of the Principal Representative, separate eleven month inspections may be required where the one year guarantees do not run reasonably concurrent.

Written Punch Lists and reports of these inspections shall be made by the Architect/Engineer and forwarded to the Construction Manager, the Principal Representative, State Buildings Program, and all other participants within ten (10) days after the completion of the inspections. The Punch List shall itemize all guarantee items, prior Punch List items still to be corrected or completed and any other requirements of the Contract Documents to be completed which were not waived by final acceptance because they were not obvious or could not reasonably have been previously observed. The Construction Manager shall immediately initiate such remedial Work as may be necessary to correct any deficiencies or defective Work shown by this report, and shall promptly complete all such remedial Work in a manner satisfactory to the Architect/Engineer, the Principal Representative and State Buildings Program.

If the Construction Manager fails to promptly correct all deficiencies and defects shown by this report, the Principal Representative may do so, after giving the Construction Manager ten (10) days written Notice of intention to do so.

The State of Colorado, acting by and through the Principal Representative, shall be entitled to collect from the Construction Manager all costs and expenses incurred by it in correcting such deficiencies and defects, as well as all damages resulting from such deficiencies and defects.

46 ARTICLE 46 TIME OF COMPLETION AND LIQUIDATED DAMAGES

It is hereby understood and mutually agreed, by and between the parties hereto, that the date of beginning, rate of progress, and the time for completion of the Work to be done hereunder are ESSENTIAL CONDITIONS of this Agreement, and it is understood and agreed that the Work embraced in this Contract shall be commenced at the time specified in the Notice to Proceed (SC-7.261).

It is further agreed that time is of the essence of each and every portion of this Contract, and of any portion of the Work described on the Drawings or Specifications, wherein a definite and certain length of time is fixed for the performance of any act whatsoever. The parties further agree that where under the Contract additional time is allowed for the completion of the Work or any identified portion of the Work, the new time limit or limits fixed by such extension of the time for completion shall be of the essence of this Agreement.

The Construction Manager acknowledges that subject to any limitations in the Advertisement for Bids, issued for the Project, the Construction Manager's bid is consistent with and considers the number of days to substantially complete the Project and the number of days to finally complete the Project to which the parties may have stipulated in the Agreement, which stipulation was based on the Construction Manager's bid. The Construction Manager agrees that Work shall be prosecuted regularly, diligently and uninterruptedly at such rate of progress as will confirm the Project will be substantially complete, and fully and finally complete, as recognized by the issuance of all required Notices of Substantial Completion and Notices of Final Acceptance, within any times stipulated and specified in the Agreement, as the same may be amended by Change

Order or other written modification, and that the Principal Representative will be damaged if the times of completion are delayed.

It is expressly understood and agreed, by and between the parties hereto, that the times for the Substantial Completion of the Work or for the final acceptance of the Work as may be stipulated in the Agreement, and as applied here and in Section 7.6 of the Agreement (SC-6.5), Modifications of Article 46, are reasonable times for these stages of completion of the Work, taking into such consideration all factors, including the average climatic range and usual industrial conditions prevailing in the locality of the building operations.

If the Construction Manager shall neglect, fail or refuse to complete the Work within the times specified in the Agreement, such failure shall constitute a breach of the terms of the Contract and the State of Colorado, acting by and through the Principal Representative, shall be entitled to liquidated damages for such neglect, failure or refusal, as specified in Section 7.6, of the Agreement (SC-6.5), Modification of Article 46.

The Construction Manager and the Construction Manager's Surety shall be jointly liable for and shall pay the Principal Representative, or the Principal Representative may withhold, the sums hereinafter stipulated as liquidated damages for each calendar day of delay until the entire Project is 1) substantially completed, and the Notice (or all Notices) of Substantial Completion are issued, 2) finally complete and accepted and the Notice (or all Notices) of Acceptance are issued, or 3) both. Delay in substantial completion shall be measured from the Date of the Notice to Proceed and delay in final completion and acceptance shall be measured from the Date of the Notice of Substantial Completion.

In the first instance, specified in Section 7.6.1 of the Agreement (SC-6.5), Modification of Article 46, liquidated damages, if any, shall be the amount specified therein, for each calendar day of delay beginning after the stipulated number of days for Substantial Completion from the date of the Notice to Proceed, until the date of the Notice of Substantial Completion. Unless otherwise specified in any Supplementary General Conditions, in the event of any partial Notice of Substantial Completion, liquidated damages shall accrue until all required Notices of Substantial Completion are issued.

In the second instance, specified in Section 7.6.2 of the Agreement (SC-6.5), Modification of Article 46, liquidated damages, if any, shall be the amount specified therein for each calendar day in excess of the number of calendar days specified in the Construction Manager's bid for the Project and stipulated in the Agreement to finally complete the Project (as defined by the issuance of the Notice of Acceptance) after the final Notice of Substantial Completion has been issued.

In the third instance, when so specified in both Sections 7.6.1 and 7.6.2 of the Agreement (SC-6.5), both types of liquidated damages shall be separately assessed where those delays have occurred.

The parties expressly agree that said amounts are a reasonable estimate of the presumed actual damages that would result from any of the breaches listed, and that any liquidated damages that are assessed have been agreed to in light of the difficulty of ascertaining the actual damages that would be caused by any of these breaches at the time this Contract was formed; the liquidated damages in the first instance representing an estimate of damages due to the inability to use the

Project; the liquidated damages in the second instance representing an estimate of damages due to the additional administrative, technical, supervisory and professional expenses related to and arising from the extended closeout period including delivery of any or all guarantees and warranties, the submittals of sales and use tax payment forms, the calling for the final inspection and the completion of the final Punch List.

The parties also agree and understand that the liquidated damages to be assessed in each instance are separate and distinct, although potentially cumulative, damages for the separate and distinct breaches of delayed substantial completion or final acceptance. Such liquidated damages shall not be avoided by virtue of the fact of concurrent delay caused by the Principal Representative, or anyone acting on behalf of the Principal Representative, but in such event the period of delay for which liquidated damages are assessed shall be equitably adjusted in accordance with Article 38 of these General Conditions, Delays and Extensions of Time.

47 ARTICLE 47 DAMAGES

If either party to this Contract shall suffer damage under this Contract in any manner because of any wrongful act or neglect of the other party or of anyone employed by either of them, Notice of Claim shall be made in writing to such other party within a ten working days after the first observance of such damage, except to the extent of damages liquidated for the Construction Manager's failure to achieve timely completion as set forth in Article 46 of these General Conditions, Time of Completion and Liquidated Damages, the Principal Representative shall be responsible for, and at their option may insure against, loss of use of any existing property not included in the Work, due to fire or otherwise, however caused. Notwithstanding the foregoing, or any other provision of this Contract, to the contrary, no term or condition of this contract shall be construed or interpreted as a waiver, express or implied, of any of the immunities, rights, benefits, protection, or other provisions of the Colorado Governmental Immunity Act, §24-10-101, *et seq.*, CRS, as now or hereafter amended. The parties understand and agree that liability for claims for injuries to persons arising out of negligence of the State of Colorado, its departments, institutions, agencies, boards, officials and employees is controlled and limited by the provisions of §24-101-101, *et seq.*, CRS, as now or hereafter amended and the risk management statutes, §24-30-1501, *et seq.*, CRS, as now or hereafter amended.

Notice of intent to file a claim under Article 47 shall be made in writing to the party liable within a reasonable time of the first observance of such damage, except that in the case of claims by the Principal Representative involving warranties against faulty Work or materials Notice shall be required only to the extent stipulated elsewhere in these General Conditions. Claims made to the Principal Representative involving extra cost or extra time arising by virtue of instructions to the Construction Manager to which Article 36 of these General Conditions, Claims, applies shall be made in accordance with Article 36 of these General Conditions. Other claims arising under the Contract involving extra cost or extra time which are made to the Principal Representative under this Article 47 shall also be made in accordance with the procedures of Article 36 of these General Conditions, whether or not arising by virtue of instructions to the Construction Manager; provided however that it shall not be necessary to first obtain or request a written judgment of the Architect/Engineer.

Provided written Notice of intent to file a claim is provided as required in the preceding paragraph, nothing in this Article 47 shall limit or restrict the rights of either party to bring an action at law

or to seek other relief to which either party may be entitled, including consequential damages, if any, and shall not be construed to limit the time during which any action might be brought. Nothing in these General Conditions shall be deemed to limit the period of time during which any action may be brought as a matter of contract, tort, warranty or otherwise, it being the intent of the parties to allow any and all actions at law or in equity for such periods as the law permits. All such rights shall, however be subject to the obligation to assert claims and to appeal denials pursuant to Article 36 of these General Conditions, Claims, where applicable.

48 ARTICLE 48 STATE'S RIGHT TO DO THE WORK; TEMPORARY SUSPENSION OF WORK; DELAY DAMAGES

48.1 STATE'S RIGHT TO DO THE WORK

If after receipt of Notice to do so, the Construction Manager should neglect to prosecute the Work properly or fail to perform any provision of the Contract, the Principal Representative, after a second seven (7) days' advance written Notice to the Construction Manager and the Surety and, without prejudice to any other remedy the Principal Representative may, take control of all or a portion of the Work, as the Principal Representative deems necessary and make good such deficiencies deducting the cost thereof from the payment then or thereafter due the Construction Manager, as provided in Article 30, Correction Of Work Before Acceptance and Article 33 of these General Conditions, Payments Withheld, provided, however, that the Architect/Engineer shall approve the amount charged to the Construction Manager by approval of the Change Order.

48.2 TEMPORARY SUSPENSION OF WORK

The Principal Representative, acting for itself or by and through the Architect/Engineer, shall have the authority to suspend the Work, either wholly or in part, for such period or periods as may be deemed necessary due to:

- a) Unsuitable weather;
- b) Faulty workmanship;
- c) Improper superintendence or project management;
- d) Construction Manager's failure to carry out orders or to perform any provision of the Contract Documents;
- e) Loss of, or restrictions to, appropriations; and
- f) Conditions, which may be considered unfavorable for the prosecution of the Work.

If it should become necessary to stop Work for an indefinite period, the Construction Manager shall store materials in such manner that they will not become an obstruction or become damaged in any way; and they shall take every precaution to prevent damage to or deterioration of the Work, provide suitable drainage and erect temporary structures where necessary.

Notice of suspension of Work shall be provided to the Construction Manager in writing stating the reasons therefore. The Construction Manager shall again proceed with the Work when so notified in writing.

The Construction Manager understands and agrees that the Principal Representative and State of Colorado cannot predict with certainty future revenues and could ultimately lack the revenue to fund the appropriations applicable to this Contract. The Construction Manager further

acknowledges and agrees that in such event that the Principal Representative may, upon Notice to the Construction Manager, suspend the Work in anticipation of a termination of the Contract for the convenience of the State, pursuant to Article 50 of these General Conditions, Termination for Convenience of State. If the Contract is not so terminated, the Contract sum and the Contract time shall be equitably adjusted at the time the Principal Representative directs the Work to be recommenced and gives Notice that the revenue to fund the appropriation is available.

48.3 DELAY DAMAGES

The Principal Representative shall be liable to the Construction Manager for the payment of any claim for extra costs, extra compensation or damages occasioned by hindrances or delays encountered in the Work only when and to the limited extent that such hindrance or delay is caused by an act or omission within the control of the Principal Representative, the Architect/Engineer or other persons or entities acting on behalf of the Principal Representative. Further, the Principal Representative shall be liable to the Construction Manager for the payment of such a claim only if the Construction Manager has provided required Notice of the delay or impact, or has presented its claim for an extension of time or claim of other delay or other impact due to changes ordered in the Work before proceeding with the changed Work. Except as otherwise provided, claims for extension of time shall be Noticed and filed in accordance with Article 38 of these General Conditions, Delays and Extensions of Time, within three (3) business days of the beginning of the delay with any claim filed within seven (7) days after the delay has ceased, or such claim is waived. Claims for extension of time or for other delay or other impact resulting from changes ordered in the Work shall be presented and adjusted as provided in Article 35 of these General Conditions, Changes in the Work.

49 ARTICLE 49 STATE'S RIGHTS TO TERMINATE CONTRACT

49.1 GENERAL

If the Construction Manager should be adjudged bankrupt, or if they should make a general assignment for the benefit of their creditors, or if a receiver should be appointed to take over their affairs, or if they should fail to prosecute their Work with due diligence and carry the Work forward in accordance with the construction schedule and the time limits set forth in the Contract Documents, or if they should fail to subsequently perform one or more of the provisions of the Contract Documents to be performed by them, the Principal Representative may serve written Notice on the Construction Manager and the Surety on performance and payment bonds, stating their intention to exercise one of the remedies hereinafter set forth and the grounds upon which the Principal Representative bases their right to exercise such remedy.

In such event, unless the matter complained of is satisfactorily cleared within ten (10) days after delivery of such Notice, the Principal Representative may, without prejudice to any other right or remedy, exercise one of such remedies at once, having first obtained the concurrence of the Architect/Engineer in writing that sufficient cause exists to justify such action.

49.2 CONDITIONS AND PROCEDURES

49.2.1 The Principal Representative may terminate the services of the Construction Manager, which termination shall take effect immediately upon service of Notice thereof on the Construction Manager and their Surety, whereupon the Surety shall have the right to take over and perform the Contract. If the Surety does not provide Notice to the Principal Representative of its intent to commence performance of the Contract within ten (10) days after delivery of the Notice of

termination, the Principal Representative may take over the Work, take possession of and use all materials, tools, equipment and appliances on the premises and prosecute the Work to completion by such means as they shall deem best. In the event of such termination of their service, the Construction Manager shall not be entitled to any further payment under the Contract until the Work is completed and accepted. If the Principal Representative takes over the Work and if the unpaid balance of the contract price exceeds the cost of completing the Work, including compensation for any damages or expenses incurred by the Principal Representative through the default of the Construction Manager, such excess shall be paid to the Construction Manager. If, however, the cost, expenses and damages as certified by the Architect/Engineer exceed such unpaid balance of the contract price, the Construction Manager and their Surety shall pay the difference to the Principal Representative.

49.2.2 The Principal Representative may require the Surety on the Construction Manager's bond to take control of the Work and see to it that all the deficiencies of the Construction Manager are made good, with due diligence within ten (10) days of delivery of Notice to the Surety to do so. As between the Principal Representative and the Surety, the cost of making good such deficiencies shall all be borne by the Surety. If the Surety takes over the Work, either by election upon termination of the services of the Construction Manager pursuant to Section 49.2.1 of this Article 49, State's Right To Terminate Contract, or upon instructions from the Principal Representative to do so, the provisions of the Contract Documents shall govern the Work to be done by the Surety, the Surety being substituted for the Construction Manager as to such provisions, including provisions as to payment for the Work, the times of completion and provisions of this Article 49 as to the right of the Principal Representative to do the Work or to take control of all or a portion of the Work.

49.2.3 The Principal Representative may take control of all or a portion of the Work and make good the deficiencies of the Construction Manager, or the Surety if the Surety has been substituted for the Construction Manager, with or without terminating the Contract, employing such additional help as the Principal Representative deems advisable in accordance with the provisions of Article 48.1, State's Right To Do The Work; Temporary Suspension Of Work; Delay Damages. In such event, the Principal Representative shall be entitled to collect from the Construction Manager and their Surety, or to deduct from any payment then or thereafter due the Construction Manager, the costs incurred in having such deficiencies made good and any damages or expenses incurred through the default of Construction Manager, provided the Architect/Engineer approves the amount thus charged to the Construction Manager. If the Contract is not terminated, a Change Order to the Contract shall be executed, unilaterally if necessary, in accordance with the procedures of Article 35, Changes in the Work.

49.3 ADDITIONAL CONDITIONS

If any termination by the Principal Representative for cause is later determined to have been improper, the termination shall be automatically converted to and deemed to be a termination by the Principal Representative for convenience and the Construction Manager shall be limited in recovery to the compensation provided for in Article 50, Termination for Convenience of State. Termination by the Construction Manager shall not be subject to such conversion.

50 ARTICLE 50 TERMINATION FOR CONVENIENCE OF STATE

50.1 NOTICE OF TERMINATION

The performance of Work under this Contract may be terminated, in whole or from time to time in part, by the State whenever for any reason the Principal Representative shall determine that such termination is in the best interest of State. Termination of Work hereunder shall be effected by delivery to the Construction Manager of a Notice of such termination specifying the extent to which the performance of Work under the Contract is terminated and the date upon which such termination becomes effective.

50.2 PROCEDURES

After receipt of the Notice of termination, the Construction Manager shall, to the extent appropriate to the termination, cancel outstanding commitments hereunder covering the procurement of materials, supplies, equipment and miscellaneous items. In addition, the Construction Manager shall exercise all reasonable diligence to accomplish the cancellation or diversion of all applicable outstanding commitments covering personal performance of any Work terminated by the Notice. With respect to such canceled commitments, the Construction Manager agrees to:

- 50.2.1 Settle all outstanding liabilities and all claims arising out of such cancellation of commitments, with approval or ratification of the Principal Representative, to the extent he or she may require, which approval or ratification shall be final for all purposes of this clause; and,
- 50.2.2 Assign to the State, in the manner, at the time, and to the extent directed by the Principal Representative, all of the right, title, and interest of the Construction Manager under the orders and subcontracts so terminated, in which case the State shall have the right, in its discretion, to settle or pay any or all claims arising out of the termination of such orders and subcontracts.

The Construction Manager shall submit their termination claim to the Principal Representative promptly after receipt of a Notice of termination, but in no event later than three (3) months from the effective date thereof, unless one or more extensions in writing are granted by the Principal Representative upon written request of the Construction Manager within such three-month period or authorized extension thereof. Upon failure of the Construction Manager to submit their termination claim within the time allowed, the Principal Representative may determine, on the basis of information available to him, the amount, if any, due to the Construction Manager by reason of the termination and shall thereupon pay to the Construction Manager the amount so determined.

Costs claimed, agreed to, or determined pursuant to the preceding and following paragraph shall be in accordance with the provisions of the Colorado Procurement Code or the applicable procurement code for institutions of higher education.

Subject to the preceding provisions, the Construction Manager and the Principal Representative may agree upon the whole or any part of the amount or amounts to be paid to the Construction Manager by reason of the termination under this clause, which amount or amounts may include any reasonable cancellation charges thereby incurred by the Construction Manager and any reasonable loss upon outstanding commitments for personal services which he or she is unable to cancel; provided, however, that in connection with any outstanding commitments for personal services which the Construction Manager is unable to cancel, the Construction Manager shall have

exercised reasonable diligence to divert such commitments to other activities and operations. Any such agreement shall be embodied in an Amendment to this Contract and the Construction Manager shall be paid the agreed amount.

The State may from time to time, under such terms and conditions as it may prescribe, make partial payments against costs incurred by the Construction Manager in connection with the termination portion of this Contract, whenever, in the opinion of the Principal Representative, the aggregate of such payments is within the amount to which the Construction Manager will be entitled hereunder.

The Construction Manager agrees to transfer title and deliver to the State, in the manner, at the time, and to the extent, if any, directed by the Principal Representative, such information and items which, if the Contract had been completed, would have been required to be furnished to the State, including:

- a) Completed or partially completed plans, Drawings and information; and,
- b) Materials or equipment produced or in process or acquired in connection with the performance of the Work terminated by the Notice.

Other than the above, any termination inventory resulting from the termination of the Contract may, with written approval of the Principal Representative, be sold or acquired by the Construction Manager under the conditions prescribed by and at a price or prices approved by the Principal Representative. The proceeds of any such disposition shall be applied in reduction of any payments to be made by the State to the Construction Manager under this Contract or shall otherwise be credited to the price or cost of Work covered by this Contract or paid in such other manners as the Principal Representative may direct. Pending final disposition of property arising from the termination, the Construction Manager agrees to take such action as may be necessary, or as the Principal Representative may direct, for the protection and preservation of the property related to this Contract which is in the possession of the Construction Manager and in which the State has or may acquire an interest.

Any disputes as to questions of fact, which may arise hereunder, shall be subject to the Remedies provisions of the Colorado Procurement Code or the applicable procurement code for institutions of higher education.

51 ARTICLE 51 CONSTRUCTION MANAGER'S RIGHT TO STOP WORK AND/OR TERMINATE CONTRACT

If the Work shall be stopped under an order of any court or other public authority for a period of three (3) months through no act or fault of the Construction Manager or of any one employed by him, then the Construction Manager may on seven (7) days' written Notice to the Principal Representative and the Architect/Engineer stop Work or terminate this Contract and recover from the Principal Representative payment for all Work executed, any losses sustained on any plant or material, and a reasonable profit only for the Work completed. If the Architect/Engineer shall fail to issue or otherwise act in writing upon any certificate for payment within ten (10) days after it is presented and received by the Architect/Engineer, as provided in Article 31, Applications For Payments, or if the Principal Representative shall fail to pay the Construction Manager any sum certified that is not disputed in whole or in part by the Principal Representative in writing to the

Construction Manager and the Architect/Engineer within thirty (30) days after the Architect/Engineer's certification, then the Construction Manager may on ten (10) days' written Notice to the Principal Representative and the Architect/Engineer stop Work and/or give written Notice of intention to terminate this Contract.

If the Principal Representative shall thereafter fail to pay the Construction Manager any amount certified by the Architect/Engineer and not disputed in writing by the Principal Representative within ten (10) days after receipt of such Notice, then the Construction Manager may terminate this Contract and recover from the Principal Representative payment for all Work executed, any losses sustained upon any plant or materials, and a reasonable profit only for the Work completed. The Principal Representative's right to dispute an amount certified by the Architect/Engineer shall not relieve the Principal Representative of the obligation to pay amounts not in dispute as certified by the Architect/Engineer.

52 ARTICLE 52 COLORADO SPECIAL PROVISIONS

52.1 CONTROLLER'S APPROVAL, C.R.S. § 24-30-202(1)

This contract shall not be valid until it has been approved by the Colorado State Controller or designee.

52.2 FUND AVAILABILITY, C.R.S. § 24-30-202(5.5)

Financial obligations of the State payable after the current fiscal year are contingent upon funds for that purpose being appropriated, budgeted, and otherwise made available.

52.3 GOVERNMENTAL IMMUNITY

Liability for claims for injuries to persons or property arising from the negligence of the State, its departments, boards, commissions committees, bureaus, offices, employees and officials shall be controlled and limited by the provisions of the Colorado Governmental Immunity Act, §24-10-101, et seq., C.R.S.; the Federal Tort Claims Act, 28 U.S.C. Pt. VI, Ch. 171 and 28 U.S.C. 1346(b), and the State's risk management statutes, §§24-30-1501, et seq. C.R.S. No term or condition of this Contract shall be construed or interpreted as a waiver, express or implied, of any of the immunities, rights, benefits, protections, or other provisions, contained in these statutes.

52.4 INDEPENDENT CONTRACTOR

Contractor shall perform its duties hereunder as an independent Contractor and not as an employee. Neither Contractor nor any agent or employee of Contractor shall be deemed to be an agent or employee of the State. Contractor shall not have authorization, express or implied, to bind the State to any agreement, liability or understanding, except as expressly set forth herein. **Contractor and its employees and agents are not entitled to unemployment insurance or workers compensation benefits through the State and the State shall not pay for or otherwise provide such coverage for Contractor or any of its agents or employees. Contractor shall pay when due all applicable employment taxes and income taxes and local head taxes incurred pursuant to this Contract. Contractor shall (i) provide and keep in force workers' compensation and unemployment compensation insurance in the amounts required by law, (ii) provide proof thereof when requested by the State, and (iii) be solely responsible for its acts and those of its employees and agents.**

52.5 COMPLIANCE WITH LAW

Contractor shall comply with all applicable federal and State laws, rules, and regulations in effect or hereafter established, including, without limitation, laws applicable to discrimination and unfair employment practices.

52.6 CHOICE OF LAW, JURISDICTION, AND VENUE

Colorado law, and rules and regulations issued pursuant thereto, shall be applied in the interpretation, execution, and enforcement of this Contract. Any provision included or incorporated herein by reference which conflicts with said laws, rules, and regulations shall be null and void. All suits or actions related to this Contract shall be filed and proceedings held in the State of Colorado and exclusive venue shall be in the City and County of Denver.

52.7 PROHIBITED TERMS

Any term included in this Contract that requires the State to indemnify or hold Contractor harmless; requires the State to agree to binding arbitration; limits Contractor's liability for damages resulting from death, bodily injury, or damage to tangible property; or that conflicts with this provision in any way shall be void ab initio. Nothing in this Contract shall be construed as a waiver of any provision of §24-106-109, C.R.S.

52.8 SOFTWARE PIRACY PROHIBITION. SOFTWARE PIRACY PROHIBITION

State or other public funds payable under this Contract shall not be used for the acquisition, operation, or maintenance of computer software in violation of federal copyright laws or applicable licensing restrictions. Contractor hereby certifies and warrants that, during the term of this Contract and any extensions, Contractor has and shall maintain in place appropriate systems and controls to prevent such improper use of public funds. If the State determines that Contractor is in violation of this provision, the State may exercise any remedy available at law or in equity or under this Contract, including, without limitation, immediate termination of this Contract and any remedy consistent with federal copyright laws or applicable licensing restrictions.

52.9 EMPLOYEE FINANCIAL INTEREST/CONFLICT OF INTEREST

C.R.S. § 24-18-201 and C.R.S. § 24-50-507

The signatories aver that to their knowledge, no employee of the State has any personal or beneficial interest whatsoever in the service or property described in this contract. Contractor has no interest and shall not acquire any interest, direct or indirect, that would conflict in any manner or degree with the performance of Contractor services and Contractor shall not employ any person having such known interests.

52.10 VENDOR OFFSET AND ERRONEOUS PAYMENTS

C.R.S. § 24-30-202(1) & C.R.S. § 24-30-202.4

Subject to §24-30-202.4(3.5), C.R.S., the State Controller may withhold payment under the State's vendor offset intercept system for debts owed to State agencies for: (i) unpaid child support debts or child support arrearages; (ii) unpaid balances of tax, accrued interest, or other charges specified in §§39-21-101, et seq., C.R.S.; (iii) unpaid loans due to the Student Loan Division of the Department of Higher Education; (iv) amounts required to be paid to the Unemployment Compensation Fund; and (v) other unpaid debts owing to the State as a result of final agency determination or judicial action. The State may also recover, at the State's discretion, payments made to Contractor in error for any reason, including, but not limited to, overpayments or improper payments, and unexpended or excess funds received by Contractor by deduction from subsequent payments under this Contract, deduction from any payment due under any other

contracts, grants or agreements between the State and Contractor, or by any other appropriate method for collecting debts owed to the State.

53 ARTICLE 53 MISCELLANEOUS PROVISIONS

53.1 PROFESSIONAL ASSOCIATION PERMITTED

The Contractor may, with the prior written consent of the Principal Representative, join with him in the performance of this Agreement any other duly licensed Architect or Architects or registered Engineers with whom he may, in good faith, and enter into an association.

53.2 DISSOLUTION OF PROFESSIONAL ASSOCIATION

In the event there is dissolution of the association, other than by death of a member, the State of Colorado, acting by and through the Principal Representative, shall designate which former member shall continue with the work and may make all payments thereafter falling due in connection with the work directly to the person or persons so designated and without being required to look to the application of such payments as among the former members.

53.3 WAGE RATES, in accordance with C.R.S. § 24-30-1404 (1)

As amended, the Contractor has executed a schedule, which is attached hereto and made a part hereof by reference as **Exhibit B**, Wage Rates Schedule, and by doing so is certifying that wage rates and other factual unit costs supporting the compensation paid by the State for these professional services are accurate, complete and current.

The original contract price and any additions thereto shall be adjusted to exclude any significant sums by which the Principal Representative determines the contract price had been increased due to inaccurate, incomplete, or non-current wage rates and other factual unit costs. All such contract adjustments shall be made within one year following the end of this contract.

53.4 PUBLIC ART LAW

In recognition of the Public Art Law, C.R.S. § 24-48.5-312, as amended, if the State determines that this project is eligible for the acquisition of artworks in accordance with this law, the Contractor agrees to participate in the art selection process as an art jury member and to cooperate with and to advise the State in working with the commissioned artist(s) for this Capital Construction Project.

53.5 ASSIGNMENT

Contractor's rights and obligations under this Contract are personal and may not be transferred or assigned without the prior, written consent of the State. Any attempt at assignment or transfer without such consent shall be void. Any assignment or transfer of Contractor's rights and obligations approved by the State shall be subject to the provisions of this Contract.

53.6 SUBCONTRACTS

Contractor shall not enter into any subcontract in connection with its obligations under this Contract without the prior, written approval of the State. Contractor shall submit to the State a copy of each such subcontract upon request by the State. All subcontracts entered into by Contractor in connection with this Contract shall comply with all applicable federal and state laws and regulations, shall provide that they are governed by the laws of the State of Colorado, and shall be subject to all provisions of this Contract.

53.7 BINDING EFFECT

Except as otherwise provided in §53.5, all provisions of this Contract, including the benefits and burdens, shall extend to and be binding upon the Parties' respective successors and assigns.

53.8 AUTHORITY

Each Party represents and warrants to the other that the execution and delivery of this Contract and the performance of such Party's obligations have been duly authorized.

53.9 CAPTIONS AND REFERENCES

The captions and headings in this Contract are for convenience of reference only, and shall not be used to interpret, define, or limit its provisions. All references in this Contract to sections (whether spelled out or using the § symbol), subsections, exhibits or other attachments, are references to sections, subsections, exhibits or other attachments contained herein or incorporated as a part hereof, unless otherwise noted.

53.10 COUNTERPARTS

This Contract may be executed in multiple, identical, original counterparts, each of which shall be deemed to be an original, but all of which, taken together, shall constitute one and the same agreement.

53.11 ENTIRE UNDERSTANDING

This Contract represents the complete integration of all understandings between the Parties related to the Work, and all prior representations and understandings related to the Work, oral or written, are merged into this Contract. Prior or contemporaneous additions, deletions, or other changes to this Contract shall not have any force or effect whatsoever, unless embodied herein.

53.12 DIGITAL SIGNATURES

If any signatory signs this Contract using a digital signature in accordance with the Colorado State Controller Contract, Grant and Purchase Order Policies regarding the use of digital signatures issued under the State Fiscal Rules, then any agreement or consent to use digital signatures within the electronic system through which that signatory signed shall be incorporated into this Contract by reference.

53.13 MODIFICATION

Except as otherwise provided in this Contract, any modification to this Contract shall only be effective if agreed to in a formal amendment to this Contract, properly executed and approved in accordance with applicable Colorado State law and State Fiscal Rules. Modifications permitted under this Contract, other than contract amendments, shall conform to the policies issued by the Colorado State Controller.

53.14 STATUTES, REGULATIONS, FISCAL RULES AND OTHER AUTHORITY

Any reference in this Contract to a statute, regulation, State Fiscal Rule, fiscal policy or other authority shall be interpreted to refer to such authority then current, as may have been changed or amended since the Effective Date of this Contract.

53.15 EXTERNAL TERMS AND CONDITIONS

Notwithstanding anything to the contrary herein, the State shall not be subject to any provision included in any terms, conditions, or agreements appearing on Contractor's or a Subcontractor's website or any provision incorporated into any click-through or online agreements related to the Work unless that provision is specifically referenced in this Contract.

53.16 SEVERABILITY

The invalidity or unenforceability of any provision of this Contract shall not affect the validity or enforceability of any other provision of this Contract, which shall remain in full force and effect, provided that the Parties can continue to perform their obligations under this Contract in accordance with the intent of this Contract.

53.17 SURVIVAL AND CERTAIN CONTRACT TERMS

Any provision of this Contract that imposes an obligation on a Party after termination or expiration of this Contract shall survive the termination or expiration of this Contract and shall be enforceable by the other Party.

53.18 TAXES

The State is exempt from federal excise taxes under I.R.C. Chapter 32 (26 U.S.C., Subtitle D, Ch. 32) (Federal Excise Tax Exemption Certificate of Registry No. 84-730123K) and from State and local government sales and use taxes under §§39-26-704(1), et seq., C.R.S. (Colorado Sales Tax Exemption Identification Number 98-02565). The State shall not be liable for the payment of any excise, sales, or use taxes, regardless of whether any political subdivision of the state imposes such taxes on Contractor. Contractor shall be solely responsible for any exemptions from the collection of excise, sales or use taxes that Contractor may wish to have in place in connection with this Contract.

53.19 THIRD PARTY BENEFICIARIES

Except for the Parties' respective successors and assigns described in § 53.5, this Contract does not and is not intended to confer any rights or remedies upon any person or entity other than the Parties. Enforcement of this Contract and all rights and obligations hereunder are reserved solely to the Parties. Any services or benefits which third parties receive as a result of this Contract are incidental to this Contract, and do not create any rights for such third parties.

53.20 WAIVER

A Party's failure or delay in exercising any right, power, or privilege under this Contract, whether explicit or by lack of enforcement, shall not operate as a waiver, nor shall any single or partial exercise of any right, power, or privilege preclude any other or further exercise of such right, power, or privilege.

53.21 CORA DISCLOSURE

To the extent not prohibited by federal law, this Contract and the performance measures and standards required under §24-106-107, C.R.S., if any, are subject to public release through the CORA.

53.22 STANDARD AND MANNER OF PERFORMANCE

Contractor shall perform its obligations under this Contract in accordance with the highest standards of care, skill and diligence in Contractor's industry, trade, or profession.

53.23 LICENSES, PERMITS, AND OTHER AUTHORIZATIONS

Contractor shall secure, prior to the Effective Date, and maintain at all times during the term of this Contract, at its sole expense, all licenses, certifications, permits, and other authorizations required to perform its obligations under this Contract, and shall ensure that all employees, agents and Subcontractors secure and maintain at all times during the term of their employment, agency or subcontract, all license, certifications, permits and other authorizations required to perform their obligations in relation to this Contract.

53.24 INDEMNIFICATION

53.24.1 General Indemnification

Contractor shall indemnify, save, and hold harmless the State, its employees, agents and assignees (the "Indemnified Parties"), against any and all costs, expenses, claims, damages, liabilities, court awards and other amounts (including attorneys' fees and related costs) incurred by any of the Indemnified Parties in relation to any act or omission by Contractor, or its employees, agents, Subcontractors, or assignees in connection with this Contract.

53.24.2 Confidential Information Indemnification

Disclosure or use of State Confidential Information by Contractor in violation of Article 54 may be cause for legal action by third parties against Contractor, the State, or their respective agents. Contractor shall indemnify, save, and hold harmless the Indemnified Parties, against any and all claims, damages, liabilities, losses, costs, expenses (including attorneys' fees and costs) incurred by the State in relation to any act or omission by Contractor, or its employees, agents, assigns, or Subcontractors in violation of Article 54.

53.24.3 Intellectual Property Indemnification

Contractor shall indemnify, save, and hold harmless the Indemnified Parties, against any and all costs, expenses, claims, damages, liabilities, and other amounts (including attorneys' fees and costs) incurred by the Indemnified Parties in relation to any claim that any Deliverable, Good or Service, software, or Work Product provided by Contractor under this Contract (collectively, "IP Deliverables"), or the use thereof, infringes a patent, copyright, trademark, trade secret, or any other intellectual property right. Contractor's obligations hereunder shall not extend to the combination of any IP Deliverables provided by Contractor with any other product, system, or method, unless the other product, system, or method is (a) provided by Contractor or Contractor's subsidiaries or affiliates; (b) specified by Contractor to work with the IP Deliverables; (c) reasonably required in order to use the IP Deliverables in its intended manner and the infringement could not have been avoided by substituting another reasonably available product, system, or method capable of performing the same function; or (d) is reasonably expected to be used in combination with the IP Deliverables.

53.24.4 Accessibility Indemnification

Contractor shall indemnify, save, and hold harmless the state, its employees, agents and assignees (collectively, the "Indemnified Parties"), against any and all costs, expenses, claims, damages, liabilities, court awards and other amounts (including attorneys' fees and related costs) incurred by any of the Indemnified Parties in relation to Contractor's failure to comply with §§24-85-101, et seq., C.R.S., or the Accessibility Standards for Individuals with a Disability as established by the Office of Information Technology pursuant to Section §24-85-103 (2.5), C.R.S.

53.25 ACCESSIBILITY

53.25.1 Contractor shall comply with and the Work Product provided under this Contract shall be in compliance with all applicable provisions of §§24-85-101, et seq., C.R.S., and the Accessibility Standards for Individuals with a Disability, as established by the Governor's Office Of Information Technology (OIT), pursuant to Section §24-85-103 (2.5), C.R.S. Contractor shall also comply with all State of Colorado technology standards related to technology accessibility and with Level AA

of the most current version of the Web Content Accessibility Guidelines (WCAG), incorporated in the State of Colorado technology standards.

- 53.25.2 The State may require Contractor's compliance to the State's Accessibility Standards to be determined by a third party selected by the State to attest to Contractor's Work Product and software is in compliance with §§24-85-101, et seq., C.R.S., and the Accessibility Standards for Individuals with a Disability as established by the Office of Information Technology pursuant to Section §24-85-103 (2.5), C.R.S.

54 ARTICLE 54 CONFIDENTIAL INFORMATION-STATE RECORDS

54.1 CONFIDENTIALITY

Contractor shall keep confidential, and cause all Subcontractors to keep confidential, all State Records, unless those State Records are publicly available. Contractor shall not, without prior written approval of the State, use, publish, copy, disclose to any third party, or permit the use by any third party of any State Records, except as otherwise stated in this Contract, permitted by law or approved in writing by the State. Contractor shall provide for the security of all State Confidential Information in accordance with all policies promulgated by the Colorado Office of Information Security and all applicable laws, rules, policies, publications, and guidelines. If Contractor or any of its Subcontractors will or may receive the following types of data, Contractor or its Subcontractors shall provide for the security of such data according to the following: Contractor shall immediately forward any request or demand for State Records to the State's Principal Representative.

54.2 OTHER ENTITY ACCESS AND NONDISCLOSURE AGREEMENTS

Contractor may provide State Records to its agents, employees, assigns and Subcontractors as necessary to perform the Work, but shall restrict access to State Confidential Information to those agents, employees, assigns and Subcontractors who require access to perform their obligations under this Contract. Contractor shall ensure all such agents, employees, assigns, and Subcontractors sign agreements containing nondisclosure provisions at least as protective as those in this Contract, and that the nondisclosure provisions are in force at all times the agent, employee, assign or Subcontractor has access to any State Confidential Information. Contractor shall provide copies of those signed nondisclosure provisions to the State upon execution of the nondisclosure provisions if requested by the State.

54.3 USE, SECURITY, AND RETENTION

Contractor shall use, hold, and maintain State Confidential Information in compliance with any and all applicable laws and regulations only in facilities located within the United States, and shall maintain a secure environment that ensures confidentiality of all State Confidential Information. Contractor shall provide the State with access, subject to Contractor's reasonable security requirements, for purposes of inspecting and monitoring access and use of State Confidential Information and evaluating security control effectiveness. Upon the expiration or termination of this Contract, Contractor shall return State Records provided to Contractor or destroy such State Records and certify to the State that it has done so, as directed by the State. If Contractor is prevented by law or regulation from returning or destroying State Confidential Information, Contractor warrants it will guarantee the confidentiality of, and cease to use, such State Confidential Information.

54.4 INCIDENT NOTICE AND REMEDIATION

If Contractor becomes aware of any Incident, Contractor shall notify the State immediately and cooperate with the State regarding recovery, remediation, and the necessity to involve law enforcement, as determined by the State. Unless Contractor can establish that Contractor and its Subcontractors are not the cause or source of the Incident, Contractor shall be responsible for the cost of notifying each person who may have been impacted by the Incident. After an Incident, Contractor shall take steps to reduce the risk of incurring a similar type of Incident in the future as directed by the State, which may include, but is not limited to, developing and implementing a remediation plan that is approved by the State at no additional cost to the State. The State may adjust or direct modifications to this plan in its sole discretion, and Contractor shall make all modifications as directed by the State. If Contractor cannot produce its analysis and plan within the allotted time, the State, in its discretion, may perform such analysis and produce a remediation plan, and Contractor shall reimburse the State for the actual costs thereof. The State may, in its sole discretion and at Contractor's sole expense, require Contractor to engage the services of an independent, qualified, State-approved third party to conduct a security audit. Contractor shall provide the State with the results of such audit and evidence of Contractor's planned remediation in response to any negative findings.

54.5 DATA PROTECTION AND HANDLING

Contractor shall ensure that all State Records and Work Product in the possession of Contractor or any Subcontractors are protected and handled in accordance with the requirements of this Contract, including the requirements of any Exhibits hereto, at all times.

54.6 SAFEGUARDING PERSONAL IDENTIFIABLE INFORMATION (PII)

If Contractor or any of its Subcontractors will or may receive Personal Identifiable Information (PII) under this Contract, Contractor shall provide for the security of such PII, in a manner and form acceptable to the State, including, without limitation, State non-disclosure requirements, use of appropriate technology, security practices, computer access security, data access security, data storage encryption, data transmission encryption, security inspections, and audits. Contractor shall be a "Third-Party Service Provider" as defined in §24-73-103(1)(i), C.R.S. and shall maintain security procedures and practices consistent with §§24-73-101 et seq., C.R.S. In addition, as set forth in § 24-74-102, et. seq., C.R.S., Contractor, including, but not limited to, Contractor's employees, agents and Subcontractors, agrees not to share any PII with any third parties for the purpose of investigating for, participating in, cooperating with, or assisting with Federal immigration enforcement. If Contractor is given direct access to any State databases containing PII, Contractor shall execute, on behalf of itself and its employees, a certification as provided by the Office of the State Controller on an annual basis Contractor's duty and obligation to certify shall continue as long as Contractor has direct access to any State databases containing PII. If Contractor uses any Subcontractors to perform services requiring direct access to State databases containing PII, the Contractor shall require such Subcontractors to execute and deliver the certification to the State on an annual basis, so long as the Subcontractor has access to State databases containing PII.



STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM

DIRECT LABOR BURDEN CALCULATION

Institution/Agency: _____
Project No./Name: _____

This form is required to be submitted for review prior to execution of a construction agreement.

List items below by the percentage of what makes up the total labor overhead; Items include benefits that a contractor pays to employees on their payroll. Examples include taxes, pension cost, health and dental insurance etc. The Labor Burden percentage must be agreed to by both the contractor and Principal Representative and will be included in the contract as part of Exhibit A and will be used in the calculation of any future Change Order Proposals (SC-6.312) Line 2.

Major sub-contractors defined as electricians, plumbers, mechanical contractors, excavators, millwork, concrete, block layers etc. Please provide one (1) Labor Burden Calculation Sheet per contractor and for each sub-contractor. These labor burdens shall be used in the calculation of any future Change Order Proposals (SC-6.312) Line 10.

State reserves the right to require back-up confirmation of all information included in this calculation.

Contractor/Subcontractor Name:		
	Percent of Salary Paid	
Payroll Taxes		
Pension Costs		
Health Insurance		
Dental Insurance		
Life Insurance		
Other (Specify)		Description: _____
Other (Specify)		Description: _____
Total Labor Burden Percentage:	0%	

"General Decision Number: C020250025 03/07/2025

Superseded General Decision Number: C020240025

State: Colorado

Construction Type: Building

County: Mesa County in Colorado.

BUILDING CONSTRUCTION PROJECTS (does not include single family homes or apartments up to and including 4 stories).

Note: Contracts subject to the Davis-Bacon Act are generally required to pay at least the applicable minimum wage rate required under Executive Order 14026 or Executive Order 13658. Please note that these Executive Orders apply to covered contracts entered into by the federal government that are subject to the Davis-Bacon Act itself, but do not apply to contracts subject only to the Davis-Bacon Related Acts, including those set forth at 29 CFR 5.1(a)(1).

If the contract is entered into on or after January 30, 2022, or the contract is renewed or extended (e.g., an option is exercised) on or after January 30, 2022:	. Executive Order 14026 generally applies to the contract. . The contractor must pay all covered workers at least \$17.75 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on the contract in 2025.
If the contract was awarded on or between January 1, 2015 and January 29, 2022, and the contract is not renewed or extended on or after January 30, 2022:	. Executive Order 13658 generally applies to the contract. . The contractor must pay all covered workers at least \$13.30 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on that contract in 2025.

The applicable Executive Order minimum wage rate will be adjusted annually. If this contract is covered by one of the Executive Orders and a classification considered necessary for performance of work on the contract does not appear on this wage determination, the contractor must still submit a conformance request.

Additional information on contractor requirements and worker protections under the Executive Orders is available at <http://www.dol.gov/whd/govcontracts>.

Modification Number	Publication Date
0	01/03/2025
1	03/07/2025

ENGI0009-017 05/01/2024

	Rates	Fringes
POWER EQUIPMENT OPERATOR (Crane)		
141 tons and over.....	\$ 39.80	15.20
50 tons and under.....	\$ 35.78	15.20
51 to 90 tons.....	\$ 36.09	15.20
91 to 140 tons.....	\$ 37.34	15.20

IRON0024-009 11/01/2024

	Rates	Fringes
IRONWORKER, ORNAMENTAL.....	\$ 39.21	12.50

IRON0024-010 11/01/2024

	Rates	Fringes
IRONWORKER, STRUCTURAL.....	\$ 39.21	12.50

* PAIN0079-009 08/01/2024

	Rates	Fringes
PAINTER (Spray).....	\$ 27.41	11.56

PLUM0003-009 06/01/2024

	Rates	Fringes
PLUMBER (Excludes HVAC Duct, Pipe and Unit Installation).....	\$ 45.43	20.15

PLUM0208-009 06/01/2024

	Rates	Fringes
PIPEFITTER, Excludes HVAC Duct, Pipe and Unit Installation.....	\$ 44.15	22.43

SHEE0009-006 07/01/2024

	Rates	Fringes
SHEET METAL WORKER (Includes HVAC Duct and Unit Installation; Excludes HVAC Pipe Installation).....	\$ 39.47	21.78

* SUC02013-011 07/31/2015

	Rates	Fringes
BRICKLAYER.....	\$ 21.96	0.00
CARPENTER.....	\$ 20.53	0.00
CEMENT MASON/CONCRETE FINISHER...	\$ 21.44	10.23
ELECTRICIAN.....	\$ 25.63	9.51

INSULATOR - MECHANICAL (Duct, Pipe & Mechanical System Insulation).....	\$ 20.49	3.85
LABORER: Common or General.....	\$ 13.25 **	0.00
LABORER: Mason Tender - Brick...	\$ 15.99 **	0.00
LABORER: Mason Tender - Cement/Concrete.....	\$ 16.00 **	0.00
LABORER: Pipelayer.....	\$ 16.96 **	3.68
OPERATOR: Backhoe/Excavator/Trackhoe.....	\$ 20.78	5.78
OPERATOR: Bobcat/Skid Steer/Skid Loader.....	\$ 18.58	2.42
OPERATOR: Grader/Blade.....	\$ 21.50	0.00
PAINTER (Brush and Roller).....	\$ 19.56	2.05
PIPEFITTER (HVAC Pipe Installation Only).....	\$ 24.26	10.66
ROOFER.....	\$ 16.18 **	0.00
TRUCK DRIVER: Dump Truck.....	\$ 17.34 **	0.00

WELDERS - Receive rate prescribed for craft performing
operation to which welding is incidental.

=====

** Workers in this classification may be entitled to a higher minimum wage under Executive Order 14026 (\$17.75) or 13658 (\$13.30). Please see the Note at the top of the wage determination for more information. Please also note that the minimum wage requirements of Executive Order 14026 are not currently being enforced as to any contract or subcontract to which the states of Texas, Louisiana, or Mississippi, including their agencies, are a party.

Note: Executive Order (EO) 13706, Establishing Paid Sick Leave for Federal Contractors applies to all contracts subject to the Davis-Bacon Act for which the contract is awarded (and any solicitation was issued) on or after January 1, 2017. If this contract is covered by the EO, the contractor must provide employees with 1 hour of paid sick leave for every 30 hours they work, up to 56 hours of paid sick leave each year. Employees must be permitted to use paid sick leave for their own illness, injury or other health-related needs, including preventive care; to assist a family member (or person who is like family to the employee) who is ill, injured, or has other health-related needs, including preventive care; or for reasons resulting from, or to assist a family member (or person who is like family to the employee) who is a victim of, domestic violence, sexual assault, or stalking. Additional information on contractor requirements and worker protections under the EO is available at <https://www.dol.gov/agencies/whd/government-contracts>.

Unlisted classifications needed for work not included within the scope of the classifications listed may be added after award only as provided in the labor standards contract clauses (29CFR 5.5 (a) (1) (iii)).

The body of each wage determination lists the classifications and wage rates that have been found to be prevailing for the type(s) of construction and geographic area covered by the wage determination. The classifications are listed in alphabetical order under rate identifiers indicating whether the particular rate is a union rate (current union negotiated rate), a survey rate, a weighted union average rate, a state adopted rate, or a supplemental classification rate.

Union Rate Identifiers

A four-letter identifier beginning with characters other than ""SU"", ""UAVG"", ?SA?, or ?SC? denotes that a union rate was prevailing for that classification in the survey. Example: PLUM0198-005 07/01/2024. PLUM is an identifier of the union whose collectively bargained rate prevailed in the survey for this classification, which in this example would be Plumbers. 0198 indicates the local union number or district council number where applicable, i.e., Plumbers Local 0198. The next number, 005 in the example, is an internal number used in processing the wage determination. The date, 07/01/2024 in the example, is the effective date of the most current negotiated rate.

Union prevailing wage rates are updated to reflect all changes over time that are reported to WHD in the rates in the collective bargaining agreement (CBA) governing the classification.

Union Average Rate Identifiers

The UAVG identifier indicates that no single rate prevailed for those classifications, but that 100% of the data reported for the classifications reflected union rates. EXAMPLE: UAVG-OH-0010 01/01/2024. UAVG indicates that the rate is a weighted union average rate. OH indicates the State of Ohio. The next number, 0010 in the example, is an internal number used in producing the wage determination. The date, 01/01/2024 in the example, indicates the date the wage determination was updated to reflect the most current union average rate.

A UAVG rate will be updated once a year, usually in January, to reflect a weighted average of the current rates in the collective bargaining agreements on which the rate is based.

Survey Rate Identifiers

The ""SU"" identifier indicates that either a single non-union rate prevailed (as defined in 29 CFR 1.2) for this classification in the survey or that the rate was derived by computing a weighted average rate based on all the rates reported in the survey for that classification. As a weighted average rate includes all rates reported in the survey, it may include both union and non-union rates. Example: SUFL2022-007 6/27/2024. SU indicates the rate is a single non-union prevailing rate or a weighted average of survey data for that classification. FL indicates the State of Florida. 2022 is the

year of the survey on which these classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. The date, 6/27/2024 in the example, indicates the survey completion date for the classifications and rates under that identifier.

?SU? wage rates typically remain in effect until a new survey is conducted. However, the Wage and Hour Division (WHD) has the discretion to update such rates under 29 CFR 1.6(c)(1).

State Adopted Rate Identifiers

The "SA" identifier indicates that the classifications and prevailing wage rates set by a state (or local) government were adopted under 29 C.F.R 1.3(g)-(h). Example: SAME2023-007 01/03/2024. SA reflects that the rates are state adopted. ME refers to the State of Maine. 2023 is the year during which the state completed the survey on which the listed classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. The date, 01/03/2024 in the example, reflects the date on which the classifications and rates under the ?SA? identifier took effect under state law in the state from which the rates were adopted.

WAGE DETERMINATION APPEALS PROCESS

1) Has there been an initial decision in the matter? This can be:

- a) a survey underlying a wage determination
- b) an existing published wage determination
- c) an initial WHD letter setting forth a position on a wage determination matter
- d) an initial conformance (additional classification and rate) determination

On survey related matters, initial contact, including requests for summaries of surveys, should be directed to the WHD Branch of Wage Surveys. Requests can be submitted via email to davisbaconinfo@dol.gov or by mail to:

Branch of Wage Surveys
Wage and Hour Division
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

Regarding any other wage determination matter such as conformance decisions, requests for initial decisions should be directed to the WHD Branch of Construction Wage Determinations. Requests can be submitted via email to BCWD-Office@dol.gov or by mail to:

Branch of Construction Wage Determinations
Wage and Hour Division
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

2) If an initial decision has been issued, then any interested party (those affected by the action) that disagrees with the decision can request review and reconsideration from the Wage

and Hour Administrator (See 29 CFR Part 1.8 and 29 CFR Part 7). Requests for review and reconsideration can be submitted via email to dba.reconsideration@dol.gov or by mail to:

Wage and Hour Administrator
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

The request should be accompanied by a full statement of the interested party's position and any information (wage payment data, project description, area practice material, etc.) that the requestor considers relevant to the issue.

3) If the decision of the Administrator is not favorable, an interested party may appeal directly to the Administrative Review Board (formerly the Wage Appeals Board). Write to:

Administrative Review Board
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210.

=====
END OF GENERAL DECISION"



COLORADO

Office of the State Architect

Department of Personnel & Administration

Colorado Apprenticeship 2025 Contribution Rates

Table of Contents

International Brotherhood of Boilermakers, Iron Ship Builders, Blacksmiths, Forgers and Helpers	2
International Union of Bricklayers and Allied Craft Workers (CO/WY)	2
Carpet, Linoleum and Resilient Tile Layers (IUPAT).....	2
Glazier, Architectural Metal and Glass Workers, (IUPAT).....	2
Painters and Drywall Finishers (IUPAT).....	3
Operative Plasterers and Cement Masons International Association	3
International Brotherhood of Electrical Workers (IBEW)	3
International Union of Elevator Constructors.....	4
International Association of Heat and Frost Insulators and Allied Workers.....	4
International Association of Bridge, Structural, Ornamental, and Reinforcing Iron Workers.....	4
Laborers' International Union of North America (LIUNA)	4
International Union of Operating Engineers	4
Pipefitters (United Association-UA)	5
Plumbers & Pipefitters.....	5
Western Colorado Plumbers and Pipefitters	5
Plumbers (UA).....	5
United Union of Roofers, Water Proofers, and Allied Workers.....	6
Sheet Metal Workers International Association.....	6
Southwest Regional Council of Carpenters #255.....	6
Southwest Regional Council of Carpenters #555.....	6
Sprinkler fitters (UA).....	6
International Association of Bridge, Structural, Ornamental, and Reinforcing Iron Workers.....	7
Teamsters (IBTTJC).....	7

International Brotherhood of Boilermakers, Iron Ship Builders, Blacksmiths, Forgers and Helpers

- Local Union #101
- Geographic Region: Colorado
- Apprenticeship Rate: \$1.50 per hour

International Union of Bricklayers and Allied Craft Workers (CO/WY)

- Local Union #07
- Geographic Region: Colorado unless otherwise noted
- Apprenticeship Rate Refractory Projects: \$0.35 per hour
- Apprenticeship Rate Tile, Terrazzo, Marble Stone, Finishers: \$0.35 per hour
- Apprenticeship Rate Masonry - Northern Counties: \$0.30 per hour
- Apprenticeship Rate Masonry - Southern Counties: \$0.42 per hour

Northern Counties

Covering Northern Colorado Counties of Adams, Arapahoe, Boulder, Broomfield, Clear Creek, Denver, Douglas, Eagle, Garfield, Gilpin, Grand, Jackson, Jefferson, Larimer, Logan, Moffat, Morgan, Phillips, Pitkin, Rio Blanco, Routt, Sedgewick, Summit, Washington, Weld and Yuma counties.

Southern Counties

Covering Southern Colorado Counties of Alamosa, Archuleta, Baca, Bent, Chaffee, Cheyenne, Conejos, Costilla, Crowley, Custer, Delta, Dolores, El Paso, Elbert, Fremont, Gunnison, Hinsdale, Huerfano, Kiowa, Kit Carson, La Plata, Lake, Las Animas, Lincoln, Mesa, Mineral, Montezuma, Montrose, Otero, Ouray, Park, Prowers, Pueblo, Rio Grande, Saguache, San Juan, San Miguel and Teller counties

Carpet, Linoleum and Resilient Tile Layers (IUPAT)

- Local Union #419
- Geographic Region: Colorado
- Apprenticeship Rate: \$1.50 per hour

Glazier, Architectural Metal and Glass Workers, (IUPAT)

- Local Union #390
- Geographic Region: Colorado
- Apprenticeship Rate: \$0.80 per hour

Painters and Drywall Finishers (IUPAT)

- Local Union #79
- Geographic Region: Colorado
- Apprenticeship Rate: \$0.30

Operative Plasterers and Cement Masons International Association

- Local Union #577
- Geographic Region: Colorado
- Apprenticeship Rate: \$0.75

International Brotherhood of Electrical Workers (IBEW)

IBEW-Grand Junction Electrical Apprenticeship

- Local Union #111

Geographic Region	Region Description	Apprenticeship Rate (per hour)
Zone 1	Mesa, Delta, Montrose, Rio Blanco, Routt, Moffat, Garfield, Hinsdale Dolores, Gunnison, Montezuma, and La Plata Counties	\$0.84
Zone 2	Pitkin, San Miguel, San Juan, Ouray Counties	\$0.84
Zone 3	Mesa, Delta, Montrose, Garfield, Rio Blanco and Counties	\$0.84

IBEW #68

- Local Union #68
- Geographic Region: Adams; Arapahoe; Boulder; Broomfield; Clear Creak; Denver; Douglas; Eagle; Gilpin; Grand; Jackson; Jefferson; Lake; Larimer; Logan; Morgan; Phillips; Sedgwick; Summit; Washington; Weld and Yuma Counties
- Commercial Apprenticeship Rate: \$0.68
- Residential Apprenticeship Rates: \$0.17

IBEW #12

- Local Union #12
- Geographic Region: Adams; Arapahoe; Boulder; Broomfield; Clear Creak; Denver; Douglas; Eagle; Gilpin; Grand; Jackson; Jefferson; Lake; Larimer; Logan; Morgan; Phillips; Sedgwick; Summit; Washington; Weld and Yuma Counties

- Commercial Apprenticeship Rate: \$0.60
- Residential Apprenticeship Rate: \$0.23

IBEW-Colorado Springs Joint Electrical Apprenticeship

- Local Union #113
- Geographic Region: El Paso County
- Apprenticeship Rate: \$0.75 per hour

International Union of Elevator Constructors

- Local #25
- Geographic Region: Colorado
- Apprenticeship Rate: \$0.85 per hour

International Association of Heat and Frost Insulators and Allied Workers

- Local Union #28
- Geographic Region: Colorado
- Apprenticeship Rate: \$1.00 per hour

International Association of Bridge, Structural, Ornamental, and Reinforcing Iron Workers

- Local Union #24
- Geographic Region: Colorado
- Apprenticeship Rate Industrial: \$1.84 per hour
- Apprenticeship Rate Commercial: \$0.48 per hour

Laborers' International Union of North America (LIUNA)

- Local Union #720
- Geographic Region: Colorado
- Apprenticeship Rate: \$0.68

International Union of Operating Engineers

- Local Union #9
- Geographic Region: Colorado
- Apprenticeship Rate: \$1.00

Pipefitters (United Association-UA)

- Local Union #208
- Geographic Region: Denver & Northern Colorado
- Apprenticeship Rate Commercial: \$0.93 per hour
- Apprenticeship Rate Industrial: \$0.93 per hour
- Apprenticeship Rate Service: \$0.53 per hour

Plumbers & Pipefitters

- Local #58
- Geographic Region: Southern Colorado
- Apprenticeship Rate: \$1.80

Western Colorado Plumbers and Pipefitters

- Local Union #145
- Geographic Region: Western Colorado
- Apprenticeship Rate Commercial: \$0.80 per hour
- Apprenticeship Rate Industrial: \$0.50 per hour

Region Description:

Western Colorado, commencing at the Colorado New Mexico state lines, including the following counties: Archuleta, Hinsdale, Gunnison, Pitkin, and that portion of the Eagle County west of the line to and including the town of Edwards and northerly to the southwest corner of Routt County, Routt, Moffat, Rio Blanco, Garfield, Mesa, Delta, Montrose, Ouray, San Miguel, San Juan, Montezuma, La Plata and Dolores Counties.

Plumbers (UA)

- Local Union #3
- Geographic Region: Denver and Northern Colorado
- Apprenticeship Rate Commercial: \$0.95 per hour
- Apprenticeship Rate Industrial: \$0.95 per hour
- Apprenticeship Rate Pipe Tradesman: \$0.95 per hour
- Apprenticeship Rate Utility: \$0.95 per hour

United Union of Roofers, Water Proofers, and Allied Workers

- Local Union #58
- Geographic Region: Colorado
- Apprenticeship Rate: \$0.16

Sheet Metal Workers International Association

- Local Union #9
- Geographic Region: Denver, Colorado Springs, Grand Junction JATC

Year	Apprenticeship Rate (per hour)
1st year	\$1.30
2nd year	\$1.54
3rd year	\$1.66
4th year	\$1.90
Journeyman	\$2.37

Southwest Regional Council of Carpenters #255

- Local Union #255
- Geographic Region: Colorado
- Apprenticeship Rate: \$0.43

Southwest Regional Council of Carpenters #555

- Local Union #555
- Geographic Region: Colorado
- Apprenticeship Rate Statewide Building Construction: \$0.55 per hour
- Apprenticeship Rate Independent Drywall, Ceiling and Interior Systems and Millwright: \$0.55 per hour

Sprinkler fitters (UA)

- Local Union #669
- Geographic Region: Colorado
- Apprenticeship Rate: \$0.52

International Association of Bridge, Structural, Ornamental, and Reinforcing Iron Workers

- Local Union #847
- Geographic Region: Colorado
- Apprenticeship Rate: \$1.25

Teamsters (IBTTJC)

- Local Union #455
- Geographic Region: Colorado
- Apprenticeship Rate: \$0.50



Apprenticeship Utilization Certification (Public Projects of \$1 million or more)

Institution/Agency: _____

Project No./Name: _____

General Contractor: _____

For each trade listed below attach documentation that all firms identified participate in apprenticeship programs as described in the Certification Statement below.

Trade	Subcontractor	Union Certification
Mechanical		
Sheet Metal		
Fire Suppression		
Sprinkler Fitting		
Plumbing		
Electrical		

Certification Statement

§ 24-92-115, C.R.S. (SB 19-196)

The above named General Contractor certifies and agrees as follows:

That all firms identified above participate in apprenticeship programs registered with the United States Department of Labor's Employment and Training Administration or state apprenticeship councils recognized by the United States Department of Labor and have a proven record of graduating apprentices at a minimum of fifteen percent of its apprentices for at least three of the past five years. The General Contractor shall supply supporting documentation from the United States Department of Labor's office of apprenticeship verifying the certification.

The above documentation shall be made publicly available by the contracting agency through its website within thirty (30) days from when it is submitted.

The General Contractor shall agree to provide additional documentation to the contracting agency regarding affected apprenticeship training programs relating to the requirements above. If a contracting agency determines that a subcontractor has willfully

falsified documentation or willfully misrepresented their qualifications, the agency shall direct the General Contractor to terminate the subcontractor contract immediately and the subcontractor will be immediately removed from the public project. At the discretion of the Director of the Department of Personnel, the State may initiate the process to debar the General Contractor pursuant to § 24-109-105, C.R.S., and may pursue any other remedy provided by law.

CERTIFIED and AGREED to this _____ day of _____, 20____.

General Contractor:

Full Legal Name

By: _____




COLORADO MESA
UNIVERSITY

Program Plan for:

NEW PARKING STRUCTURE

within the Grand Junction Campus Interior

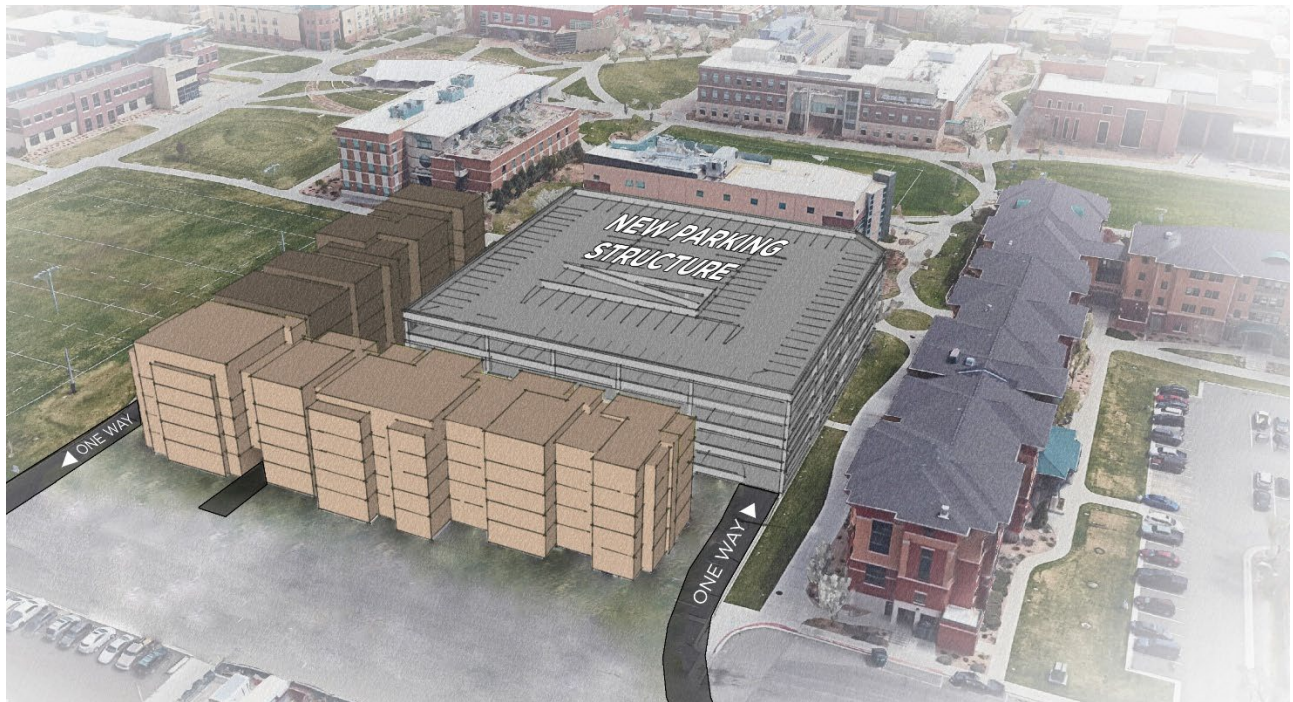

January 26, 2026

DESIGN
WEST

CONTRIBUTORS

Colorado Mesa University:

President John Marshall
Vice President for Finance & Administration Michelle Quinn
Vice President for Student Service Dr. Roberto Montoya
Vice President for Capital Planning, Sustainability and Campus Operations..... Kent Marsh
Vice President of External Relations Derek Wagner

Document Prepared By:

Design West Architects, Salt Lake City, Utah

Principal Authors Stephen Williams, Principal
Larry Hepworth, Principal-in-Charge
Blake Wright, President, Contract Principal

Graphics Stephen Williams, Principal

1 SUMMARY (January 2026)

1.1 Objective and Purpose:

As part of master-planning exercises in recent years and the diminishment of existing surface level parking available in the area of campus known as The Formation District, parking capacity on campus has lessened from Colorado Mesa University implementing and the further developing and expanding the campus at Grand Junction. CMU now intends to take steps to go vertical with the construction of a 500 stall parking structure.

1.2 Project Site

The property is situated with the Rugby Pitch to the north, Bunting Avenue Student Housing to the south, the Fine Arts Building to the east, and the new (under construction) **Formation Food Hall** to the west.


A prospective student housing project if approved on the same property will be built in two phases, first a north-south wing on the west side of the parking structure, then a second east-west phase connecting to the first phase on the north side of the parking structure, between the parking structure and the Rugby pitch on the north.

This site itself is an existing asphalt paved parking lot.

Considerations for the Parking Structure design should include:

- Maximum of 5 levels of parking
 - Approximately 100 stalls per level
 - Parking structure should not exceed the height of the surrounding buildings
- Maximum of 12' floor to floor
 - Floor to floor efficiency is dependent on the structural system used
 - A goal for a minimum of 8'-2" overhead clearance is desired for van-accessible vehicles.
- Elevator at one location serving all 5 levels with an adjacent stair
- A second stair on the opposite side of the parking structure
- The current intent is for the structure to be open-air as it is with the two parking structures existing on campus.
- Because of its proposed location and it's adjacency to both existing student housing and planned student housing, screening and exterior aesthetic should be given strong consideration.

- If geotechnical analysis merits it, and water table is sufficiently low, the parking structure can be sunken to reduce the building height up to one full level.
- Exterior Finishes
 - Precedents of surrounding structures should be considered in incorporating the vernacular fabric of the new parking structure's surroundings.
 - Consider using screening panels particularly on the elevations that front current and/or future housing elevations.
 - Exterior beams that also serve as vehicular barriers, should be of sufficient height to occlude head lights from shining into adjacent buildings and should be tall enough to provide safety for parking structure users.

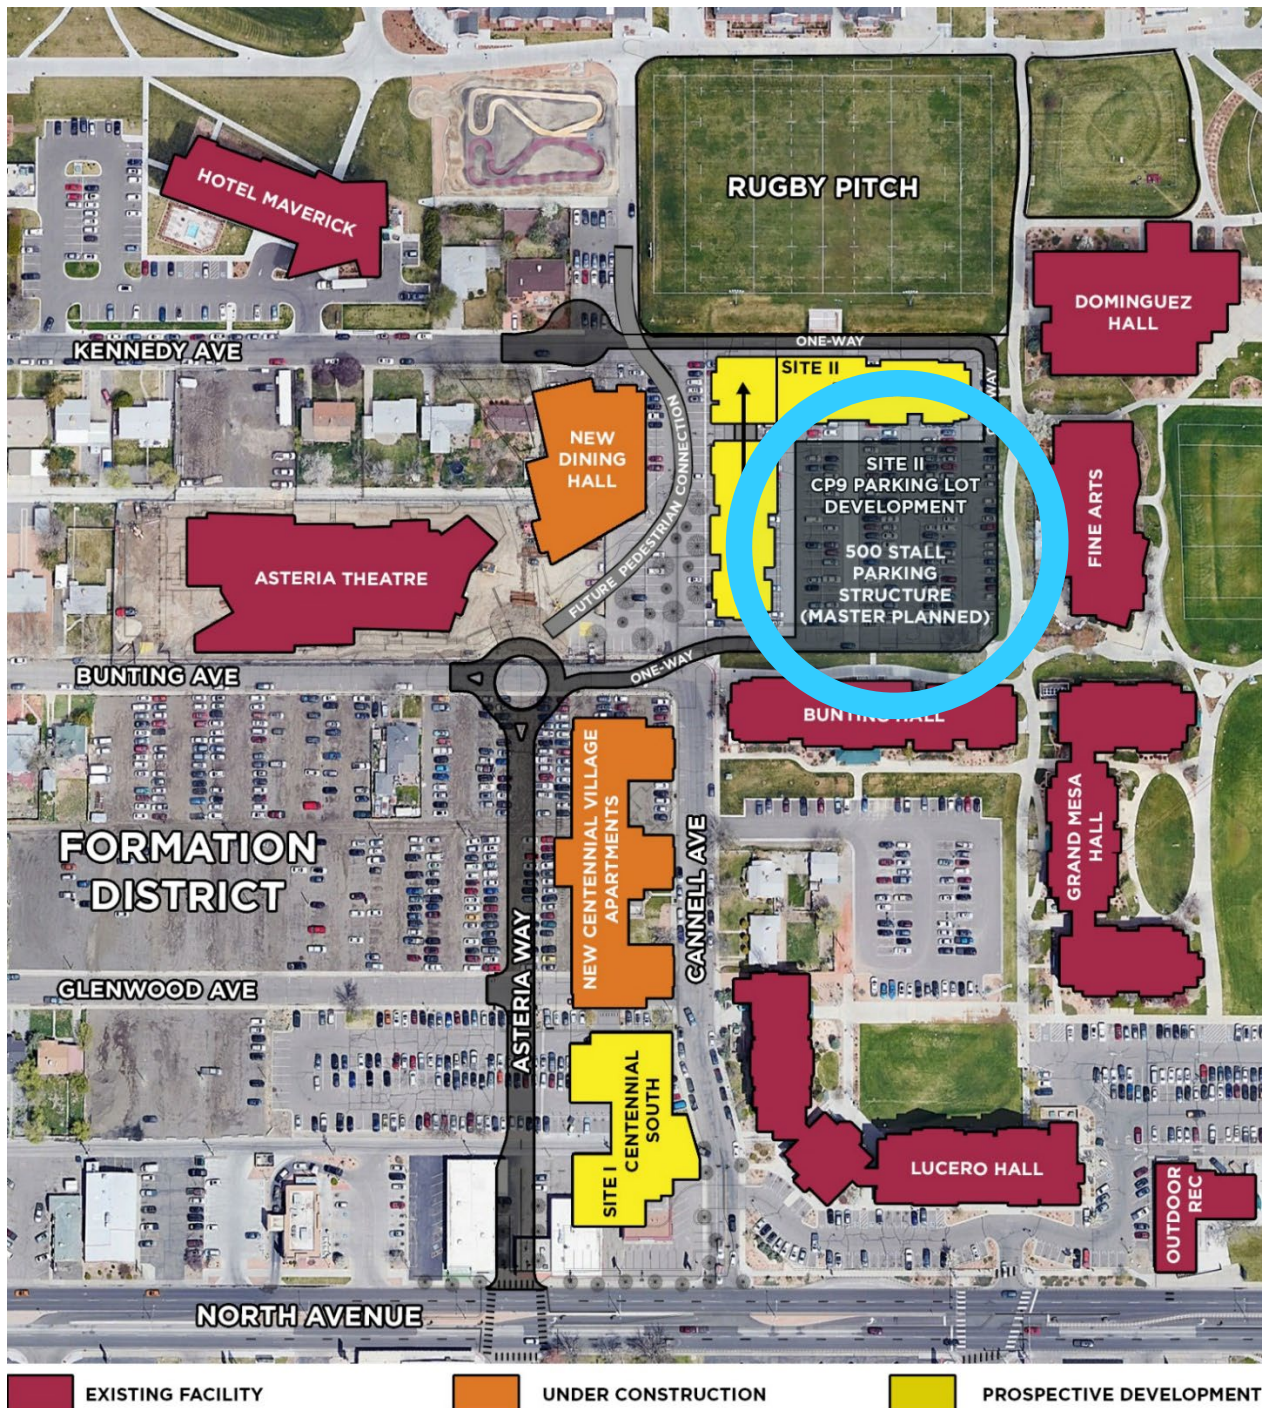

Access to the planned Parking Structure is onto a one-way entrance off the first exit of the roundabout from Asteria Way, and the second exit from Bunting Avenue. The exit from the parking structure is also one-way and exists to the north, east of the planned Phase 2 housing east-west wing, and then along the north side, south of the rugby pitch and onto Kennedy Avenue to exit.

Should someone unintentionally take the one-way road from the roundabout, they will have a small window to exit the parking structure without incurring a fee.

1.3 Parking Structure Type


The following are parking structure types:

- Long Plan Post Tension (PT)
- Short Span Post Tension (PT)
- Precast
- Composite Steel (Steel and Composite Deck)
- Hybrid (Steel and PT)
- Shallow Beam Post Tension (PT)

Current parking structure precedent on campus appears to be **Precast**, namely CP11 (University Center) and CP1 (Commuter Parking).

Should the campus deviate from this precedent, the case should be made for the benefit of an alternative weighing pros and cons of the alternative including but not limited to effects on local economy, availability of required materials, life-cycle costs, maintenance, etc.

1.4 Schematic Plan

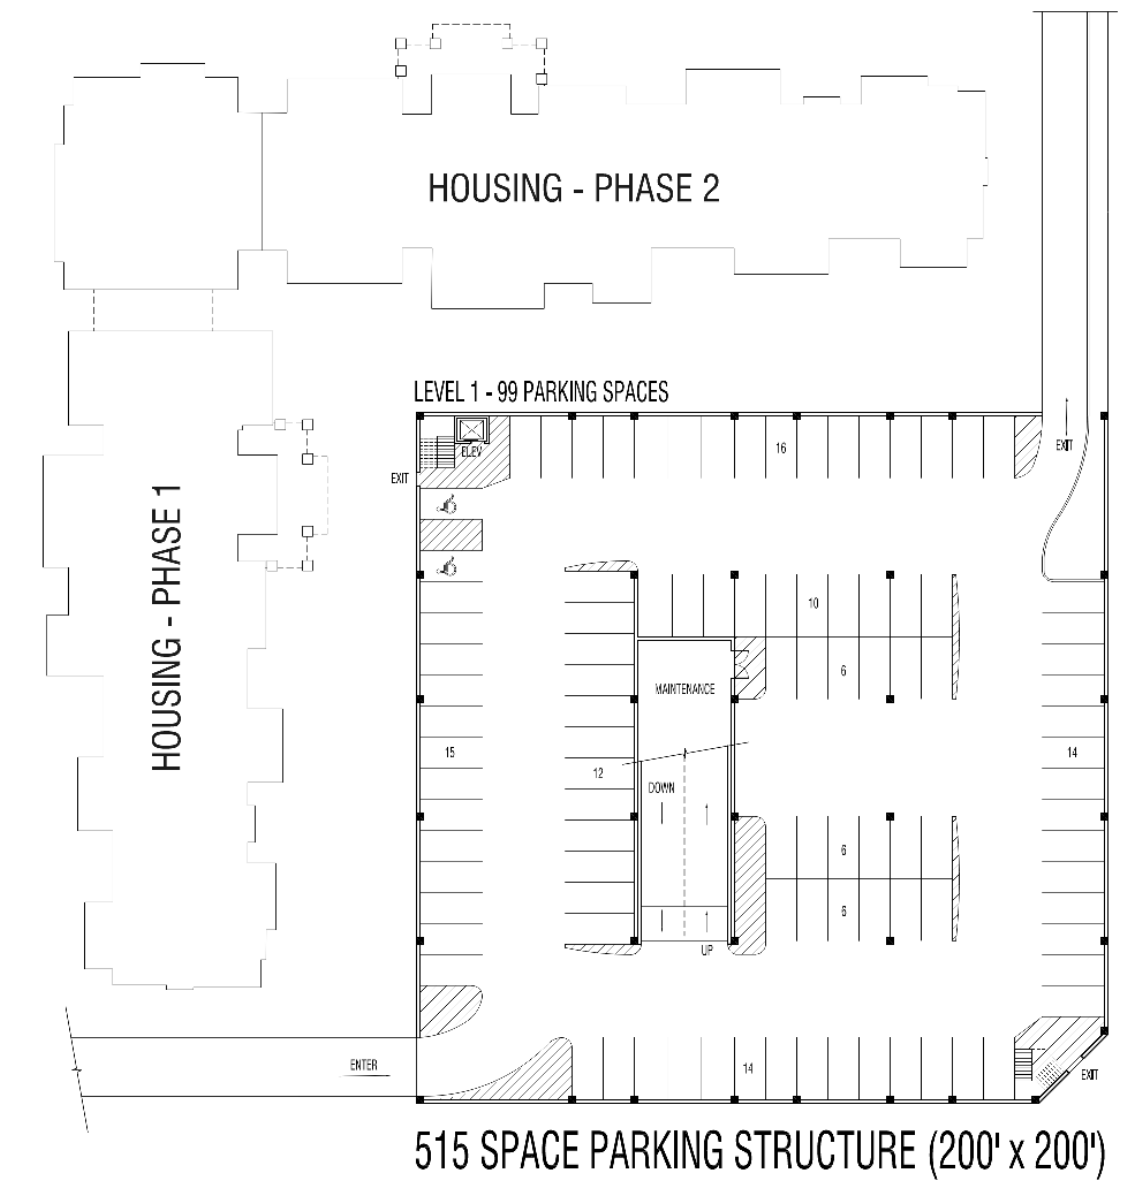


The example plans on the previous page and to the right have 3+ level parking platforms. Double loaded aisles with 2-way traffic are the most efficient design for maximizing parking.


This example has an interior two-way ramp connecting each level. A driver seeking a parking space on each level will be able to determine if there is any open parking in a singular loop around each platform level and then can continue upward to the next level after completing the loop and finding the level full.


The placement of the elevator is away from the entrance and exit to the structure, however is close to a pedestrian path leading to a breezway planned for the student housing on the west which further connects them to the Formation Food Hall and the Asteria Theatre.

103 PARKING SPACES - LEVELS 2-4

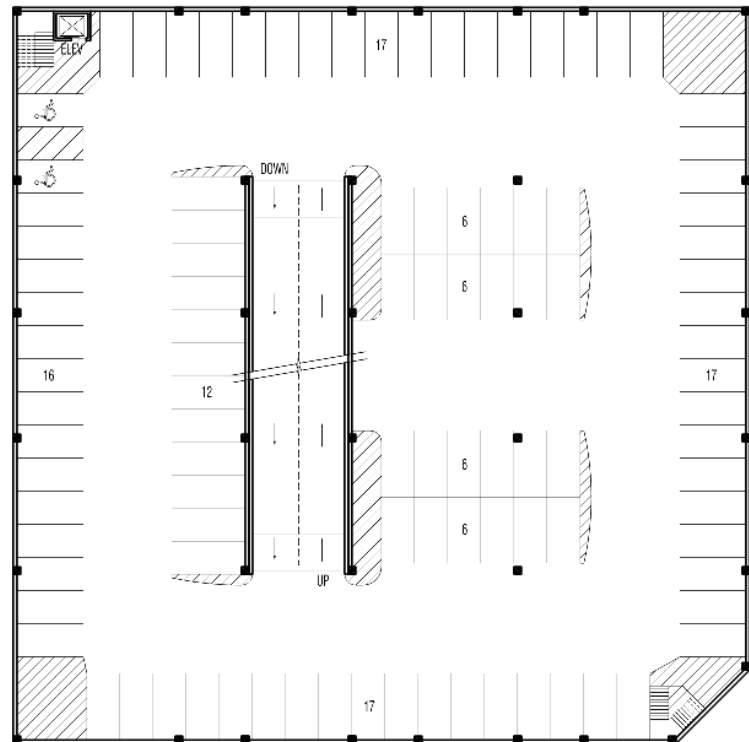


107 PARKING SPACES

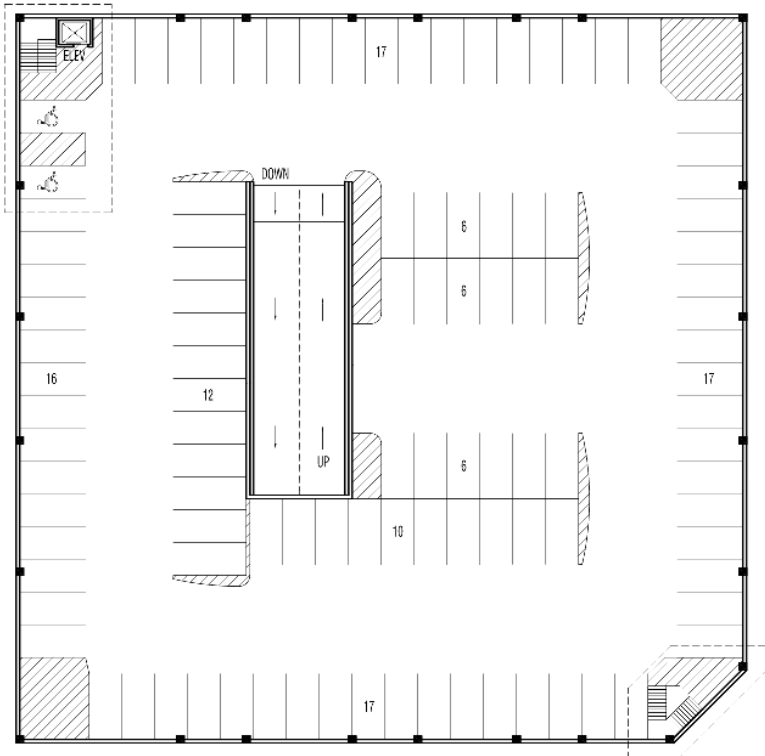

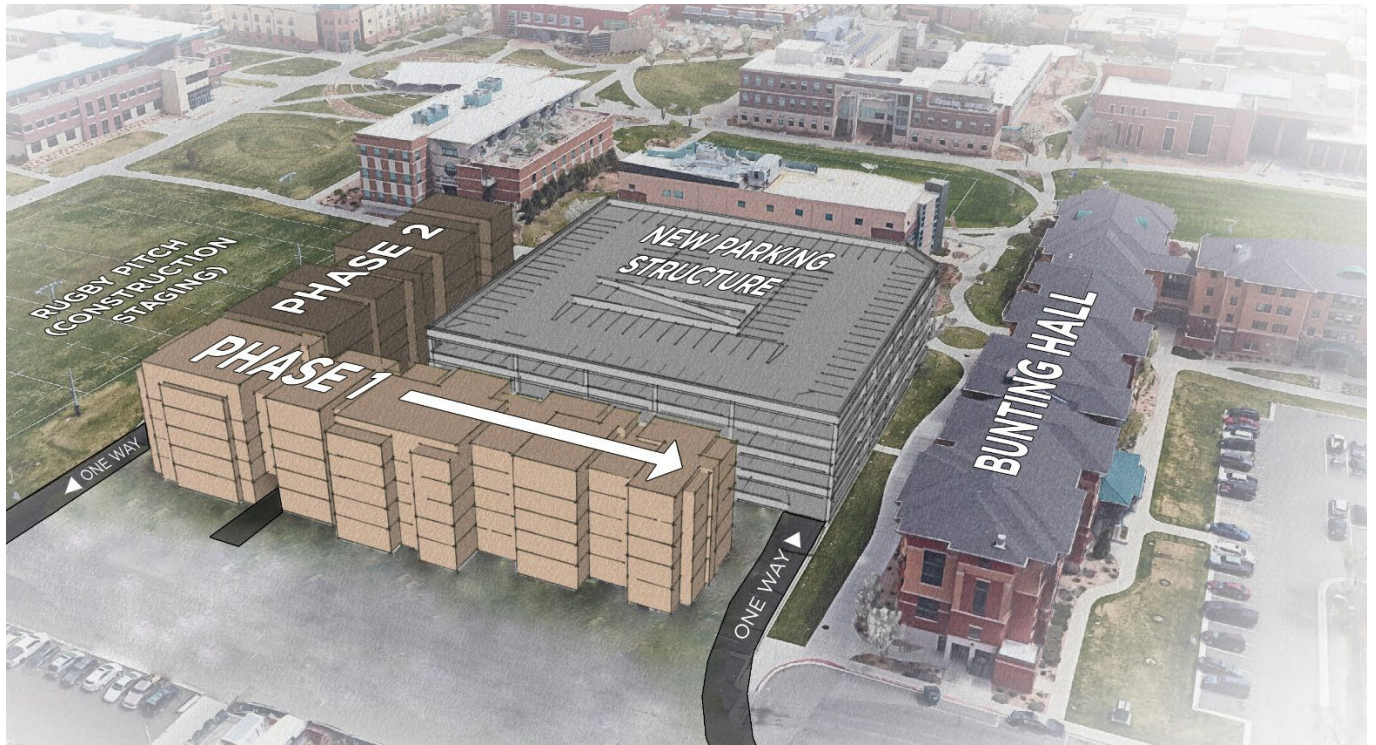

Rendering 1 – New Parking Structure Schematic Model with Two Phases of Future Housing, Ph. 1 on the West, Ph. 2 on the North

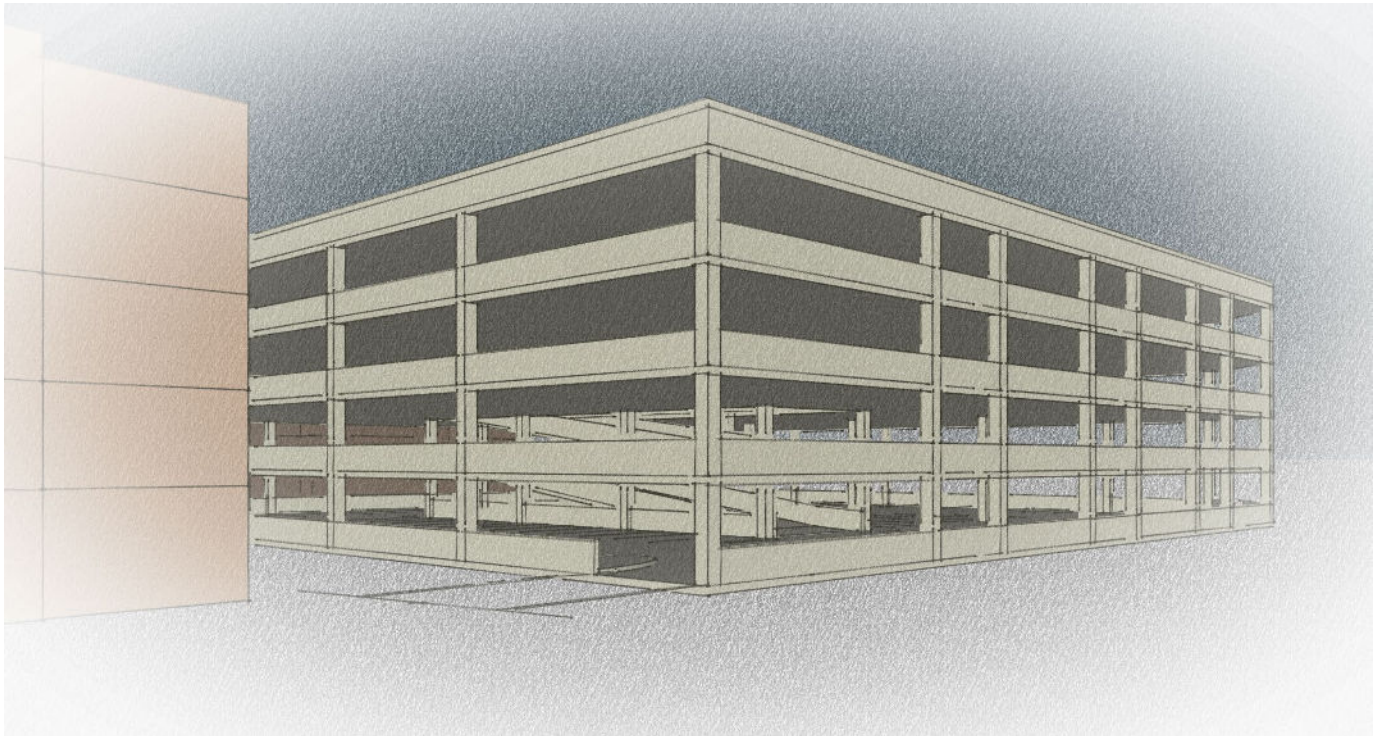

Rendering 2 – New Parking Structure Schematic Model

UNDERSTANDING & JUSTIFICATION

Colorado Mesa University is one of Colorado's premier institutions of higher education, with a tri-partite mission in providing baccalaureate and graduate programs as a state-wide institution, as a regional community college, and as a county-wide provider of vocational programs.

1.5 Undergraduate Growth: Multi-Year Effect

Enrollment at CMU continues to increase year over year and demand for on-campus housing has not slowed, especially with the current high cost and scarcity of affordable housing opportunities for students competing with the public in the surrounding area for off-campus housing. It is understood that the City of Grand Junction has approved several multi-unit apartment or housing complex that could privately serve for off-campus housing for students and public alike for a few years. However, the current high rental costs have placed a strain on affordable housing offerings for a growing student population thus placing a higher demand for on-campus housing that presents a more affordable solution.

CMU has determined that student experience and retention is critical and on campus housing and extracurricular programs and events play a huge part in the formula for students' success and retention. In house studies have shown that CMU has a high rate of Freshman to Sophomore retention. The same can be stated for upperclassman retention. With the challenges of off-campus housing cost and public demand for affordable housing for all CMU Students, it has driven the requirement for additional on campus housing to meet the overriding goals for high quality, value-based education and a great college student experience.

1.6 Current Projected Growth Model and Assumptions

With the continued build-out of the campus master plan due to continued growth, with each building constructed on campus, classroom, student housing, arts venues or otherwise, ground level parking lots diminish as theirs is the easiest on which to develop. With density of building increasing on campus as a result, as part of the master plan, a number of parking structures are strategically positioned to support the grown demand that Colorado Mesa University is experiencing.

1.7 Formation District – Site Location Guiding Principles

The Formation District is a part of Southern Front Door and Gateway along with the Western Front Door and Gateway concepts. The intent is to help define the creation of the Formation District and gradual expansion towards North Ave to the south and ensure a vibrant mix of public and private building uses that can be integrated into this District to the west. In the short-term, wayfinding and branding elements along connecting streets can create front doors to the campus. In the long run, the district can potentially expand west and south to establish a mixed-use community destination.

The long-term goal of the Formation District is the development of a designed community where the private sector can interact with CMU knowledge assets, creating opportunities for students and staff to interact and collaborate with private companies and across discipline interests. Where the general community and public can interact with, enjoy and engage with the CMU student and faculty community thus, being able to enjoy the assets that CMU has to offer.

The goal for the Development of the Formation District master plan as developed by Semple Brown Architects is it to expand west from Centennial Housing bounded by Cannell Ave. The expectation is to attract local, regional and state professionals and retail business to locate to the district. In addition to this development axis bounded to the west by 7th Ave, the north south axis will connect the Hotel Maverick, the new Asteria Performing Arts Hall to a point on the south side of Glenwood Ave. This would allow for mixed use developments to occur around a central plaza connection between the developments. Along an east-west axis and a north-south axis.

The CMU stake holders are looking for vibrant building designs with unique amenities that responds to the “Live-Work-Play-Learn-Connect” lifestyle of the proposed Formation District. The buildings that make up this District need to respond with designs that are efficient, financially viable and environmentally responsible. The final design needs to include, as far as practicable, robust economic, environmental and social convergence encouraging social connections.



Photo 1 – University Center Parking (UC1)

Architectural Response

The exterior building image and exterior quality is to match the general theme of the surrounding university buildings and the proposed vision of the Formation District with a creative use of durable and maintainable masonry, metal panels and glass systems and other approved materials.

The arrangement of building masses, parking, open space, landscaping, walks and site furnishing shall encourage pedestrian activity, create unique views and create an approachable site while following the approved master plan. Use high quality materials that will last for the life of the building.

Use exterior colors and material schemes that are compatible or harmonious with the surrounding built environment while preserving the presence and imagery of the adjoining facilities.

Landscape/Site

The site landscape is to create an attractive visually compliment to the environment and vision of this area. The site needs to communicate a sense of place, purpose, and connection. Create welcoming open space, site connectivity with the other buildings that define this district. Provide privacy for adjacent residential units while maintaining the integration of the buildings and site areas as they develop according to the master plan. The site design needs to provide a direct response to facilitate pedestrian and vehicular movement between proposed and existing destination paths of the university and the developing Formation District.

Accessibility Site Circulation

The facility will be accessible and meet the accessibility requirements of the governing agencies. Site grades must provide barrier free circulation amenities and spaces per code. At least two points of access and egress from the building shall be fully accessible. Anticipated paths from accessible parking and building entrances and into adjacent buildings shall be accessible.

Sustainability

Sustainability is a major focus for the stakeholders and the university administration. The design team is encouraged to design the facility with creative and innovative approaches to sustainability as a long-term facility operations and efficiency model. The design should respond to the impacts on climate and environment while preserving natural resources and improving quality of life.

1.8 State Energy Conservation Requirements

The project will be designed in accordance with the requirements of the State of Colorado and will strive to achieve the highest possible High-Performance Standards.

1.9 Durable Materials

Materials suitable for indefinite exterior exposure and are proven in the Western Colorado climate are required. Materials shall be able to withstand the local weather and climate, and be selected for their anti-corrosive and resilient properties...

1.10 ADA Requirements

Requirements for accessible parking spaces per the IBC and ADAAG 2010. Elevator provided for conveyance. Accessible routes shall also meet the requirements of the IBC and ADAAG 2010.

By no means is this section of this report meant to be inclusive of all requirements relating to accessibility. Instead, it is the intent to bring to the designer's attention the need to address these issues within the confines of good design to meet all legal and enforceable requirements addressing accessibility, adaptability, and visit-ability throughout the building(s).

1.11 Exterior Building Materials

Cast concrete materials and clay masonry are precededented on the CMU campus. Careful consideration should be given and explored based on established parking structures on campus.

2 GENERAL BUILDING PERFORMANCE REQUIREMENTS

2.1 Basic Site Requirements

Site Standards: All site related elements will comply with Colorado Mesa University's Campus Master Plan and Design Standards.

2.2 Accessibility Site Circulation

All buildings including parking structures will be accessible and meet accessibility requirements of local, state, and federal jurisdictions. The site grading must provide barrier-free circulation for accessibility and visit-ability to all buildings and amenities. CMU will comply with all applicable code requirements.

At least two (2) points of access and egress from each building shall be accessible. Anticipated paths from accessible parking to building entrances and into each building shall be accessible. The main entrance to each building is encouraged to have push-pad entry assist doors for visit-ability, and elevators are programmed for accessible access to all levels of the buildings.

Stairs may need to be provided at secondary entrances or sidewalks. These are to be provided as dictated by the site design meeting code requirements of proper railing and stair configuration. Ramps and accessible curb cuts with truncated domes and dimensions as outlined by code are to be provided to ensure a barrier-free site.

2.3 New Utilities Required

It is anticipated that electrical and telephone services will be readily required. These need to be readily available for the project, for lighting, elevator and/or campus call buttons, and communication with ticketing machines, gate arms, and access control systems. Lighting must be efficient with adequate coverage however it needs to be screened from adjacent student housing buildings.

2.4 Building Systems

2.5 Structural

The primary structure will be concrete post and beam, supporting either pre-stressed tees or pre-stressed concrete composite shallow beams and slabs.

The foundation system shall be made of perimeter and interior grade concrete beams supported on steel screw piles which penetrate the soil as per the soils report requirements. The spacing of these piles will be based on the load capacity of the soils and piles.

2.6 Plumbing

As a detached parking structure, plumbing will be limited to the scope of storm drainage through troughs, piping, and other common work related to parking structures.

2.7 Fire Protection System

Fire sprinklers complying with NFPA 88A are required for this structure and compliance with all other codes for fire and life safety.

2.8 Heating, Ventilation and Air Conditioning (HVAC)

Not applicable

2.9 Electrical

- Lighting

General lighting and illumination typical for parking structures. Exterior illumination shall be architectural in nature and highlight architectural features to the design where they occur and shall be coordinated with the architect and engineer.

- General Power

The electrical service shall be minimally sized to accommodate the conveyance elevator, general and architectural lighting, and EV charging where required.

- Systems

Data and voice systems will use Category 6 (Cat 6) cabling. The electrical contractor will perform rough-in only, including boxes and conduit. The phone/data system will consist of 1-inch conduits extending from each Telephone / Data location up to an accessible location. Dedicated, isolated ground receptacles will be used for power.

Conduits and rough-ins will be required for installation of closed circuit security and camera systems where coordinated with the university.

Wireless Access Points (WAPs) shall be installed and integrated into the campus network.

2.10 Fire Alarm System

A fully functioning fire alarm system shall be provided in the building. The system shall monitor all smoke detectors and flow/tamper switches on the fire protection system.

2.11 Codes

All items under this section shall be designed and built following currently adopted codes with any associated amendments as found on the OSA website:

The 2021 edition of the International Building Code (IBC)

(As adopted by the Colorado State Buildings Program as follows: Chapter 1 as amended, Chapters 2-35 and Appendices C and I).

The 2021 edition of the International Mechanical Code (IMC)

(As adopted by the Colorado State Buildings Program as follows: Chapters 2-15 and Appendix A)

The 2021 edition of the International Energy Conservation Code (IECC) (As adopted by the Colorado State Buildings Program and Colorado Energy Office)

Colorado Model Electric Ready and Solar Ready Code

(Published by the Colorado Energy Office) Effective July 1, 2023

The 2023 edition of the National Electrical Code (NEC) (NFPA 70®)

(As adopted by the Colorado State Electrical Board) Effective July 30, 2023

The 2021 edition of the International Plumbing Code (IPC), first printing (March 2020)

(As adopted by the Colorado Examining Board of Plumbers Effective May 15, 2023)

The 2021 edition of the International Fuel Gas Code (IFGC) first printing (August 2020)

(As adopted by the Colorado Examining Board of Plumbers Effective May 15, 2023)

The National Fire Protection Association Standards (NFPA)

(As adopted by the Department of Public Safety/Division of Fire Prevention and Control)

The 2021 edition of the International Fire Code (IFC)

(As adopted by the Department of Public Safety/Division of Fire Prevention and Control (DFPC).

Projects requiring DFPC review should be designed with the most restrictive requirements)

The 2015 edition of the ASME Boiler and Pressure Vessel Code

(As adopted by the Department of Labor and Employment/Boiler Inspection Section) Effective July 1, 2017.

The 2017 edition of the National Boiler Inspection Code (NBIC)

(As adopted by the Department of Labor and Employment/Boiler Inspection Section) Effective July 1, 2017.

The 2015 edition of the Controls and Safety Devices for Automatically Fired Boilers CSD-1

(As adopted by the Department of Labor and Employment/Boiler Inspection Section) Effective July 1, 2017.

The 2015 edition of the Boiler and Combustion Systems Hazards Code, NFPA 85

(As adopted by the Department of Labor and Employment/Boiler Inspection Section) Effective July 1, 2017.

The 2019 edition of ASME A17.1 Safety Code for Elevators and Escalators

(As adopted by the Department of Labor and Employment/Conveyance Section) Effective January 1, 2021.

The Current edition of ICC/ANSI A117.1, Accessible and Usable Buildings and Facilities

As referenced in the adopted edition of the International Building Code.

3 PROJECT BUDGET AND SCHEDULE

Projected Project Costs

Fixed Limit of Construction Cost: **\$27,757,160**

Projected Project Schedule

Anticipated A/E professional Services – Start - March 2026

Anticipated Construction Services – Start – June 2026 – August 2026

Design is projected to begin in early March 2026. The preferred delivery date for the Parking Structure is prior to the start of the Fall semester, August 2026. The final schedule will be developed with the AE team, CM/GC and Colorado Mesa University.

Colorado Mesa University anticipates using a Construction Manager/General Contractor (CM/GC) approach to project delivery. The CM/GC will evaluate, among other things, availability of materials and labor, project schedule, project costs as they relate to the established budget, and constructability, and will work with the Architect throughout the value engineering phases of the project.

(See below for a preliminary design schedule based on the dates above)

Project Design Schedule through Construction Documents

New Parking Structure (CP9 - Colorado Mesa University)

Start Date	Working Days	Weeks	100% CD Completion Date
Monday, March 2, 2026	64	12.6	Friday, May 29, 2026

	Working Days	Weeks	Milestones
Programming / Schematic Design	12	2.4	Wednesday, March 18, 2026
Design Development	17	3.4	Friday, April 10, 2026
Construction Documents	34	6.8	Friday, May 29, 2026

Construction Documents	Working Days	Weeks	CD Milestones
35% CDs	11	2.2	Monday, April 27, 2026
65% CDs	11	2.2	Tuesday, May 12, 2026
90% CDs	8	1.6	Friday, May 22, 2026
100% CDs	4	0.8	Friday, May 29, 2026



STATE OF COLORADO
OFFICE OF THE STATE ARCHITECT
STATE BUILDINGS PROGRAM

COLORADO

PERFORMANCE BOND

Institution/Agency: Colorado Mesa University

Project No./Name: CMU 2867 Student Parking Garage

BONDING COMPANY: DO NOT MAKE ANY CHANGES TO THE LANGUAGE IN THIS BOND.

KNOW ALL PERSONS BY THESE PRESENTS:

That the Contractor

as Principal and hereinafter called "Principal,"

and

as Surety and hereinafter called "Surety," a corporation organized and existing under the laws of

_____ are held and firmly bound unto **the STATE OF COLORADO** acting by and through the Institution/Agency identified above hereinafter called the "Principal Representative", in the sum of:

_____ Dollars (\$_____)
(Written Amount) (Numerical Amount)

for the payment whereof the Principal and Surety bind themselves, their heirs, executors, administrators, successors and assigns, jointly and severally, firmly, by these presents.

WHEREAS, the Principal and the State of Colorado acting by and through the Principal Representative have entered into a certain Contract, hereinafter called "Contract," dated

_____ for the construction of a PROJECT
(Leave blank, to be completed by Institution/Agency)

identified above, which Contract is hereby by reference made a part hereof;

NOW, THEREFORE, THE CONDITION OF THIS OBLIGATION, is such that, if the Principal shall promptly, fully and faithfully perform all the undertakings, covenants, terms, conditions and agreements of said Contract during the original term of said Contract any extensions thereof that may be granted by the Principal Representative with or without notice to the Surety, and during the life of any guaranty required under the Contract, and shall also well and truly perform and fulfill all undertakings, covenants, terms, conditions and agreements of any and all duly authorized modifications of said Contract that may hereafter be made, notice of which modifications to the Surety being hereby waived, then this obligation shall be null and void; otherwise it shall remain in full force and effect.

AND THE SAID SURETY, for value received hereby stipulates and agrees that whenever the Principal shall be, and declared by the Principal Representative to be in default under said Contract, the State of Colorado having performed its obligations thereunder, the Surety may promptly remedy the default or shall promptly (1) Complete the Contract in accordance with its terms and conditions, or (2) Obtain a bid or bids for submittal to the Principal Representative for completing the Contract in accordance with its terms and conditions, and upon determination by the Principal Representative and Surety of the lowest responsible bidder, arrange for a contract between such bidder and the State of Colorado acting by and through the Principal Representative and make available as work progresses (even though there should be a default or a succession of defaults under the contract or contracts of completion arranged under this paragraph) sufficient funds to pay the cost of completion, less the balance of the contract price but not exceeding, including other costs and damages for which the Surety may be liable hereunder, the amount hereinbefore set forth. The term "balance of the contract price" as herein used shall mean the total amount payable to the Principal under the Contract and any amendments thereto, less the amount properly paid by the State of Colorado to the Contractor.

No right of action shall accrue on this bond to or for the use of any person or corporation other than the State of Colorado.

IN WITNESS WHEREOF said Principal and Surety have executed this Bond, on

(If left blank, the Institution/Agency will date this bond to match the Contract date)

(Corporate Seal)

THE PRINCIPAL

ATTEST:

By: _____

Title: _____

Secretary

(Corporate Seal)

SURETY

By _____
:
Attorney-in-fact

THIS BOND MUST BE ACCOMPANIED BY POWER OF ATTORNEY, EFFECTIVELY DATED

Note: This bond is issued simultaneously with another bond conditioned for the full and faithful payment for all labor and material of the contract.
